


Bartlett Offices

7441 Bartlett Street

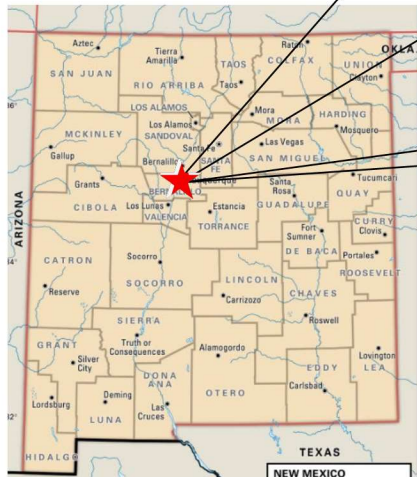

TEMPORARY EROSION AND SEDIMENT CONTROL PLAN

PAGE INDEX	
1	TITLE PAGE
2	SWPPP INFO & NOTES
3	DETAILS
4-5	TEMPORARY EROSION CONTROL PLAN
6	SCHEDULE & SWPPP TEAM



GPS COORDINATES:

Latitude: 35.165969
Longitude: -106.601597

 03/23/2023 CPESC Stamp	Bartlett Offices	
	PROJECT TITLE	
	ALBUQUERQUE, NM, BERNALILLO COUNTY	
	CITY, COUNTY, STATE	
DATE	03/23/2023	
DRAWN BY	B. Henriksen / J. Tolman	

STORMWATER POLLUTION PREVENTION PLAN INFORMATION

PERMIT NUMBER: NMR1005JR, NMR1005JQ	
NMR100000 STATE OF NEW MEXICO, EXCEPT INDIAN COUNTRY NMR101000 INDIAN COUNTRY WITHIN THE STATE OF NEW MEXICO, EXCEPT NAVAJO RESERVATION LANDS THAT ARE COVERED UNDER ARIZONA PERMIT AZR101000 AND UTE MOUNTAIN RESERVATION LANDS THAT ARE COVERED UNDER COLORADO PERMIT COR101000.	
OPERATOR NAME:	Rio Grande, LLC
OPERATOR POINT OF CONTACT:	Keith Cheshire 505-797-8589 keithcheshire@swcp.com
NOI PREPARED BY:	Inspections Plus 2
PROJECT/SITE NAME:	Bartlett Offices
PROJECT/SITE ADDRESS:	7441 Bartlett Street
LATITUDE	Latitude: 35.165969
LONGITUDE	Longitude: -106.601597
ESTIMATED PROJECT START DATE	04/15/2023
ESTIMATED PROJECT COMPLETION DATE	04/15/2023
ESTIMATED AREA TO BE DISTURBED	1.12 acres
TYPE OF CONSTRUCTION	Commercial
DEMOLITION OF ANY STRUCTURES, 10,000 SQ FT OF GREATER BUILT OR RENOVATED BEFORE JANUARY 1, 1980?	No
WAS THE PREDEVELOPMENT LAND USED FOR AGRICULTURE?	NO
COMMENCED EARTH DISTURBING ACTIVITIES?	NO
DISCHARGE TO MS4? MS4 NAME?	NO
SURFACE WATERS WITHIN 50FT?	NO
RECEIVING WATER?	Alameda Lateral
IS RECEIVING WATER IMPAIRED? TIER DESIGNATION	No
WHAT ARE THE IMPAIRMENTS, IF ANY?	
SWPPP CONTACT INFORMATION:	Keith Cheshire 505-797-8589 keithcheshire@swcp.com
ENDANGERED SPECIES CRITERIA:	CRITERION "A"; NO CRITICAL HABITATS
HISTORIC PRESERVATION CRITERIA:	CRITERION "A" PREEXISTING DEVELOPMENT

EROSION CONTROL NOTES ESC Plan Standard Notes (2022-08-23)

1. All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:
 - a. The City Ordinance § 14-5-2-11, the ESC Ordinance,
 - b. The EPA's 2017 Construction General Permit (CGP), and
 - c. The City Of Albuquerque Construction BMP Manual.



2. All BMP's must be installed prior to beginning any earth moving activities except as specified hereon in the Phasing Plan. Construction of earthen BMP's such as sediment traps, sediment basins, and diversion berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is required after installation of the BMPs and prior to beginning construction.

3. Self-inspections - At a minimum a routine compliance self-inspection is required to review the project for compliance with the Construction General Permit once every 14 days and after any precipitation event of 1/4 inch or greater until the site construction has been completed and the site determined as stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.

4. Corrective action reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.

5. Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and manufacturer's specifications for application rates, estimated functional longevity, methods of application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to stabilized area and any damaged or worn stabilization must be identified in the reports along with weed problems. Corrective actions for stabilization shall be documented in a stabilization report including actual rates and dates of stabilization, and the materials and manufacturer's specifications used.

6. BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that provides cover for at least three years without active maintenance. Final stabilization must be approved by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections.

 03/23/2023 CPESC Stamp	Bartlett Offices	
	PROJECT TITLE	
	ALBUQUERQUE, NM, BERNALILLO COUNTY <small>CITY, COUNTY, STATE</small>	
	03/23/2023 DATE B. Henriksen / J. Tolman DRAWN BY	 INSPECTIONS PLUS

SEDIMENT TRACK OUT CONTROL



BMP Objectives

- Sediment Control

BERMS AND SWALES



BMP Objectives

- Runoff Control
- Run-on Diversion

SILT FENCE



BMP Objectives

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control

MULCH SOCK/STRAW WATTLE



BMP Objectives



- Sediment Control
- Reduce Runoff Velocity
- Inlet Protection

INLET PROTECTION



















BMP Objectives

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control

  03/23/2023 CPESC Stamp	Bartlett Offices		PROJECT TITLE
	ALBUQUERQUE, NM, BERNALILLO COUNTY		
	CITY, COUNTY, STATE		
	03/23/2023	DATE	INSPECTIONS PLUS
B. Henriksen / J. Tolman		DRAWN BY	

LEGEND



-  Rip Rap (3)
-  Pre & Post Construction Water Flow (1)
-  Silt Fence (2)
-  Limit of Disturbance (1)
-  ERTEC Inlet Protection (7)
-  Street Sweeping (1)
-  Stabilized Construction Exit (1)
-  SWPPP Sign (1)
-  Portable Concrete Washout Bin (1)
-  Dumpster (1)
-  Portable Toilet (1)
-  Materials Storage (1)
-  Spill Kit (1)
-  Stockpiles (1)
-  Water Truck (1)
-  Blockade (1)

	
Bartlett Offices	
PROJECT TITLE	
ALBUQUERQUE, NM, BERNALILLO COUNTY	
CITY, COUNTY, STATE	
03/23/2023	DATE
B. Henriksen / J. Tolman	DRAWN BY
 INSPECTIONS PLUS	

Owner:

Rio Grande, LLC

Keith Cheshire

Property Owner Contact

505-797-8589

keith.cheshire@swcp.com

Responsibility: Oversees project development.

Operator(s):

Cheshire Company, LLC

Keith Cheshire

Project Manager

7400 Hancock Court, Suite B

Albuquerque, NM 87109

505-797-8589

keithcheshire@swcp.com

Schedule/ Sequencing of Construction –Bartlett Offices

1. POST PERMITS
2. INSTALL REQUIRED BMPs
- 2.a. PERIMETER CONTROLS (Silt Fence)
- 2.b. STABILIZED CONSTRUCTION ENTRANCE
3. EARTHWORK AND GRADING
4. UTILITY INSTALLATION
5. PAVEMENT STRUCTURES
6. PAD STRUCTURES
7. LANDSCAPING/ STABILIZATION
8. PUNCHLIST
