#### Motel 1

#### 2001 Canelaria Road NE

#### TEMPORARY EROSION AND SEDIMENT CONTROL PLAN


PAGE INDEX	
1	TITLE PAGE
2	SWPPP INFO & NOTES
3	DETAILS
4-5	TEMPORARY EROSION
	CONTROL PLAN
6	SCHEDULE & SWPPP TEAM



# Artec Terry Anacills TAOS COLFAX UNION Anacills TAOS COLFAX UNION Anacills TAOS COLFAX UNION Anacills TAOS COLFAX UNION Anacills TAOS Anacills

#### **GPS COORDINATES:**

Latitude: 35.114737 Longitude: -106.622686



#### STORMWATER POLLUTION PREVENTION PLAN INFORMATION

#### PERMIT NUMBER: NMR1005JR, NMR1005JQ, NMR1005JK

NMR100000 STATE OF NEW MEXICO, EXCEPT INDIAN COUNTRY NMR101000 INDIAN COUNTRY WITHIN THE STATE OF NEW MEXICO, EXCEPT NAVAJO RESERVATION LANDS THAT ARE COVERED UNDER ARIZONA PERMIT AZR101000 AND UTE MOUNTAIN RESERVATION LANDS THAT ARE COVERED UNDER COLORADO PERMIT COR101000.

OPERATOR NAME:

Galles Chevrolet Inc.

OPERATOR POINT OF CONTACT Jamie Galles

505-506-9531

NOI PREPARED BY-

Inspections Plus 2

PROJECT/SITE NAME:

Motel 1


PROJECT/SITE ADDRESS:

2001 Candelaria Road NE

LATITUDE	Latitude: 35.114737
LONGITUDE	Longitude: -106.622686
ESTIMATED PROJECT START DATE	05/152023
ESTIMATED PROJECT COMPLETION DATE	008/25/2023
ESTIMATED AREA TO BE DISTURBED	1.13 acres
TYPE OF CONSTRUCTION	Commercial
DEMOLITION OF ANY STRUCTURES, 10,000 SQ FT OF GREATER BUILT OR RENOVATED BEFORE JANUARY 1, 1980	Yes
WAS THE PREDEVELOPMENT LAND USED FOR AGRICULTURE?	NO
COMMENCED EARTH DISTURBING ACTIVITIES?	NO
DISCHARGE TO MS4? MS4 NAME?	NO
SURFACE WATERS WITHIN 50FT?	NO
RECEIVING WATER?	Alameda Lateral
IS RECEIVING WATER IMPAIRED? TIER DESIGNATION	No
WHAT ARE THE IMPAIRMENTS, IF ANY?	NA
SWPPP CONTACT INFORMATION: Bertha Bolivar - 505-877-2821	bertha@coronadowrecking.co
ENDANGERED SPECIES CRITERIA: CRITERION "A"; No	O CRITICAL HABITATS
HISTORIC PRESERVATION CRITERIA: CRITERION "A" PREEXISTIN	NG DEVELOPMENT

#### EROSION CONTOL NOTES ESC Plan Standard Notes (2022-08-23)

- 1.All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:
- a. The City Ordinance § 14-5-2-11, the ESC Ordinance,
- b. The EPA's 2017 Construction General Permit (CGP), and
- c. The City Of Albuquerque Construction BMP Manual.
- 2. All BMP's must be installed prior to beginning any earth moving activities except as specified hereon in the Phasing Plan. Construction of earthen BMP's such as sediment traps, sediment basins, and diversion berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is required after installation of the BMPs and prior to beginning construction.
- 3. Self-inspections At a minimum a routine compliance self-inspection is required to review the project for compliance with the Construction General Permit once every 14 days and after any precipitation event of 1/4 inch or greater until the site construction has been completed and the site determined as stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.
- 4. Corrective action reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.
- 5. Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and manufacturer's specifications for application rates, estimated functional longevity, methods of application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to stabilized area and any damaged or worn stabilization must be identified in the reports along with weed problems. Corrective actions for stabilization shall be documented in a stabilization report including actual rates and dates of stabilization, and the materials and manufacturer's specifications used.
- 6.BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that provides cover for at least three years without active maintenance. Final stabilization must be approved by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections.



#### SEDIMENT TRACK OUT CONTROL



BMP ObjectivesSediment Control

BERMS AND SWALES



**BMP Objectives** 

- Runoff Control
- Run-on Diversion

#### SILT FENCE



#### **BMP Objectives**

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control

#### MULCH SOCK/STRAW WATTLE



#### **BMP Objectives**

- Sediment Control
- Reduce Runoff Velocity
- Inlet Protection

#### INLET PROTECTION











#### **BMP Objectives**

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control



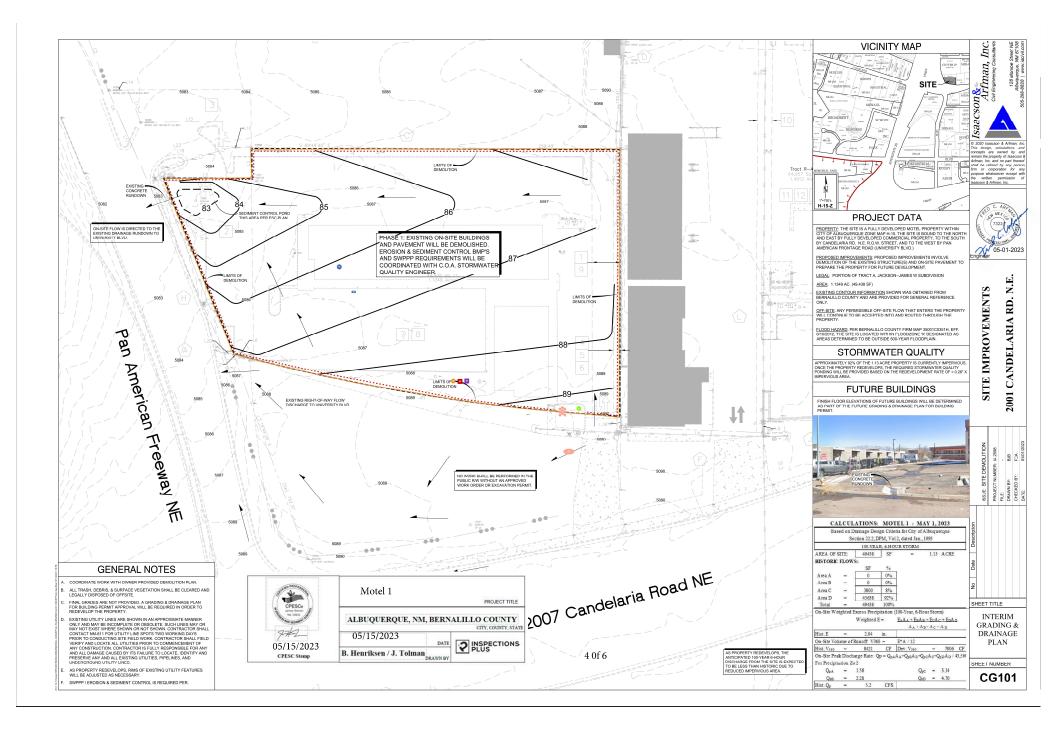


## Inspections Plus, LLC Demolition SWPPP Map-Final Motel 1

### Ш **(**) E Z D



- Property Boundary / Limit of Disturbance (1)
- Silt Fence (1)
- Stabilized Construction Exit (1)
- SWPPP Sign (1)
- Debris Stockpiles (1)
- Dumpster (1)
- Containment (1) Portable Toilet with Secondary
- Spill Kit (1)
- Water Truck (1)
- Street Sweeping (1)



Operator
Coronado Wrecking & Salvage
Jeff White
Project Manager
4200 Broadway Boulevard SE
Albuquerque, NM 87105
505-975-5410
oziewinter@yahoo.com

Galles Chevrolet Inc Jamie Galles 505-506-9531 jamiegalles@galles.com 2801 University Rd. ABQ, NM 87107

Schedule/ Sequencing of Construction – Motel 1

- 1. POST PERMITS
- 2. INSTALL REQUIRED BMPs
- 2.a. PERIMETER CONTROLS (Silt Fence)
- 3. DEMO (20-45 days)
- 4. CLEAR MATERIAL (5-10 DAYS)
- 5. SITE GRADING (4-8 DAYS)
- 6. STABILIZE and PUNCHLIST

NOTE: Coronado Wrecking is responsible for only

the demolition and stabilization of the site.

building plans. Coronado will not be responsible for any future

