2500 Carlisle Boulevard NE Boulevard 2500 Luxury Apartments

TEMPORARY EROSION AND SEDIMENT CONTROL PLAN



GPS COORDINATES: 35.106954, -106.603284

ARIZONA



Boulevard 2500 Luxury Apartments

ALBUQUERQUE, NM, BERNALILLO COUNTY

PLUS PLUS

NEW MEXICO TEXAS

STORMWATER POLLUTION PREVENTION PLAN INFORMATION

PERMIT NUMBER: NMR100578, NMR100575, NMR10058H

PERMIT AZR101000 AND UTE MOUNTAIN RESERVATION LANDS THAT ARE NAVAJO RESERVATION LANDS THAT ARE COVERED UNDER ARIZONA NMR101000 INDIAN COUNTRY WITHIN THE STATE OF NEW MEXICO, EXCEPT COVERED UNDER COLORADO PERMIT COR101000 NMR100000 STATE OF NEW MEXICO, EXCEPT INDIAN COUNTRY

OPERATOR NAME: Rhino Investments

OPERATOR POINT OF CONTACT: Jonathan Wall

Inspections Plus 2

NOI PREPARED BY:

PROJECT/SITE NAME Blvd 2500 Luxury Apartments

PROECT/SITE ADDRESS: 2500 Carlisle Blvd NE

ESTIMATED PROJECT START DATE ESTIMATED PROJECT COMPLETION DATE LONGITUDE LATITUDE 35.106954 02/15/2023 01/03/2023 -106.603284

WHAT ARE THE IMPAIRMENTS, IF ANY? IS RECEIVING WATER IMPAIRED? TIER DESIGNATION RECEIVING WATER? SURFACE WATERS WITHIN 50FT? DISCHARGE TO MS4? MS4 NAME? COMMENCED EARTH DISTURBING ACTIVITIES? GREATER BUILT OR RENOVATED BEFORE JANUARY 1, 1980? TYPE OF CONSTRUCTION ESTIMATED AREA TO BE DISTURBED AGRICULTURE? WAS THE PREDEVELOPMENT LAND USED FOR DEMOLITION OF ANY STRUCTURES, 10,000 SQ FT OF Ö COMMERCIAL BUILDING Trail on Levee NO NO NO Ö 1.75 ACRES

ESC Plan Standard Notes (2022-08-23) EROSION CONTOL NOTES

1.All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:

c.The City Of Albuquerque Construction BMP Manual b.The EPA's 2017 Construction General Permit (CGP), and a.The City Ordinance § 14-5-2-11, the ESC Ordinance,


required after installation of the BMPs and prior to beginning construction. berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is the Phasing Plan. Construction of earthen BMP's such as sediment traps, sediment basins, and diversion 2.All BMP's must be installed prior to beginning any earth moving activities except as specified hereon ir

direct the construction activities on the site and made available upon request. stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to event of 1/4 inch or greater until the site construction has been completed and the site determined as for compliance with the Construction General Permit once every 14 days and after any precipitation 3.Self-inspections - At a minimum a routine compliance self-inspection is required to review the project

activities on the site and made available upon request. 4. Corrective action reports must be kept by the person or entity authorized to direct the construction

problems. Corrective actions for stabilization shall be documented in a stabilization report including stabilized area and any damaged or worn stabilization must be identified in the reports along with weed manufacturer's specifications for application rates, estimated functional longevity, methods of 5.Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal actual rates and dates of stabilization, and the materials and manufacturer's specifications used. application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and

by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections. cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the provides cover for at least three years without active maintenance. Final stabilization must be approved Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and 6.BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the



HISTORIC PRESERVATION CRITERIA: CRITERION "A" PREEXISTING DEVELOPMENT ENDANGERED SPECIES CRITERIA: CRITERION "A"; NO CRITICAL HABITATS

SWPPP CONTACT INFORMATION:

Matthew Budgher 505-553-0544 gbrunacini@brunicina.com

SEDIMENT TRACK OUT CONTROL



BMP ObjectivesSediment Control



BMP ObjectivesRunoff Control

- Run-on Diversion

SILT FENCE

INLET PROTECTION



- BMP ObjectivesSediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control







- BMP ObjectivesSediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control

BMP Objectives

- Sediment Control
 Reduce Runoff Velocity
 Inlet Protection



Blvd 2500 Luxury Apartments

PROJECT TITLE

ALBUQUERQUE, NM, BERNALILLO COUNTY CHY. COUNTY, STATE

B. Henriksen / J. Tolman DRAWN BY 11/01/22 Revision DATE

NSPECTIONS PLUS




Blvd 2500 Luxury Apartments Inspections Plus, LLC Demolition SWPPP Map-Final

LEGEND



- Silt Fence (3)
- ---- Cutback Curb / Sidewalk (5)
- Pre & Post Construction Water Flow (2)
- --- Existing Concrete Wall (1)
- Limit of Disturbance (1)
- Materials Storage (1)
- Spill Kit (1)
- ERTEC Inlet Protection (6)
- Water Truck (1)
- Debris Stockpiles (1)
- Stabilized Construction Exit (2)
- SWPPP Sign (1)
- Street Sweeping (1)
- Portable Toilet with Secondary Containment (1)
- Dumpster (1)



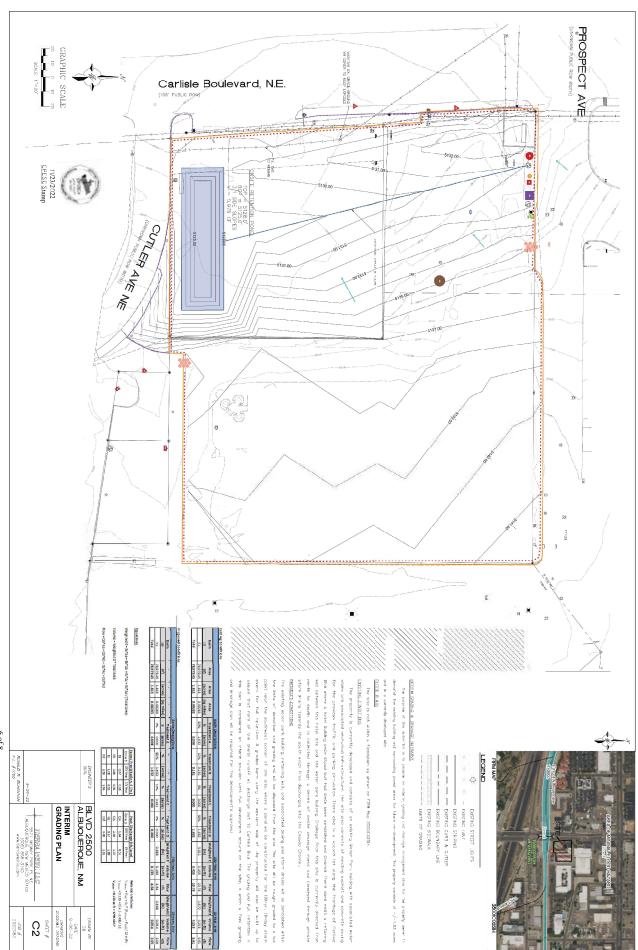

Blvd 2500 Luxury Apartments Inspections Plus, LLC Commercial SWPPP Map-Final

LEGEND





- Retention Basin (1)
- Silt Fence (3)
- ---- Cutback Curb / Sidewalk (3)
- Pre & Post Construction Water Flow (3)
- --- Existing Concrete Wall (1)
- ---- Drainage Swale (1)
- Limit of Disturbance (1)
- **ERTEC Inlet Protection (5)**
- Street Sweeping (1)
- Spill Kit (1)
- Materials Storage (1)
- Stabilized Construction Exit (2)
- Water Truck (1)
- Portable Toilet with Secondary Containment (1)
- SWPPP Sign (1)
- Dumpster (1)
- Stockpiles (1)



7 of 8

Schedule/ Sequencing of Construction – 2500 Carlisle Boulevard

- 1. POST PERMITS
- 2. INSTALL REQUIRED BMPs
 - 2.a. PERIMETER CONTROLS (Silt Fence)
 - 2.b. STABILIZED CONSTRUCTION ENTRANCE
- 3. DEMO (15-20 DAYS)
- 4. CLEAR MATERIAL (5-10 DAYS)
- 5. SITE GRADING (2-3 DAYS)
- 6. STABILIZE SITE WITH GRAVEL MILLINGS (WITHIN 14 DAYS OF SITE COMPLETION)

Owner:

Rhino Investments
Jonathan Wall
Property Owner Contact
209-573-0073
jwall@rhinoig.com
Responsibility: Oversees project development.

Operator(s):
3B Builders, Inc.
Matthew Budagher
Project Manager
1770 Hamilton Lane
Bosque Farms, NM 87068
505-553-0544
3bbuilders@gmail.com
