

BURGER KING CARLISLE

2110 CARLISLE BLVD NE

TEMPORARY EROSION AND SEDIMENT CONTROL PLAN



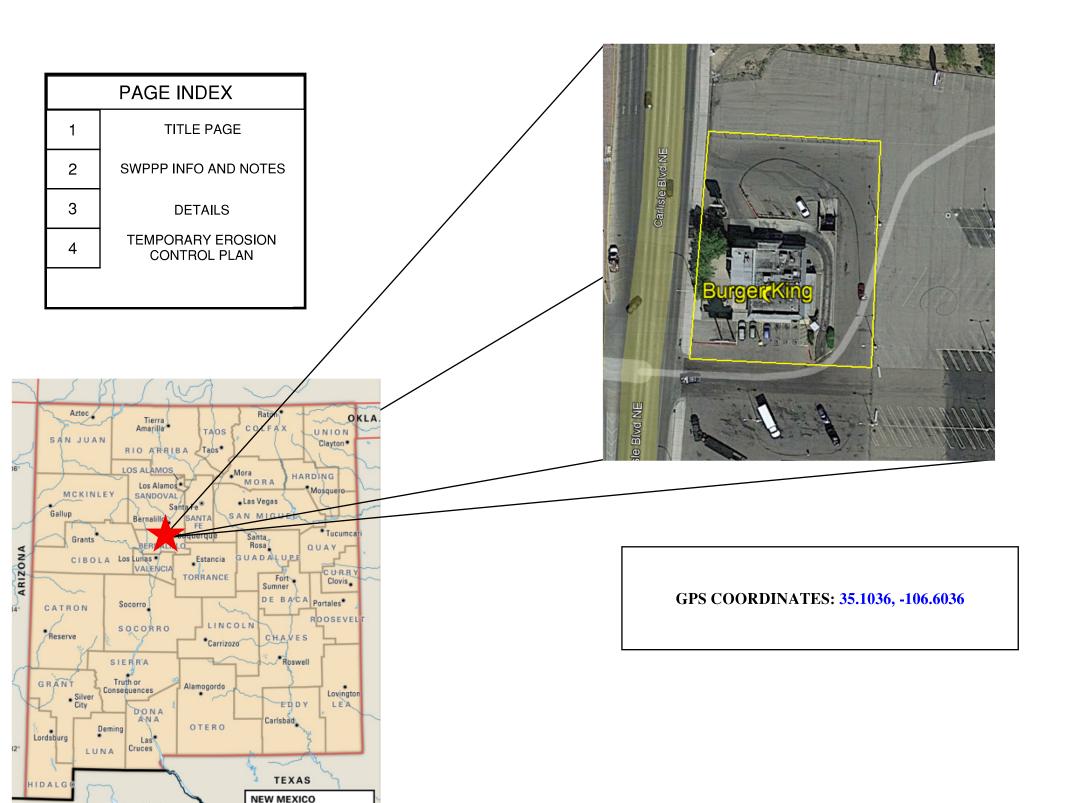



STORMWATER POLLUTION PREVENTION PLAN INFORMATION

PERMIT NUMBER: LEW NMR1004DF

NMR100000 STATE OF NEW MEXICO, EXCEPT INDIAN COUNTRY NMR101000 INDIAN COUNTRY WITHIN THE STATE OF NEW MEXICO, EXCEPT NAVAJO RESERVATION LANDS THAT ARE COVERED UNDER ARIZONA PERMIT AZR101000 AND UTE MOUNTAIN RESERVATION LANDS THAT ARE COVERED UNDER COLORADO PERMIT COR101000.

OPERATOR NAME:

PJ DEVELOPMENT, INC

OPERATOR POINT OF CONTACT:

PAT JOSEPH

NOI PREPARED BY:

INSPECTIONS PLUS

PROJECT/SITE NAME:

BURGER KING CARLISLE

PROJECT/SITE ADDRESS:

2110 CARLISLE BLVD NE

LATITUDE	35.1036
LONGITUDE	-106.6036
ESTIMATED PROJECT START DATE	12/03/2021
ESTIMATED PROJECT COMPLETION DATE	07/01/2021
ESTIMATED AREA TO BE DISTURBED	1.0 ACRE
TYPE OF CONSTRUCTION	DEMO AND RECONSTRUCTION
DEMOLITION OF ANY STRUCTURES, 10,000 SQ FT OF	NO
GREATER BUILT OR RENOVATED BEFORE JANUARY 1, 1980?	
WAS THE PREDEVELOPMENT LAND USED FOR	NO
AGRICULTURE?	
COMMENCED EARTH DISTURBING ACTIVITIES?	NO
DISCHARGE TO MS4? MS4 NAME?	YES- CITY OF ALBQ.
SURFACE WATERS WITHIN 50FT?	NO
RECEIVING WATER?	CITY MS4- NOTH DIVERSION CHANNEL
IS RECEIVING WATER IMPAIRED? TIER DESIGNATION	NO
WHAT ARE THE IMPAIRMENTS, IF ANY?	N/A
SWPPP CONTACT INFORMATION: PAT JOSEPH 505-263-6965 PAT@PJDEV.NET	

ENDANGERED SPECIES CRITERIA: CRITERION "A"; NO CRITICAL HABITATS WITHIN PROJECT AREA

HISTORIC PRESERVATION CRITERIA: CRITERION "A"; PREVIOUS DEVELOPMENT


EROSION CONTOL NOTES ESC Plan Standard Notes (2021-03-24)

1.All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:

a.The City Ordinance § 14-5-2-11, the ESC Ordinance, b.The EPA's 2017 Construction General Permit (CGP), and c.The City Of Albuquerque Construction BMP Manual.

- 2.All BMP's must be installed prior to beginning any earth moving activities except as specified hereon in the Phasing Plan. Construction of earthen BMP's such as sediment traps, sediment basins, and diversion berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is required after installation of the BMPs and prior to beginning construction.
- 3.Self-inspections At a minimum a routine compliance self-inspection is required to review the project for compliance with the Construction General Permit once every 14 days and after any precipitation event of 1/4 inch or greater until the site construction has been completed and the site determined as stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.
- 4. Corrective action reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.
- 5.Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and manufacturer's specifications for application rates, estimated functional longevity, methods of application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to stabilized area and any damaged or worn stabilization must be identified in the reports along with weed problems. Corrective actions for stabilization shall be documented in a stabilization report including actual rates and dates of stabilization, and the materials and manufacturer's specifications used.

6.BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that provides cover for at least three years without active maintenance. Final stabilization must be approved by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections.





BMP Objectives

Sediment Control





BMP Objectives

- Runoff Control
- Run-on Diversion

SILT FENCE



BMP Objectives

- **Sediment Control**
- Sheet Flow Runoff Control
- Wind Erosion Control

MULCH SOCK/STRAW WATTLE



BMP Objectives

- **Sediment Control**
- Reduce Runoff Velocity
- **Inlet Protection**

INLET PROTECTION









BMP Objectives

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control



TEMPORARY EROSION AND SEDIMENT CONTROL PLAN

PP-PP-PP- PROJECT PERIMETER



−**BW**—**BW**— EXISTING BLOCK WALL



POSTING SIGN



OUTFALL



STAGING AREA



FLOW DIRECTION



SF-SF-SF SILT FENCE



DEBRIS CONTAINMENT



CHEMICAL TOILET



CONCRETE WASHOUT



STABILIZED CONTRUCTION ENTRANCE






PROJECT TITLE

ALBUQUERQUE, NM, BERNALILLO COUNTY

12/02/2021 C. DURKIN






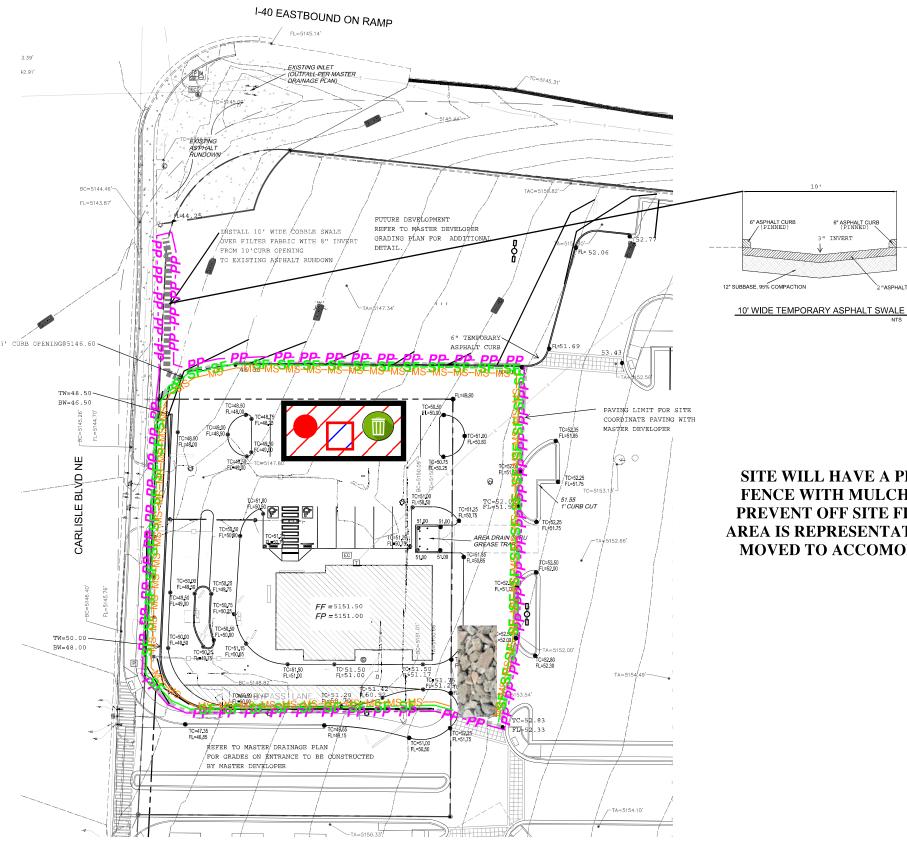

SITE WILL HAVE A PERIMETER SILT FENCE WITH MULCH SOCK BASE TO PREVENT OFF SITE FLOWS. STAGING AREA IS REPRESENTATIVE AND MAY BE MOVED TO ACCOMODATE PROJECT.

6" ASPHALT CURB (PINNED)

EXISTING GROUND

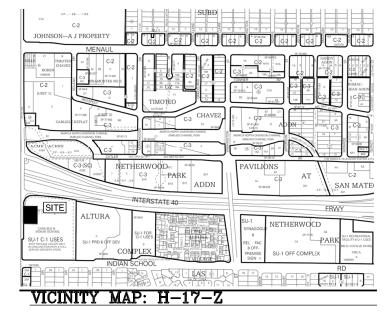

SCHEDULE/SEQUENCING OF CONSTRUCTION

- 1. POST PERMITS
- 2. INSTALL REQUIRED BMPs
 - 2.a. PERIMETER CONTROLS
 - 2.b. STABILIZED CONSTRUCTION ENTRANCE
 - 2.c. CONCRETE WASHOUT AREA
- DEMO
- UTILITY TIE INS
- PAVEMENT STRUCTURES
- VERTICAL STRUCTURES
- LANDSCPING
- 8. PUNCHLIST

SITE OPERATORS:

PJ DEVELOPMENT, INC. PAT JOSEPH 505-263-6965

STORMWATER TEAM

A: REMOVE SEDIMENT FROM ADJACENT STREETS: INSPECTIONS PLUS

B: BMP MAINTENANCE: INSPECTIONS PLUS

C. SITE INSPECTIONS: INSPECTIONS PLUS



SCALE: 1"=20"

BURGER KING CARLISLE

PROJECT TITLE

ALBUQUERQUE, NM, BERNALILLO COUNTY CITY, COUNTY, STATE

12/02/2021

INSPECTIONS PLUS

12/02/2021 CPESC Stamp

C. DURKIN DRAWN BY
