# Starbucks Coffee Company

Coors ou e ar

# TEMPORARY EROSION AND SEDIMENT CONTROL PLAN

PAGE INDEX		
1	TITLE PAGE	
2	SWPPP INFO AND NOTES	
3	DETAILS	
4	TEMPORARY EROSION CONTROL PLAN	








NEW MEXICO

### **GPS COORDINATES:**

Owner: Los Dows, LLS 5153 Lomas De Atrisco, NW Albuquerque, NM 87105 505-350-4477



## STORMWATER POLLUTION PREVENTION PLAN INFORMATION

## PERMIT NUMBER:

NMR100000 STATE OF NEW MEXICO, EXCEPT INDIAN COUNTRY NMR101000 INDIAN COUNTRY WITHIN THE STATE OF NEW MEXICO, EXCEPT NAVAJO RESERVATION LANDS THAT ARE COVERED UNDER ARIZONA PERMIT AZR101000 AND UTE MOUNTAIN RESERVATION LANDS THAT ARE COVERED UNDER COLORADO PERMIT COR101000.

OPERATOR NAME: Lou Dows, LLC

ENDANGERED SPECIES CRITERIA:

OPERATOR POINT OF CONTACT: Helen Strader

NOI PREPARED BY: Inspections Plus 2

PROJECT/SITE NAME: Starbucks Coffee Company

PROJECT/SITE ADDRESS: 1400 Coors Boulevard NW

1400 Cools Boulevard IVW	
LATITUDE	3
LONGITUDE	-106.
ESTIMATED PROJECT START DATE	10/27/2022
ESTIMATED PROJECT COMPLETION DATE	
ESTIMATED AREA TO BE DISTURBED	acres C S
TYPE OF CONSTRUCTION	COMMERCIAL
DEMOLITION OF ANY STRUCTURES, 10,000 SQ FT OF	
GREATER BUILT OR RENOVATED BEFORE JANUARY 1, 1980?	
WAS THE PREDEVELOPMENT LAND USED FOR	NO
AGRICULTURE?	NO
COMMENCED EARTH DISTURBING ACTIVITIES?	NO
DISCHARGE TO MS4? MS4 NAME?	NO
SURFACE WATERS WITHIN 50FT?	NO
RECEIVING WATER?	Rio Grande
IS RECEIVING WATER IMPAIRED? TIER DESIGNATION	Y
WHAT ARE THE IMPAIRMENTS, IF ANY? Dissolve	ed Oxygen, E. Coli Mercury, Temp.
SWPPP CONTACT INFORMATION: C ames Sc ombur	sc ombur msn com

HISTORIC PRESERVATION CRITERIA: CRITERION "A" PREEXISTING DEVELOPMENT

**CRITERION "A"; NO CRITICAL HABITATS** 

# EROSION CONTOL NOTES ESC Plan Standard Notes (202 -0 -2 )

1.All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:

a.The City Ordinance § 14-5-2-11, the ESC Ordinance, b.The EPA's 2017 Construction General Permit (CGP), and c.The City Of Albuquerque Construction BMP Manual.


2.All BMP's must be installed prior to beginning any earth moving activities except as specified hereon in the Phasing Plan. Construction of earthen BMP's such as sediment traps, sediment basins, and diversion berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is required after installation of the BMPs and prior to beginning construction.

3.Self-inspections - At a minimum a routine compliance self-inspection is required to review the project for compliance with the Construction General Permit once every 14 days and after any precipitation event of 1/4 inch or greater until the site construction has been completed and the site determined as stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.

4. Corrective action reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.

5.Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and manufacturer's specifications for application rates, estimated functional longevity, methods of application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to stabilized area and any damaged or worn stabilization must be identified in the reports along with weed problems. Corrective actions for stabilization shall be documented in a stabilization report including actual rates and dates of stabilization, and the materials and manufacturer's specifications used.

6.BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that provides cover for at least three years without active maintenance. Final stabilization must be approved by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections.



#### SEDIMENT TRACK OUT CONTROL



**BMP Objectives** 

• Sediment Control





**BMP Objectives** 

- Runoff Control
- Run-on Diversion

### SILT FENCE



# **BMP Objectives**

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control

#### MULCH SOCK/STRAW WATTLE



# **BMP Objectives**

- Sediment Control
- Reduce Runoff Velocity
- Inlet Protection

#### INLET PROTECTION










## **BMP Objectives**

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control




CPESC Stamp

**Starbucks Coffee Company** 

PROJECT TIT

ALBUQUERQUE, NM, BERNALILLO COUNTY
CITY, COUNTY, STATE

enr ksen o man DRAWN BY

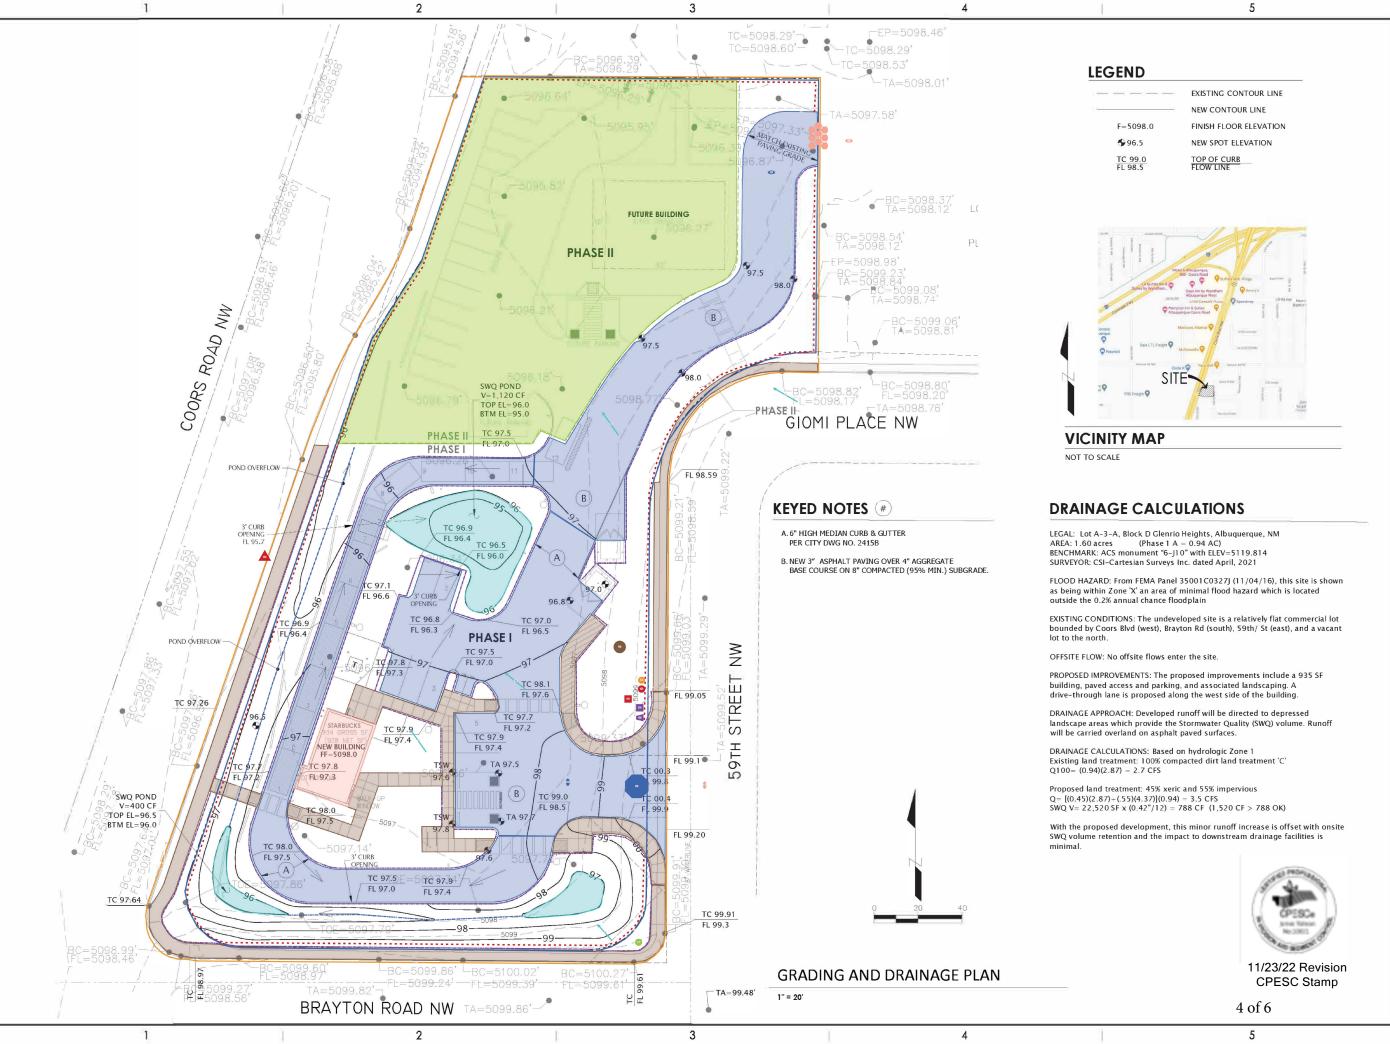



SEAL



PROJECT

STARBUCKS COFFEE COMPANY
BUILDING SHELL & SITE DEVELOPMENT
1400 COORS BOULEVARD, NW
ALBUQUERQUE, NEW MEXICO



DATE

SHEET TITLE

C101

March 17, 2022

# Starbucks Coffee Inspections Plus, LLC Commercial SWPPP map-Phase 1-Final

# LEGEND





Temporary Stabilization / Seeding - Phase 2 (1)



Asphalt Paving (3)



Concrete Sidewalk (7)



New Building (1)



Retention Basin (3)



Silt Fence (3)



Cutback Curb / Sidewalk (14)



Pre & Post Construction Water Flow (5)



--- Drainage Swale (2)



Property Boundary (1)



Limit of Disturbance (1)



Spill Kit (1)



**ERTEC Inlet Protection (1)** 



Water Truck (2)



Portable Toilet (1)



Portable Concrete Washout Bin (1)



Street Sweeping (2)



Stabilized Construction Exit (1)



SWPPP Sign (1)



Dumpster (1)



Materials Storage (1)



Blockade (1)



Stockpiles (1)



**CPESC Stamp** 

#### SCHEDULE/SEQUENCING OF CONSTRUCTION

- 1. POST PERMITS
- 2. INSTALL REQUIRED BMPs
  - 2.a. PERIMETER CONTROLS (SILT FENCE)
  - 2.b. STABILIZED CONSTRUCTION ENTRANCE
  - 2.c. CONCRETE WASHOUT AREA
- 3. EARTHWORK AND GRADING
- 4. UTILITY INSTALLATION
- **5. PAVEMENT STRUCTURES**
- 6. PAD STRUCTURES
- 7. LANDSCAPING
- 8. PUNCHLIST
- 9. STABLILIZE PHASE II AREA WITH SEED AND HYDRO MULCH

WITHIN 14 DAYS OF CONSTRUCTION COMPLETION.

Owner: Los Dows, LLC Aurther J. Dow Property Owner Contact 505-350-4477 dowaj@yahoo.com

Operator(s):
NCB Construction, Inc.
C. James Schomburg
Project Manager
325 Academy Road, Suite A
Corrales, NM 87048
505-238-2341
jschomburg05@msn.com
