Starbucks Coffee Company

1400 Coors Boulevard NW

TEMPORARY EROSION AND SEDIMENT CONTROL PLAN

PAGE INDEX		
1	TITLE PAGE	
2	SWPPP INFO AND NOTES	
3	DETAILS	
4	BMP MAP	
5	MAP LEGEND	
6	Construction Schedule & SWPPP Team	



Aztec

Tierra
Amarilla

TAOS

COLFAX

UNION

RIO ARRIBA Taos

LOS ALAMOS

LOS ALAMOS

Mora
Mora
HARDING
MOSquero
Santo-re
Rosa

CIBOLA Los Luñas
VALENCIA

TORRANCE

FORT
Sumner

DE BACA Portales

ROOSEVELT

CHAVES

ROSSEVELT

CHAVES

TEXAS


NEW MEXICO

TEXAS

NEW MEXICO

GPS COORDINATES: 35.099190, -10.707178

Owner: Los Dows, LLS 5153 Lomas De Atrisco, NW Albuquerque, NM 87105 505-350-4477



STORMWATER POLLUTION PREVENTION PLAN INFORMATION

PERMIT NUMBER: NMR10056F, NMR1005G

NMR100000 STATE OF NEW MEXICO, EXCEPT INDIAN COUNTRY NMR101000 INDIAN COUNTRY WITHIN THE STATE OF NEW MEXICO, EXCEPT NAVAJO RESERVATION LANDS THAT ARE COVERED UNDER ARIZONA PERMIT AZR101000 AND UTE MOUNTAIN RESERVATION LANDS THAT ARE COVERED UNDER COLORADO PERMIT COR101000.

OPERATOR NAME: Lou Dows, LLC

ENDANGERED SPECIES CRITERIA:

OPERATOR POINT OF CONTACT: Author Dow

NOI PREPARED BY: Inspections Plus 2

PROJECT/SITE NAME: Starbucks Coffee Company

PROJECT/SITE ADDRESS: 1400 Coors Boulevard NW

LATITUDE	35.099190	
LONGITUDE	-106.707178	
ESTIMATED PROJECT START DATE	10/27/2022	
ESTIMATED PROJECT COMPLETION DATE	03/15/2022	
ESTIMATED AREA TO BE DISTURBED	0.94 acres	
TYPE OF CONSTRUCTION	COMMERCIAL BU N	
DEMOLITION OF ANY STRUCTURES, 10,000 SQ FT OF		
GREATER BUILT OR RENOVATED BEFORE JANUARY 1, 1980?	NO	
WAS THE PREDEVELOPMENT LAND USED FOR	No.	
AGRICULTURE?	NO	
COMMENCED EARTH DISTURBING ACTIVITIES?	NO	
DISCHARGE TO MS4? MS4 NAME?	NO	
SURFACE WATERS WITHIN 50FT?	NO	
RECEIVING WATER?	Rio Grande	
IS RECEIVING WATER IMPAIRED? TIER DESIGNATION	Y	
WHAT ARE THE IMPAIRMENTS, IF ANY? Dissolv	ed Oxygen, E. Coli Mercury, Temp.	
SWPPP CONTACT INFORMATION: C. James Schomburg, 505-238-2341 jschomburg05@msn.com		

HISTORIC PRESERVATION CRITERIA: CRITERION "A" PREEXISTING DEVELOPMENT

CRITERION "A"; NO CRITICAL HABITATS

EROSION CONTOL NOTES ESC Plan Standard Notes (2022-08-23)

1.All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:

a.The City Ordinance § 14-5-2-11, the ESC Ordinance, b.The EPA's 2017 Construction General Permit (CGP), and c.The City Of Albuquerque Construction BMP Manual.


2.All BMP's must be installed prior to beginning any earth moving activities except as specified hereon in the Phasing Plan. Construction of earthen BMP's such as sediment traps, sediment basins, and diversion berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is required after installation of the BMPs and prior to beginning construction.

3.Self-inspections - At a minimum a routine compliance self-inspection is required to review the project for compliance with the Construction General Permit once every 14 days and after any precipitation event of 1/4 inch or greater until the site construction has been completed and the site determined as stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.

4. Corrective action reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.

5.Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and manufacturer's specifications for application rates, estimated functional longevity, methods of application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to stabilized area and any damaged or worn stabilization must be identified in the reports along with weed problems. Corrective actions for stabilization shall be documented in a stabilization report including actual rates and dates of stabilization, and the materials and manufacturer's specifications used.

6.BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that provides cover for at least three years without active maintenance. Final stabilization must be approved by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections.



SEDIMENT TRACK OUT CONTROL



BMP Objectives

• Sediment Control





BMP Objectives

- Runoff Control
- Run-on Diversion

SILT FENCE



BMP Objectives

- **Sediment Control**
- Sheet Flow Runoff Control
- Wind Erosion Control

MULCH SOCK/STRAW WATTLE



BMP Objectives

- **Sediment Control**
- Reduce Runoff Velocity
- **Inlet Protection**

INLET PROTECTION










BMP Objectives

- Sediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control




Starbucks Coffee Company

ALBUQUERQUE, NM, BERNALILLO COUNTY CITY, COUNTY, STATE

09/17/2022 B. Henriksen/J. Tolman DRAWN BY

inspections plus

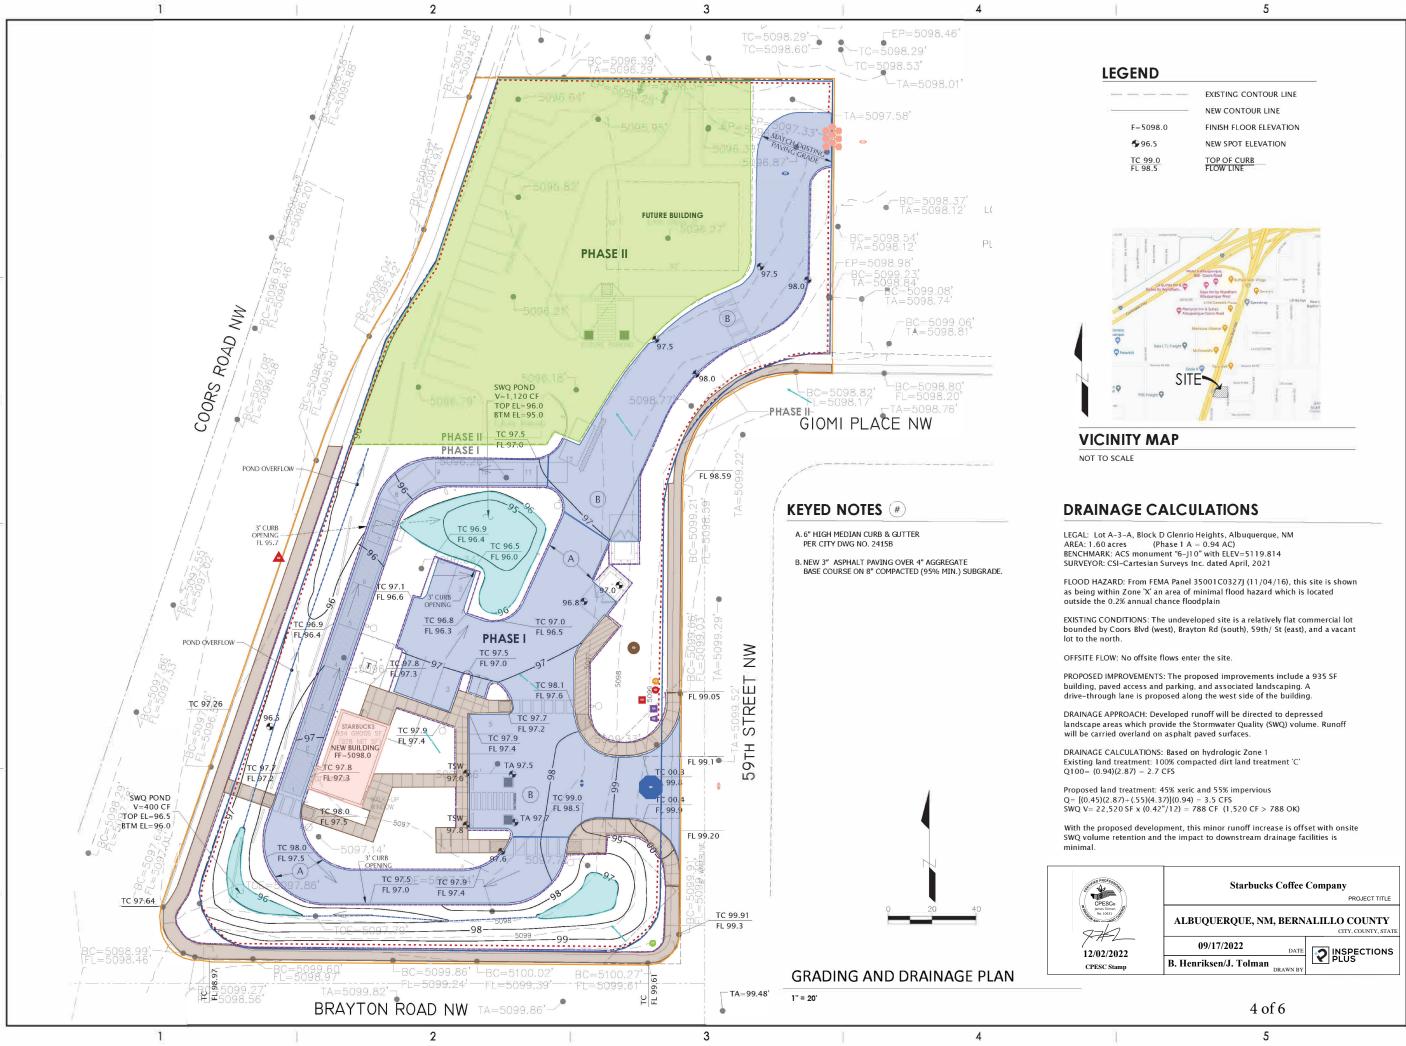





PROJECT

STARBUCKS COFFEE COMPANY
BUILDING SHELL & SITE DEVELOPMENT
1400 COORS BOULEVARD, NW
ALBUQUERQUE, NEW MEXICO



CHECKED BY March 17, 2022 DATE

SHEET TITLE

C101

Starbucks Coffee Inspections Plus, LLC

Commercial SWPPP map-Phase 1-Final

LEGEND





Temporary Stabilization / Seeding - Phase 2 (1)



Asphalt Paving (3)



Concrete Sidewalk (7)



New Building (1)



Retention Basin (3)



Silt Fence (3)



Cutback Curb / Sidewalk (14)



Pre & Post Construction Water Flow (5)



Drainage Swale (2)



Property Boundary (1)

_

Limit of Disturbance (1)



Spill Kit (1)



ERTEC Inlet Protection (1)



Water Truck (2)



Portable Toilet (1)



Portable Concrete Washout Bin (1)



Street Sweeping (2)



Stabilized Construction Exit (1)



SWPPP Sign (1)



Dumpster (1)




Materials Storage (1)



Blockade (1)



Stockpiles (1)



SCHEDULE/SEQUENCING OF CONSTRUCTION

- 1. POST PERMITS
- 2. INSTALL REQUIRED BMPs
 - 2.a. PERIMETER CONTROLS (SILT FENCE)
 - 2.b. STABILIZED CONSTRUCTION ENTRANCE
 - 2.c. CONCRETE WASHOUT AREA
- 3. EARTHWORK AND GRADING
- 4. UTILITY INSTALLATION
- **5. PAVEMENT STRUCTURES**
- 6. PAD STRUCTURES
- 7. LANDSCAPING
- 8. PUNCHLIST
- 9. STABLILIZE PHASE II AREA WITH SEED AND HYDRO MULCH

WITHIN 14 DAYS OF CONSTRUCTION COMPLETION.

Owner: Los Dows, LLC Aurther J. Dow Property Owner Contact 505-350-4477 dowaj@yahoo.com

Operator(s):
NCB Construction, Inc.
C. James Schomburg
Project Manager
325 Academy Road, Suite A
Corrales, NM 87048
505-238-2341
jschomburg05@msn.com

