




File Path: P:\JMW\106 83\1015.003.DWG | Plot Date: 03-08-2016
File Name: 151828_ESC-101.DWG | Plot Time: 11:15 am

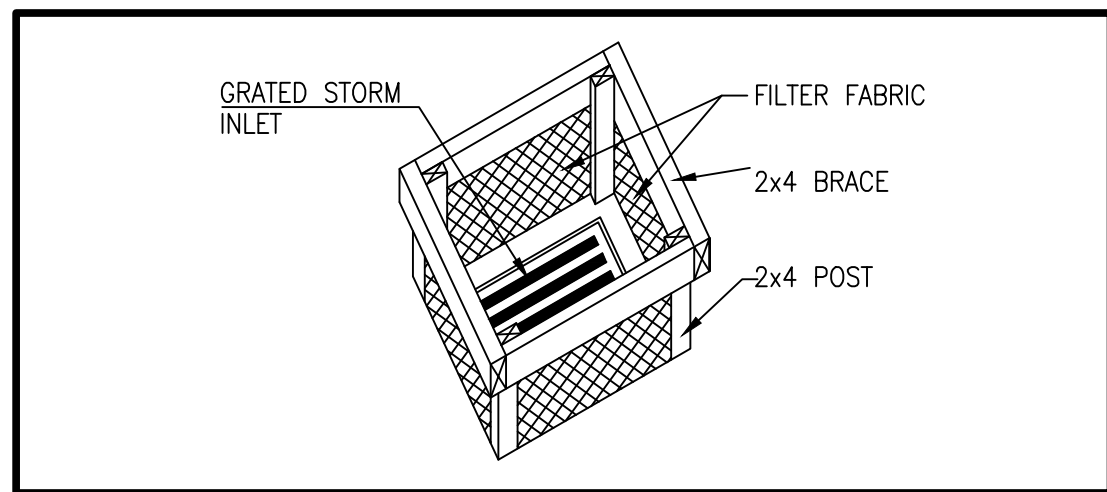


SILT FENCE INLET PROTECTION
NOT TO SCALE

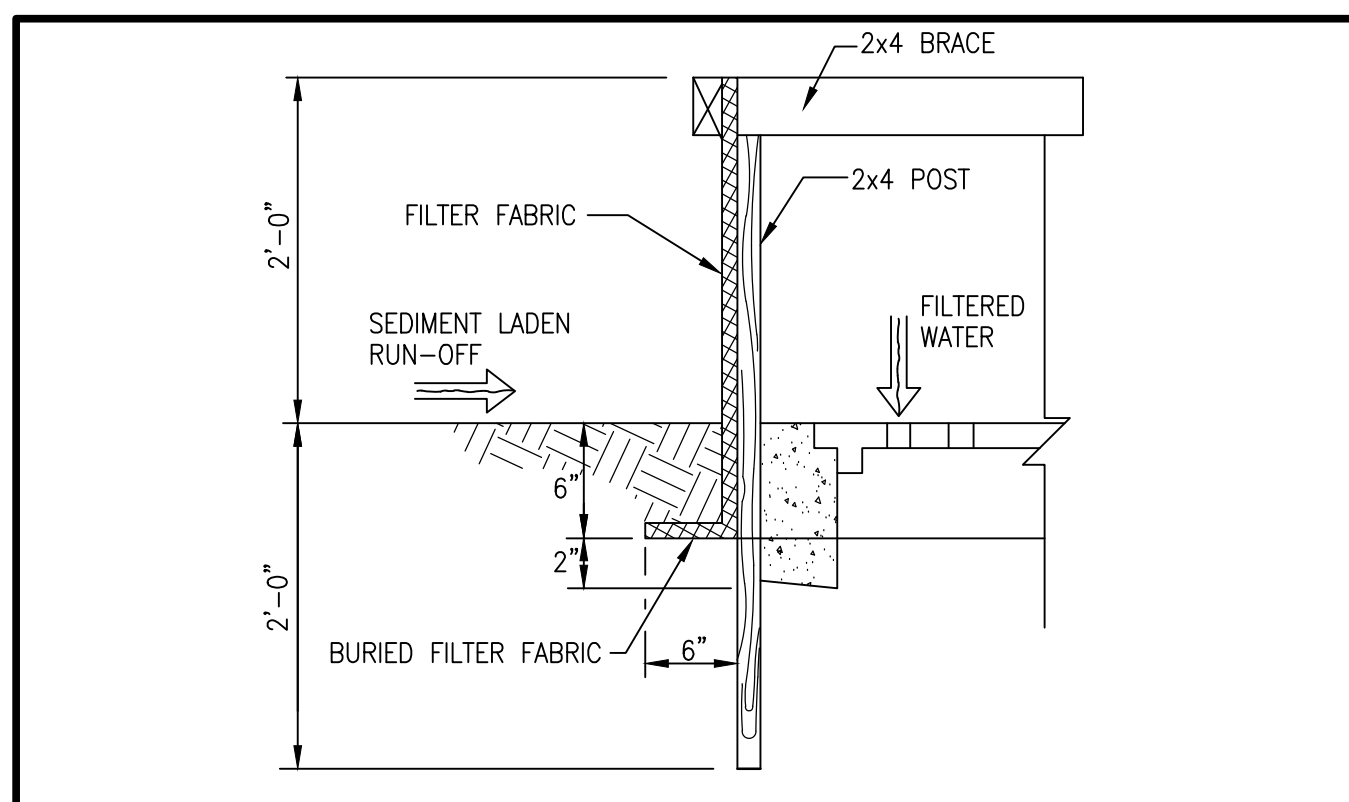


SILT FENCE INLET PROTECTION SECTION
NOT TO SCALE

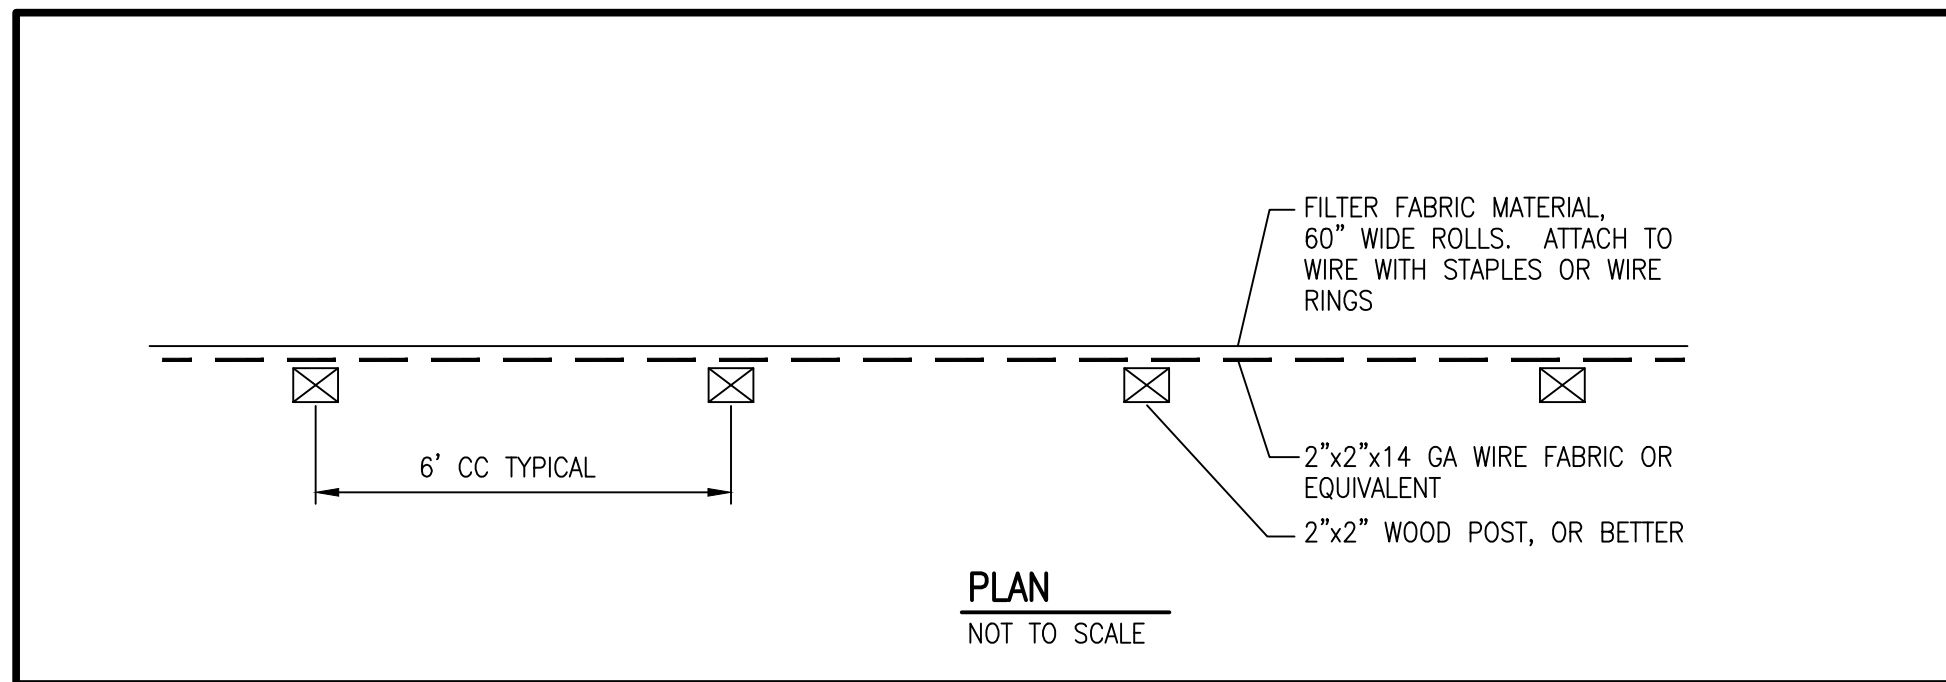


PLAN
NOT TO SCALE

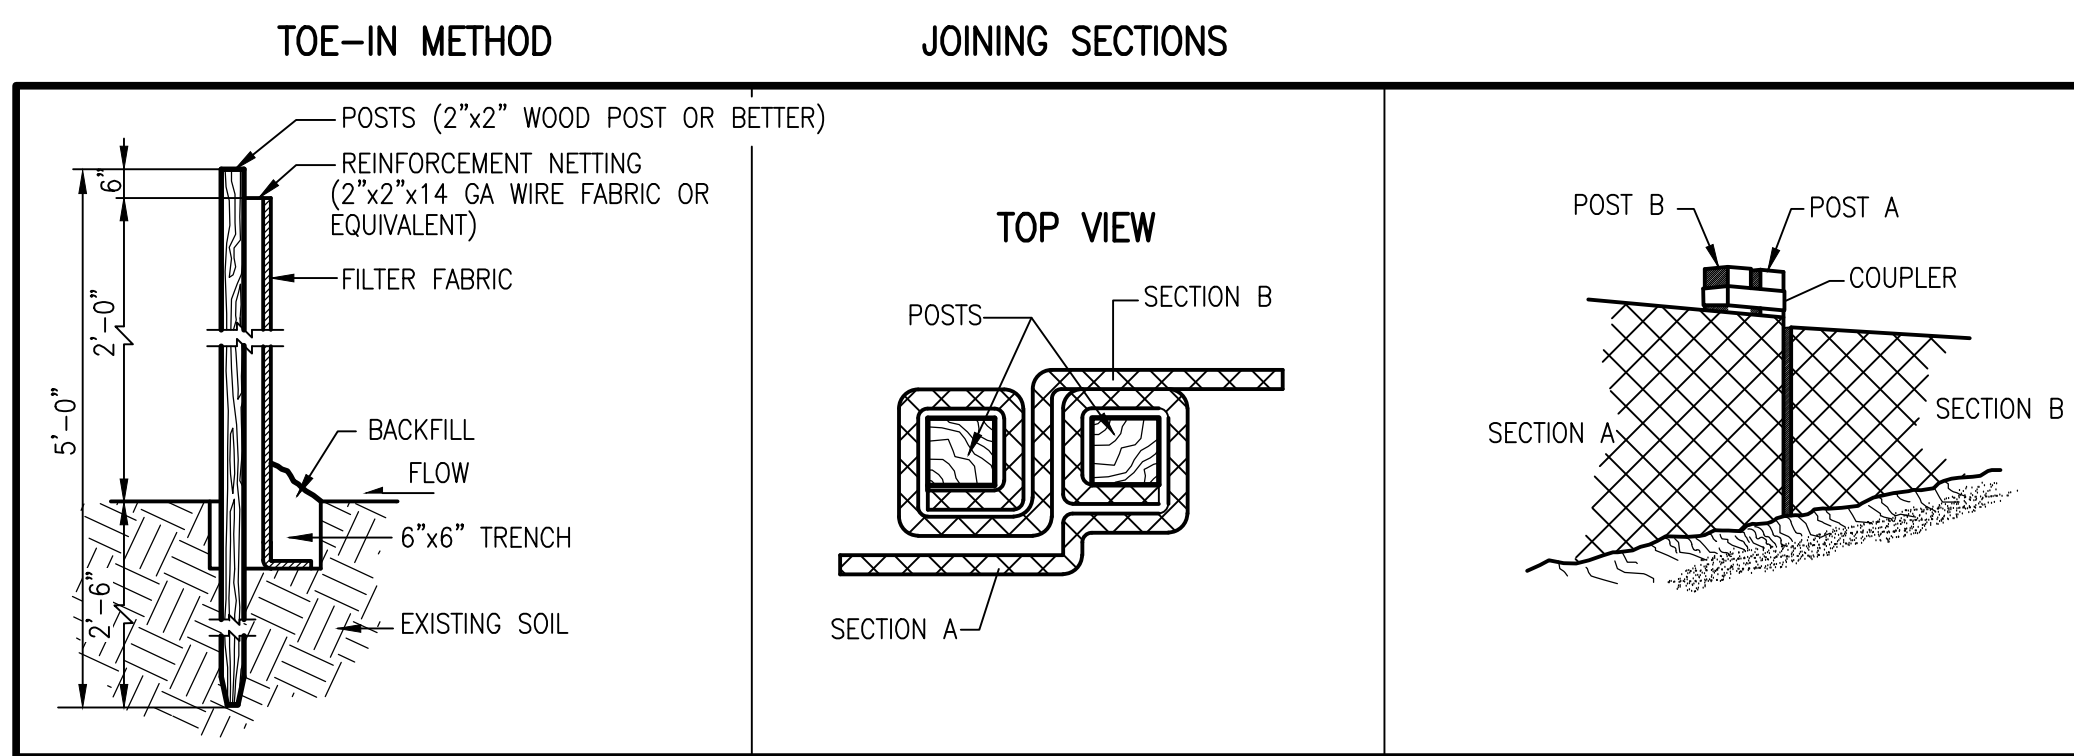


PREFABRICATED SILT FENCE DETAILS
NOT TO SCALE

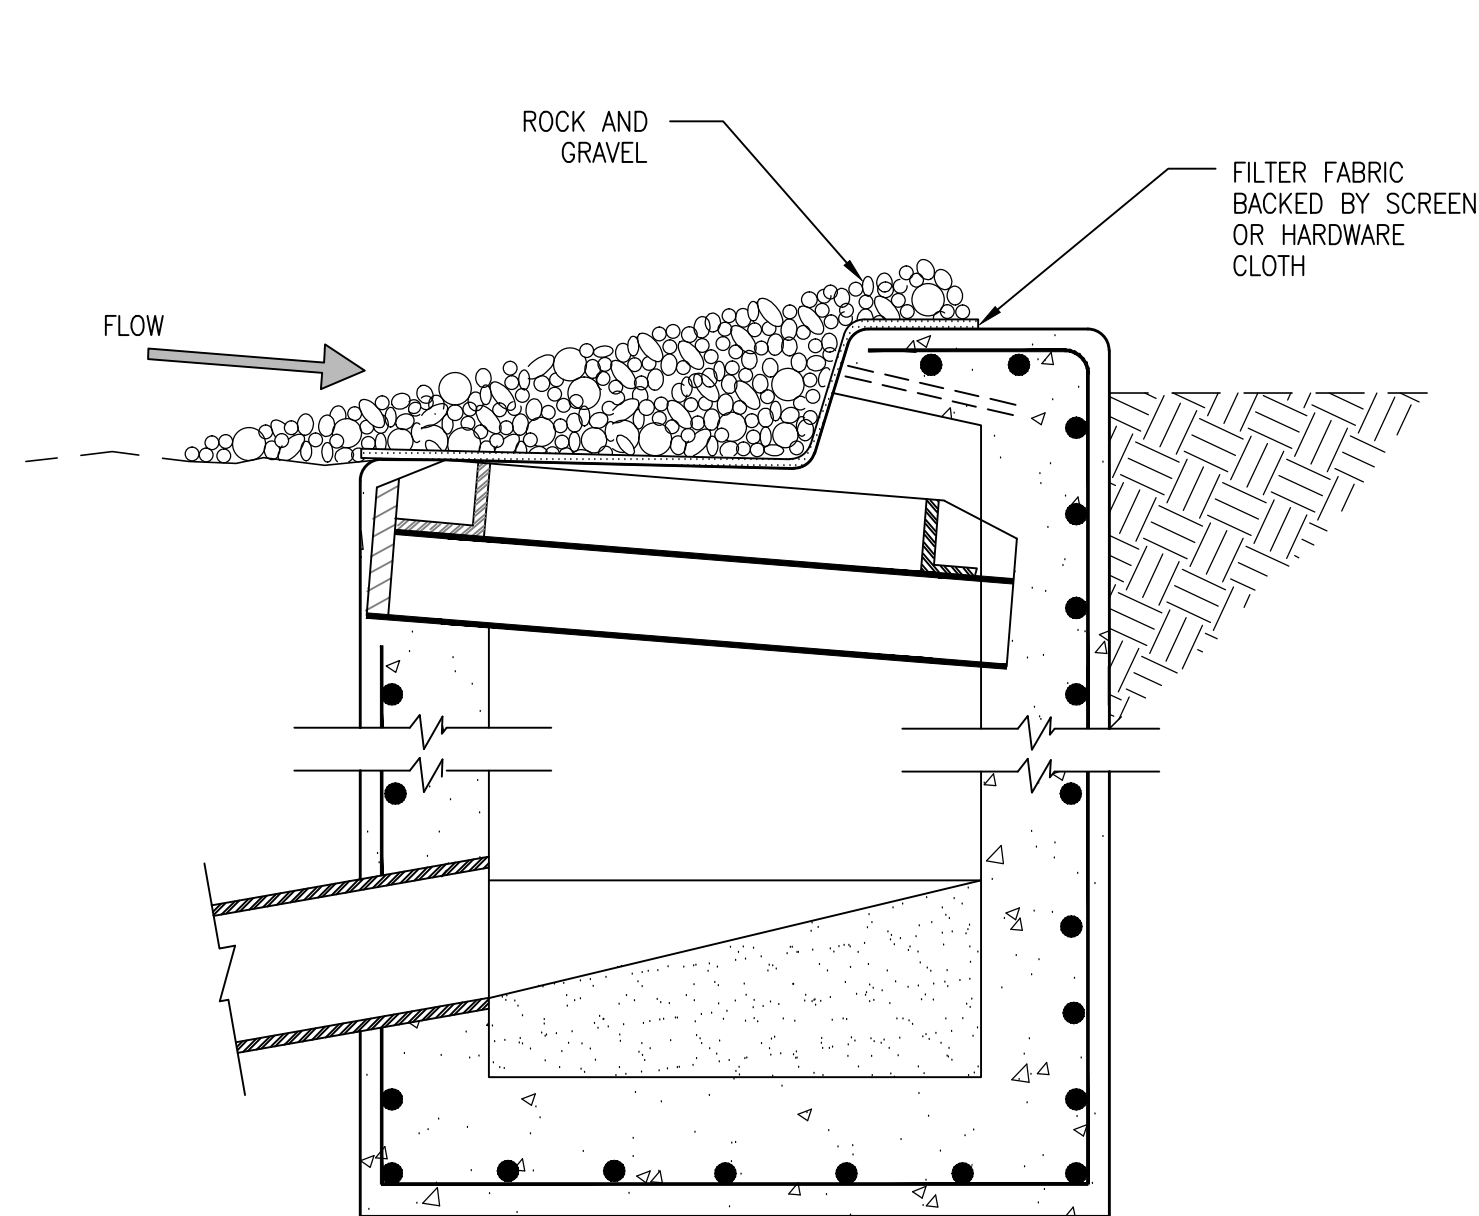

TYPICAL STORM INLET PROTECTION
SCALE: 1" = 1'-0"

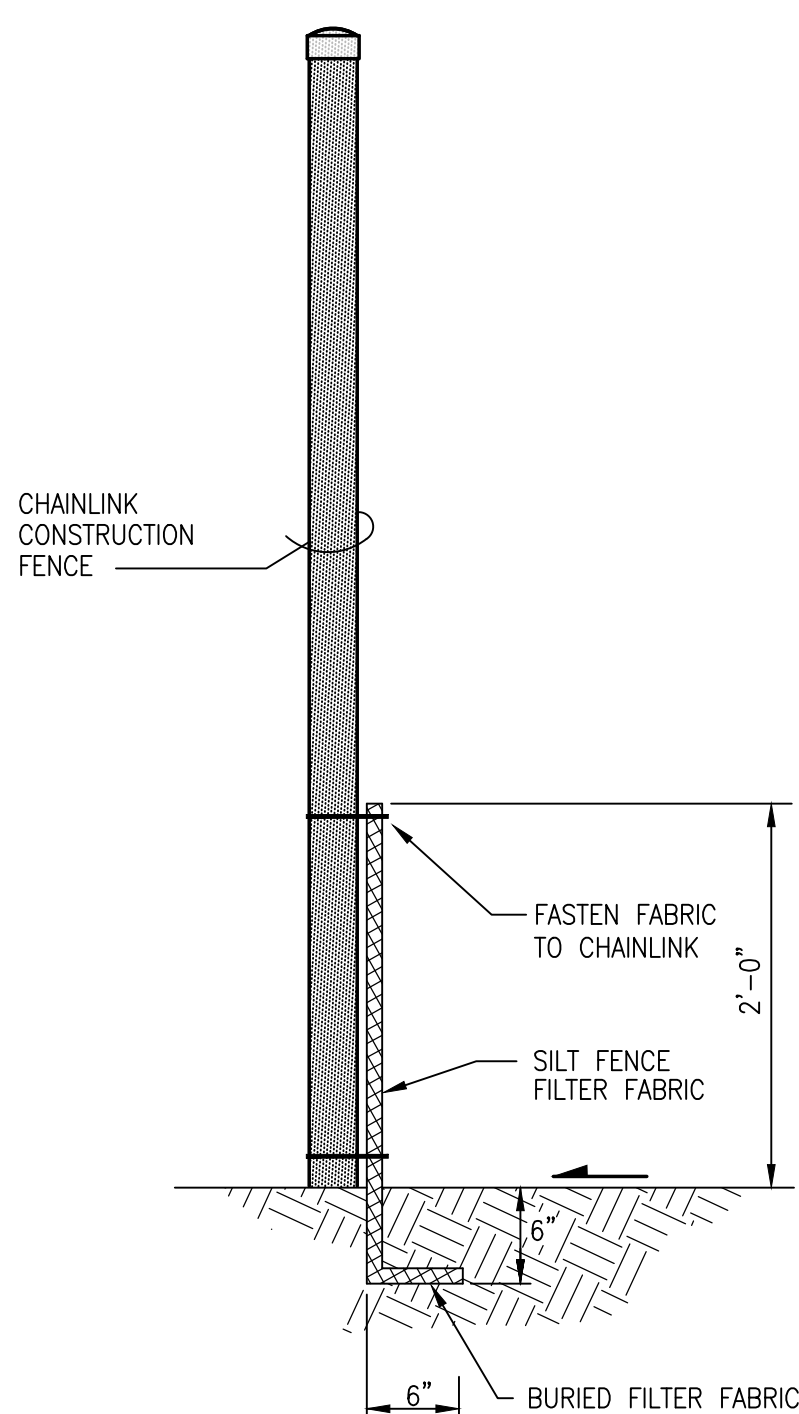


CONSTRUCTION FENCE/SILT FENCE SECTION
SCALE: 1" = 2'-0"

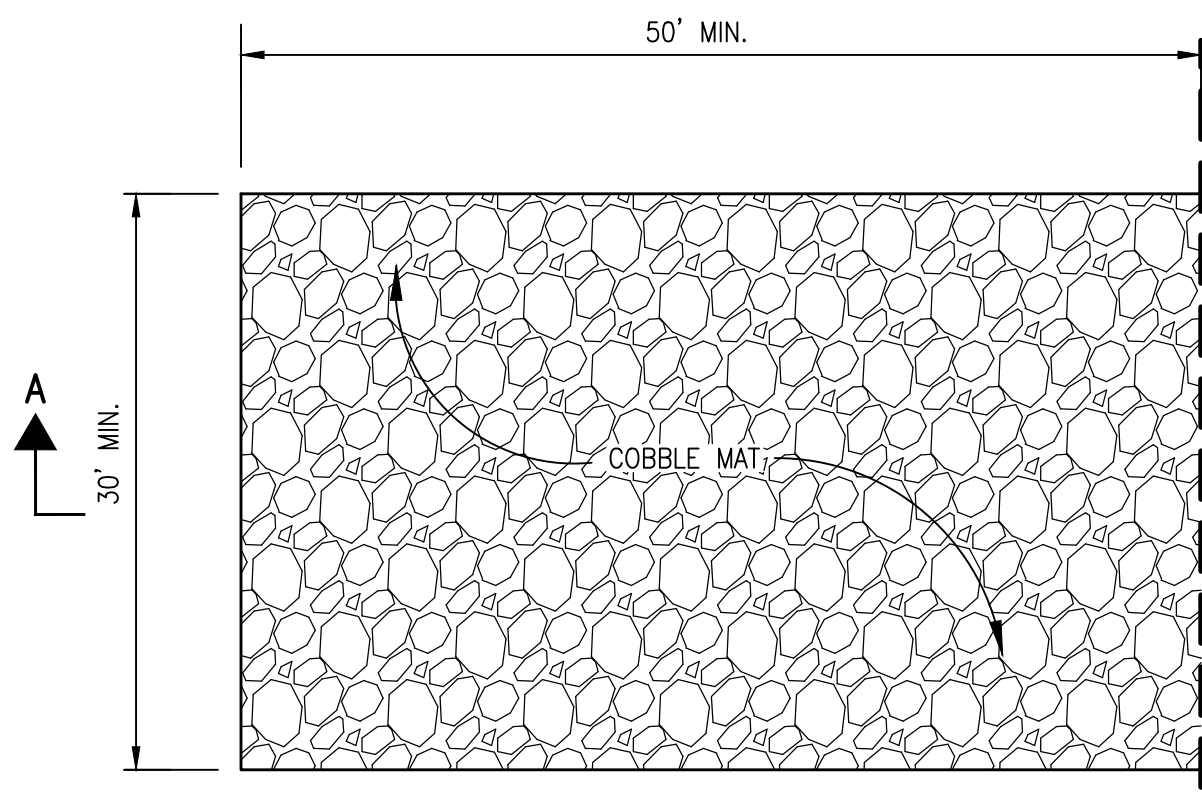

PLAN

CONSTRUCTION ENTRANCE STABILIZATION
SCALE: 1" = 10'-0" HORIZ.
1" = 2'-0" VERT.

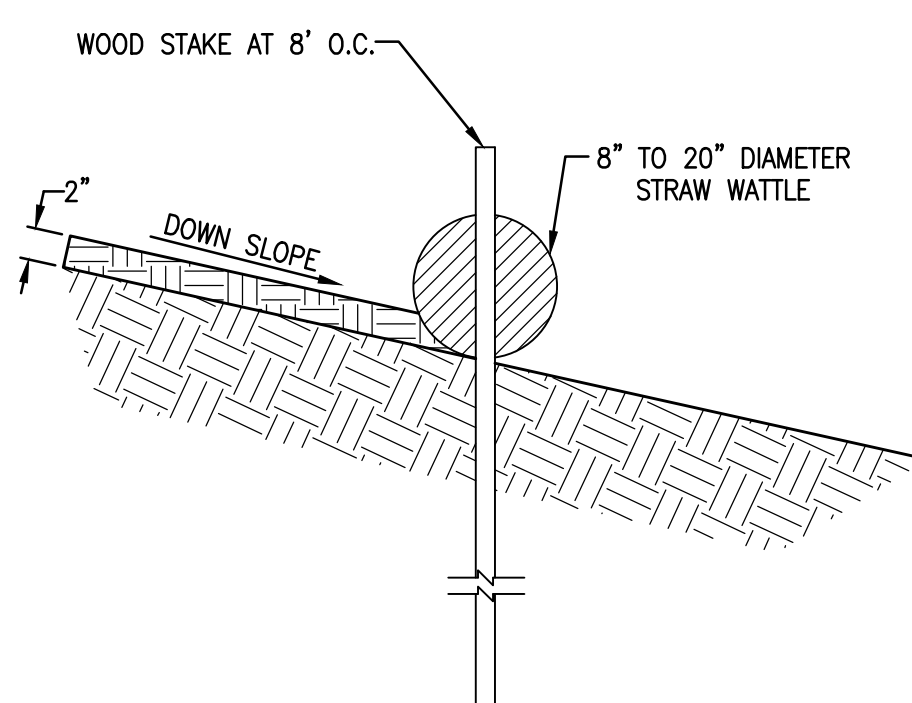


TYPICAL STRAW WATTLE INSTALLATION SECTION
SCALE: 1" = 1'-0"

SEED MIX FOR SANDY SOILS


VARIETY/COMMON NAME	GENUS/SPECIES	PLS/ACRE
"PALOMA" INDIAN RICE GRASS	ORYZOPSIS HYMENOIDES	5.0
"VIVA" GALLETA GRASS	HILARIA JAMESII	1.0
"NINER" SIDE OATS GRAMA	BOUTELOUA CURTIPENDULA	3.0
"HATCHITA" BLUE GRAMA	BOUTELOUA GRACILIS	1.0
SAND DROPSEED (NM REGION)	SPOROBOLUS CRYPTANDRUS	1.0
FOUR-WING SALT BUSH (NM REGION)	ATRIPLEX CANESCENS (DE-WINGED)	1.0
TOTAL RATE:		12.0 LBS/ACRE

EROSION AND SEDIMENT CONTROL PLAN NOTES:


- THIS PLAN ADDRESSES GENERAL AND SPECIFIC MEASURES FOR CONSTRUCTION PHASE EROSION, SEDIMENT AND DUST CONTROL. IT IS INTENDED TO COMPLEMENT THE PROJECT SPECIFIC STORM WATER POLLUTION AND PREVENTION PLAN (SWPPP) PREPARED FOR THE JEFFERSON MS MUSIC BUILDING ADDITION PROJECT THAT WILL BE ONGOING DURING THE CONSTRUCTION OF THE PUBLIC WATER LINE SHOWN IN THIS PLAN SET. THE BUILDING PERMIT PROJECT IS BROKEN INTO THREE PHASES. PHASE 1 INCLUDES THE NEW PARKING LOT CONSTRUCTION DURING WINTER 2015. PHASE 2A INCLUDES THE NEW MUSIC BUILDING CONSTRUCTION AND UTILITIES CONSTRUCTION WITHIN THE WEST STAFF PARKING LOT ADJACENT TO GIRARD BLVD NE FROM THE START OF 2016 TO SPRING 2016. PHASE 2B CONSTRUCTION INCLUDES PUBLIC WATER LINE CONSTRUCTION AND PRIVATE UTILITY AND ACCESS CONSTRUCTION FROM THE SUMMER OF 2016 TO FALL 2016. PHASE 3 CONSTRUCTION INCLUDES THE EXISTING ART BUILDING DEMOLITION, INTERIOR RENOVATIONS AND SITE WORK FROM THE FALL OF 2016 TO WINTER 2016.
- THE CONTRACTOR SHALL SECURE ALL REQUIRED PERMITS BEFORE BEGINNING CONSTRUCTION.
- THE CONTRACTOR SHALL INSTALL ALL PERIMETER Bmps BEFORE BEGINNING CONSTRUCTION.
- REFER TO THE SWPPP PREPARED BY EZRC, LLC, DATED 11-11-15 FOR PROJECT SPECIFIC PHASING AND INFORMATION. THIS PROJECT SHALL BE IMPLEMENTED IN PHASES TO MINIMIZE THE EXTENT AND DURATION OF SURFACE DISTURBANCE.
- REFER TO THE GRADING AND DRAINAGE PLAN PREPARED BY HIGH MESA CONSULTING GROUP, DATED 8-22-2015.
- THE CONTRACTOR SHALL ENSURE THAT NO SOIL ERODES FROM THE SITE INTO PUBLIC RIGHT-OF-WAY OR PRIVATE PROPERTY.
- THE CONTRACTOR SHALL PROMPTLY CLEAN-UP ANY MATERIAL EXCAVATED WITHIN THE PUBLIC RIGHT-OF-WAY SO THAT THE EXCAVATED MATERIAL IS NOT SUSCEPTIBLE TO BEING WASHED DOWN THE STREET.
- THE CONTRACTOR SHALL CLEAN AND REMOVE ALL FUGITIVE DUST, SOIL AND DEBRIS RESULTING FROM THIS PROJECT FROM THE ADJACENT STREETS AT THE END OF EACH DAY.
- THE CONTRACTOR SHALL IMPLEMENT AND MAINTAIN ALL GOOD HOUSEKEEPING MEASURES OUTLINED IN THE SWPPP INCLUDING , BUT NOT LIMITED TO, DAILY PICKING UP TRASH , LITTER AND CONSTRUCTION DEBRIS.
- THE CONTRACTOR SHALL PROMPTLY REMOVE SEDIMENT ACCUMULATION FROM SILT FENCES AND OTHER STRUCTURAL Bmps WITHIN 48 HOURS OF A RAINFALL EVENT.
- THE CONTRACTOR SHALL IMPLEMENT ONSITE STRUCTURAL EROSION CONTROL MEASURES AS REQUIRED TO COMPLY WITH THE EROSION AND SEDIMENT CONTROL PLAN AND SWPPP. THESE MEASURES MAY INCLUDE BUT ARE NOT LIMITED TO SILT FENCES, EARTHEN DIKES, DRAINAGE DIVERSIONS, SEDIMENT TRAPS, CHECK DAMS, SUBSURFACE DRAINS, PIPE SLOPE DRAINS, LEVEL SPREADERS, STORM WATER RETENTION SYSTEMS, GABIONS AND TEMPORARY OR PERMANENT SEDIMENT DETENTION BASINS. THE FOLLOWING MEASURES ARE PROPOSED FOR THIS PROJECT:
 - PERIMETER SILT FENCE
 - INTERIOR SILT FENCE
 - WATTLES
 - ONSITE INLET PROTECTION
 - INTERIM SEDIMENT DETENTION BASINS
 - GRAVEL MULCH
 - INTERIM REVEGETATION
 - SOIL STABILANT OR TACKIFIER
- THE CONTRACTOR SHALL MINIMIZE OFFSITE VEHICLE TRACKING OF SEDIMENT AND DUST GENERATION.
- CONCRETE TRUCKS SHALL BE SENT BACK TO THE PLANT FOR WASHING; THE WASHING OF CONCRETE TRUCKS SHALL NOT BE PERMITTED ON THIS SITE UNLESS OTHERWISE PROVIDED FOR BY THIS PLAN. IF PROVIDED FOR BY THIS PLAN, CONCRETE TRUCKS MAY ONLY WASH OUT IN A DESIGNATED AND LINED WASHOUT FACILITY.
- OFFSITE MATERIAL STORAGE AREAS USED BY THIS PROJECT ARE CONSIDERED PART OF THE PROJECT AND THEREFORE SUBJECT TO THE REQUIREMENTS OF THE EROSION AND SEDIMENT CONTROL PLAN AND SWPPP.
- UPON COMPLETION OF MASS GRADING, ALL DISTURBED AREAS SHALL BE STABILIZED WITH PERMANENT CONSTRUCTION, LANDSCAPING, VEGETATION AND/OR GRAVEL MULCH. SILT FENCING CAN BE REMOVED UPON SUCCESSFUL ESTABLISHMENT OF VEGETATION.
- THROUGHOUT THE DURATION OF THIS PROJECT, CONTRACTOR SHALL IMPLEMENT, MAINTAIN AND INSPECT ALL Bmps, KEEPING RECORDS OF EACH INSPECTION IN ACCORDANCE WITH THE SWPPP, AND KEEP RECORDS OF THE INSTALLATION MAINTENANCE, AND REMOVAL OF EACH Bmp SPECIFIED BY THIS PLAN OR OTHERWISE PROVIDED FOR THROUGHOUT THE LIFE OF THE PROJECT.
- THOSE PORTIONS OF THE COMPLETED PROJECT NOT STABILIZED WITH PERMANENT CONSTRUCTION OR FORMAL LANDSCAPING SHALL BE REVEGETATED WITH NATIVE GRASS SEEDING FOR SANDY SOILS PER THE SEED MIX SPECIFIED HEREIN AND SPECIFICATIONS CONTAINED WITHIN THE SWPPP.
- FINAL STABILIZATION OF THE PROJECT SITE WILL CONSIST OF THE FOLLOWING MEASURES:
 - PERMANENT BUILDING CONSTRUCTION
 - PERMANENT PAVING
 - FORMAL LANDSCAPING
 - GRAVEL MULCH
 - NATIVE GRASS VEGETATION
- TOTAL SITE AREA = 14.9997 AC± (BASED ON A LEASE SURVEY 2011.181.2 DATED 12-18-12 PREPARED BY BY HIGH MESA CONSULTING GROUP)
- TOTAL DISTURBED AREA = 3.59 AC±
- THE ACCESS AND UTILITY WORK PORTION OF THIS PROJECT IS SCHEDULED FOR SUMMER 2016. A NEW CONSTRUCTION ENTRANCE AT GIRARD BLVD. WILL BE REQUIRED DURING THIS TIME.

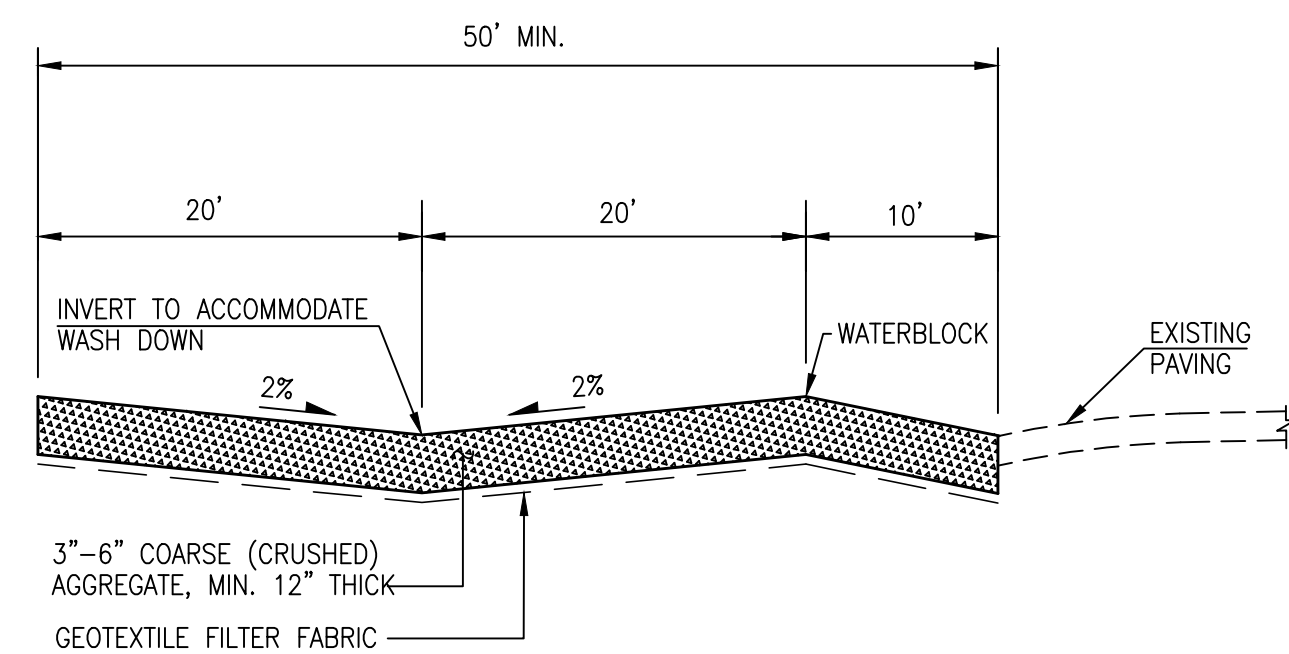


SECTION A-A

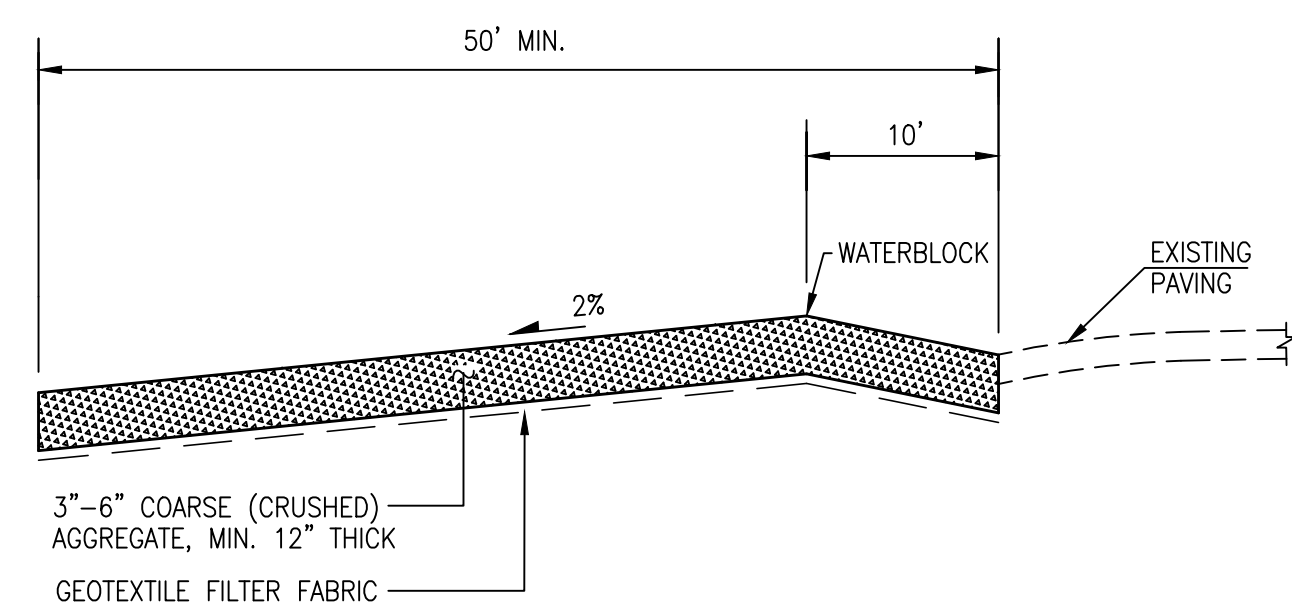

SECTION A-A

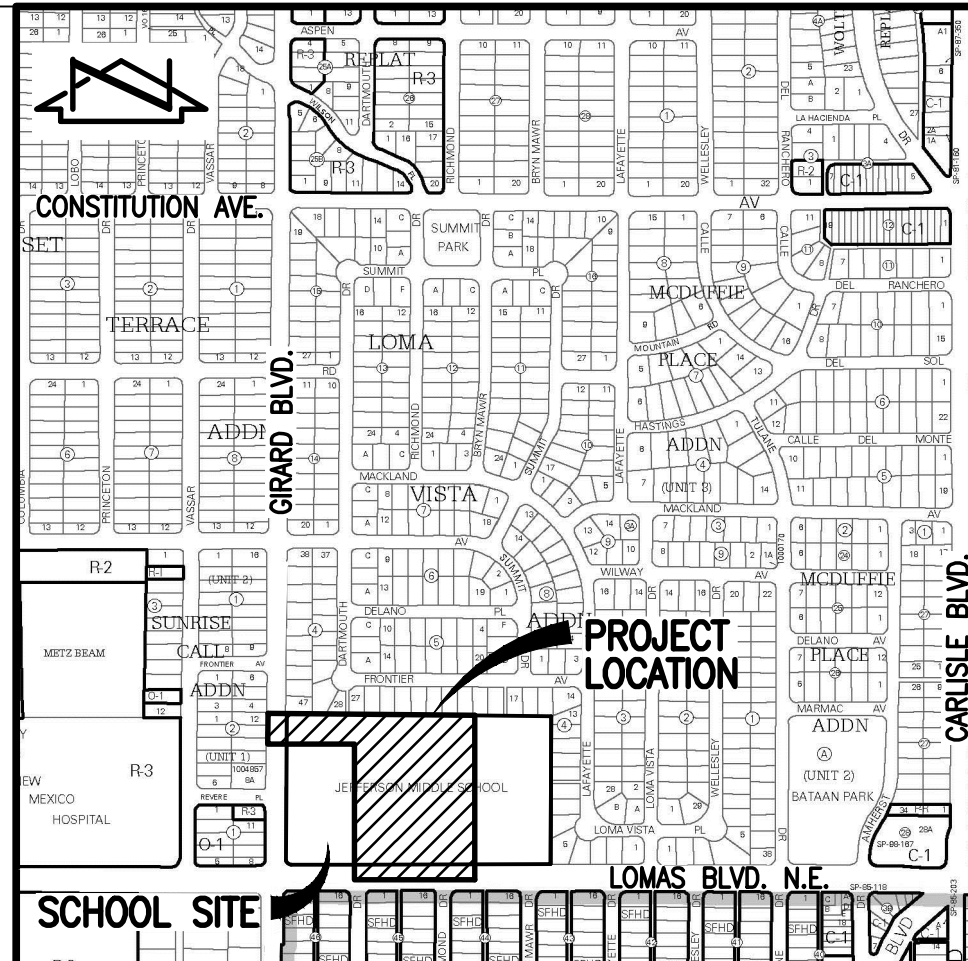

VICINITY MAP
SCALE: 1" = 750'

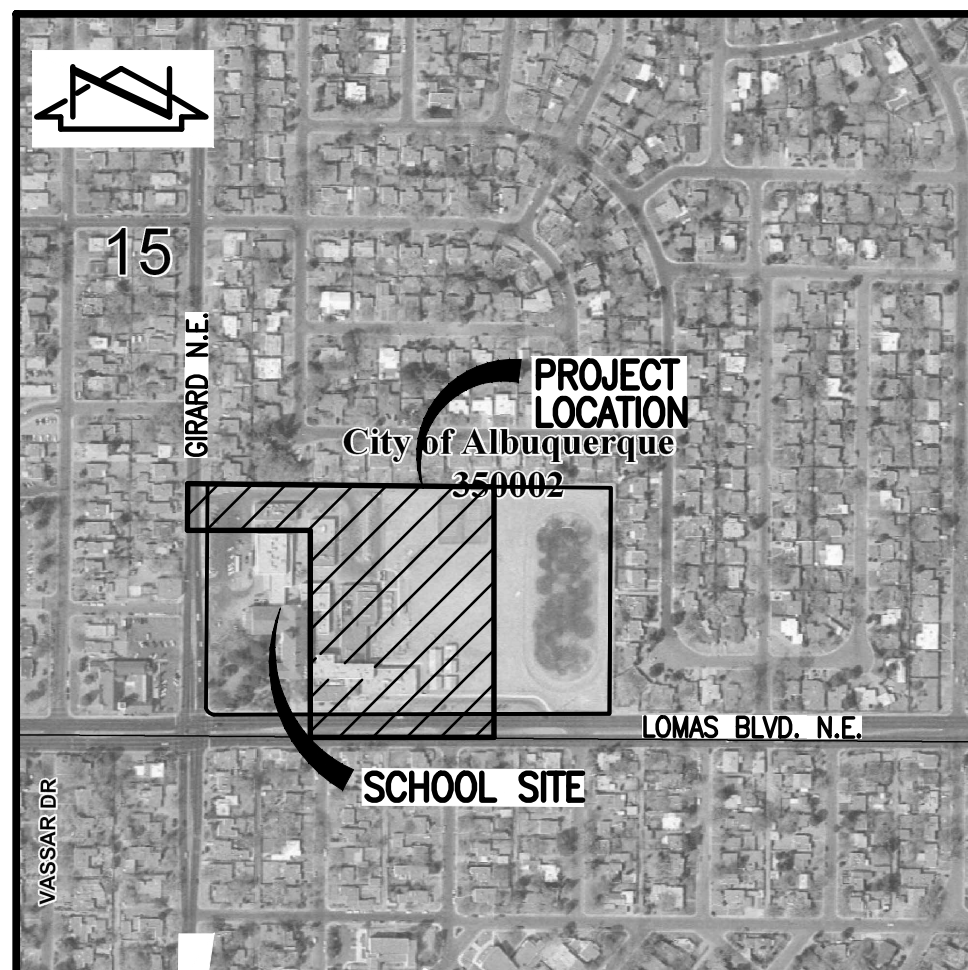

F.I.R.M. PANEL 353
SCALE: 1" = 500'
OF 825
DATE 09-26-2008

ARCHITECTURE / DESIGN / INSPIRATION

**DEKKER
PERICH
SABATINI**

7601 JEFFERSON NE, SUITE 100
ALBUQUERQUE, NM 87109

505.761.9700 / DPSDESIGN.ORG

ARCHITECT

ENGINEER




3-8-2016

PROJECT

JEFFERSON MIDDLE SCHOOL
PHASE 1 MUSIC CLASSROOM ADDITION
712 GIRARD BLVD. N.E.
ALBUQUERQUE, NM 87106

**100%
CONSTRUCTION
DOCUMENTS**

REVISIONS



DRAWN BY J.Y.R.

REVIEWED BY G.M.

DATE 03/2016

PROJECT NO. 14-0033.001

DRAWING NAME

**EROSION AND
SEDIMENT
CONTROL PLAN
NOTES AND
DETAILS**

SHEET NO.

ESC-101

**HIGH
MESA** Consulting Group

6010-8 MIDWAY PARK BLVD. NE • ALBUQUERQUE, NEW MEXICO 87109
PHONE: 505.345.4250 • FAX: 505.345.4254 • www.highmesacg.com

2014.063.T

2015.182.8
