



# VOLCANO RV STORAGE

## TEMPORARY SEDIMENT AND EROSION CONTROL DRAWINGS

### ALBUQUERQUE, BERNALILLO COUNTY, NEW MEXICO

#### DRAWING INDEX

- 1 COVER SHEET
- 2 PROJECT DETAILS
- 3 GENERAL NOTES
- 4 BEST MANAGEMENT PRACTICES
- 5 BEST MANAGEMENT PRACTICES
- 6 BEST MANAGEMENT PRACTICES
- 7 BEST MANAGEMENT PRACTICES
- 8 TEMPORARY EROSION & SEDIMENT CONTROL PLAN
- 9 FINAL STABILIZATION

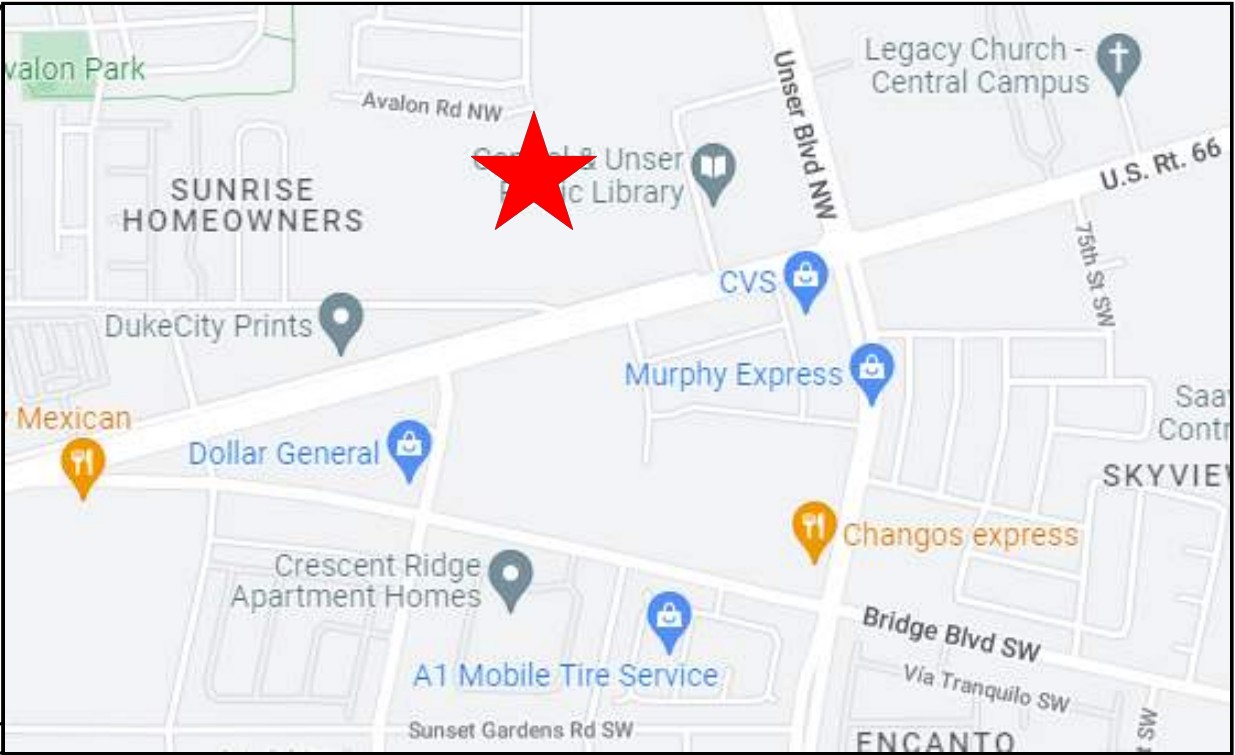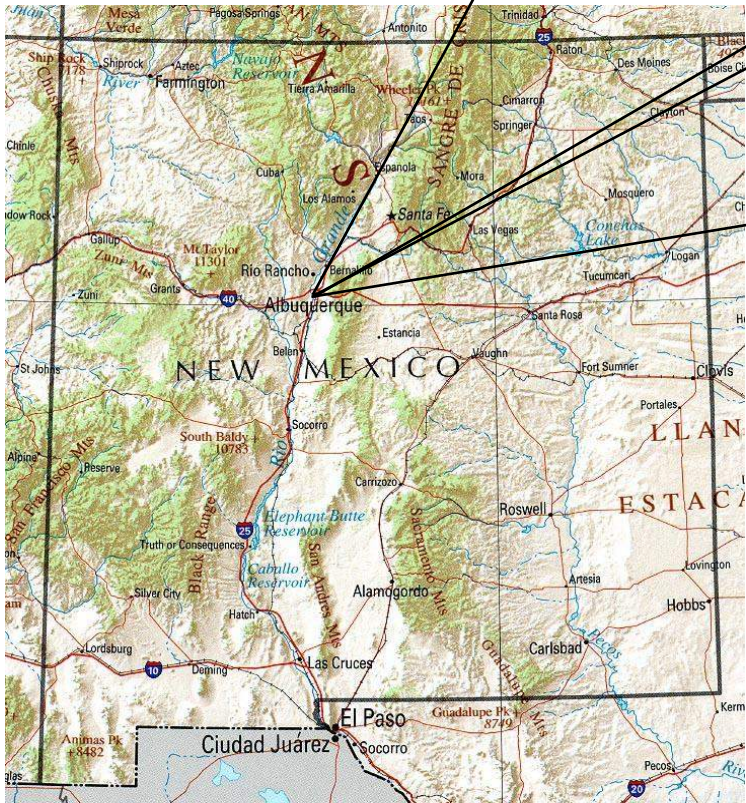

SWPPP  
Stormwater  
Erosion Control  
Reclamation  
Seeding

www.e2rc.com | 505.867.4040



DATE	REVISION ITEM	#

RMD CONSTRUCTION, LLC  
VOLCANO RV STORAGE  
ALBUQUERQUE, NM

DESIGNED BY:  
K. FETTER, P.E.  
DRAWN BY:  
S. FETTER

SHEET:  
COVER

## PROJECT DETAILS

NPDES ID: NMR10050L, NMR10055K

ADDRESS: VOLCANO RD. NW & CENTRAL AVE. NW, ALBUQUERQUE, NM 87121

GPS COORDINATES: 35.077647, -106.729109

TOTAL ACREAGE: 9.6

ANTICIPATED DISTURBED ACREAGE: 9.6

FIRST RECEIVING WATER: RIO GRANDE (NM-2105\_51)

WATERS WITHIN ONE MILE OF PROJECT: NONE

IMPAIRED/TIERED WATERS: RIO GRANDE

### ENDANGERED SPECIES: CRITERION A

SUPPORT ACTIVITIES: SEE SECTION 3.6 OF SWPPP NARRATIVE

SOIL TYPE: SEE NRCS SOIL REPORT PROVIDED IN SWPPP BINDER

TYPE PRE-CONSTRUCTION COVER: NATIVE VEGETATION, APPROXIMATELY 50% DENSITY

STABILIZATION MEASURES AND DEADLINES: SEE SECTION 6.0 OF SWPPP NARRATIVE

REGULATING AUTHORITY: ENVIRONMENTAL PROTECTION AGENCY (EPA)

## OPERATORS

PROPERTY OWNER:  
VOLCANO RV, LP  
142 HAWLEY STREET, UNIT #6  
GRAYSLAKE, IL 60030

OWNER CONTACT:  
BEN LOKHORST  
VICE PRESIDENT  
(403) 973-4882

GENERAL CONTRACTOR (GC):  
RMD CONSTRUCTION, LLC  
549 W. RANDOLPH STREET, SUITE 704  
CHICAGO, IL 60661

GC CONTACT:  
MATTHEW MONTOYA  
(505) 469-9074

STORMWATER TEAM

SEE SECTION 2.0 OF THE SWPPP NARRATIVE FOR THE PROJECT'S STORMWATER TEAM, RESPONSIBILITIES AND CONTACT INFORMATION

## SEQUENCE OF ACTIVITIES

REFER TO THE ANTICIPATED CONSTRUCTION SCHEDULE INCLUDED WITH THE SWPPP BINDER

## PHASE I: SITE PREPARATION AND PRE – CONSTRUCTION

1. PRIOR TO BEGINNING EARTH DISTURBING ACTIVITIES, THE OPERATOR(S) WILL CLEARLY DEMARCATÉ THE LIMITS OF DISTURBANCE WITH STAKES, RIBBONS, CONSTRUCTION FENCING, OR OTHER APPROPRIATE METHOD. THESE DEMARCATIÖNS SHALL REMAIN VISIBLE FOR THE DURATION OF THE PROJECT.

2.THE INITIAL EROSION CONTROL MEASURES SHALL BE INSTALLED PRIOR TO EARTH DISTURBANCE. THE INITIAL CONTROL MEASURES MAY INCLUDE BUT ARE NOT LIMITED TO:

- a.PERIMETER CONTROLS (E.G., SILT FENCE, WATTLES, CONSTRUCTION FENCE)
- b.VEHICLE TRACKING PAD IF THE SITE ENTERS/EXITS ONTO A PAVED PUBLIC ROADWAY
- c.NPDES NOTIFICATION POSTING
- d.DESIGNATED STAGING AREA
- e.ANCHORED SANILETS
- f.DUMPSTERS

## PHASE II: CONSTRUCTION ACTIVITIES

1.THE OPERATORS WILL MINIMIZE THE AREA DISTURBED AS MUCH AS FEASIBLY POSSIBLE.

2. ANY DISTURBED AREA IN WHICH CONSTRUCTION ACTIVITIES HAVE TEMPORARILY CEASED SHALL TEMPORARILY STABILIZED USING THE METHODS DESCRIBED IN SECTION 6.4 OF THE SWPPP NARRATIVE. SECTION 6.3 OF THE SWPPP NARRATIVE PROVIDES THE TEMPORARY STABILIZATION DEADLINES.

3.THE LOCATION OF SOME BMPS MAY REQUIRE ALTERATION IF DRAINAGE PATTERNS CHANGE DURING CONSTRUCTION. THE OPERATORS SHALL INSTALL ADDITIONAL BMPS OR UPGRADE BMPS IF NECESSARY.

4. IF CONCRETE IS USED ONSITE AND CONCRETE TRUCKS ARE UNABLE TO WASHOUT OFFSITE, THE OPERATORS WILL PROVIDE ONE OR MORE DESIGNATED CONCRETE WASHOUT AREAS. THE CONCRETE WASHOUTS MUST BE INSTALLED PRIOR TO CONCRETE USE ONSITE AND REMOVED ONLY AFTER CONCRETE WORK IS COMPLETE.

### PHASE III: FINAL STABILIZATION AND CONSTRUCTION COMPLETION

1. IF APPLICABLE, REVEGETATION OR LANDSCAPING SHALL BE INITIATED IMMEDIATELY UPON KNOWING WORK IN A DISTURBED AREA HAS PERMANENTLY STOPPED AND THE AREA IS NOT COVERED BY PERMANENT STRUCTURES, UNLESS INFEASIBLE. SECTION 6.5 OF THE SWPPP NARRATIVE DISCUSSES PERMANENT STABILIZATION AND ASSOCIATED DEADLINES.

2.THE OPERATORS SHALL REMOVE TEMPORARY BMPS ONLY AFTER FINAL STABILIZATION IS COMPLETE.



SWPPP  
Stormwater  
Erosion Control  
Reclamation  
Seeding

www.e2rc.com | 505.867.4040

[illegible]

RMD CONSTRUCTION, LLC  
VOLCANO RV STORAGE  
SWPPP NOTES

DESIGNED BY:  
K. FETTER, P.E.  
DRAWN BY:  
S. FETTER

SHEET:  
GENERAL  
NOTES



GENERAL NOTES

THE NPDES COMPLIANCE SWPPP DRAWING AND ASSOCIATED DOCUMENTATION IS AND SHALL BE CONSIDERED A LIVING DOCUMENT ALLOWING FOR MODIFICATIONS AS SITE CONDITIONS CHANGE OR DICTATE.

ALL SITE FEATURES (EXISTING/PROPOSED GRADES, EXISTING CONSTRUCTION, FUTURE CONSTRUCTION, ETC.) SHOWN IS PER INFORMATION FROM OTHERS.

MINIMUM REQUIREMENTS TO FURTHER DEVELOP OR MODIFY THIS STORMWATER POLLUTION PREVENTION PLAN (SWPPP) DRAWING SHALL BE BASED ON THE CURRENT EDITION OF THE NEW MEXICO STATE HIGHWAY AND TRANSPORTATION DEPARTMENT (NMSHTD), NPDES LAW AND CITY OF ALBUQUERQUE ORDINANCE § 14-5-2-11.

ALL OPERATORS SHALL SUBMIT A NOTICE OF INTENT (NOI). THE NOI SHALL BE ACTIVE AND POSTED ON THE EPA'S WEBSITE PRIOR TO COMMENCING EARTH DISTURBING ACTIVITIES.

LOCATE TEMPORARY WASHOUT, ANCHORED TOILETS, CONSTRUCTION ENTRANCE AND PARKING, STAGING, REFUELING, TRASH CONTAINMENT AREA TO MINIMIZE SITE DISTURBANCE DURING CONSTRUCTION ACTIVITY.

THE OPERATOR IS REQUIRED TO REGULARLY PERFORM STREET SWEEPING AND CLEAN - UP MEASURES IN THE EVENT OF SEDIMENT TRACK - OUT.

THE FOLLOWING ARE STANDARD EROSION CONTROL REQUIREMENTS PER THE CITY OF ALBUQUERQUE STORMWATER QUALITY DEPARTMENT (MARCH 24, 2021):

ALL EROSION AND SEDIMENT CONTROL (ESC) WORK ON THESE PLANS, EXCEPT AS OTHERWISE STATED OR PROVIDED HEREON SHALL BE PERMITTED, CONSTRUCTED, INSPECTED, AND MAINTAINED IN ACCORDANCE WITH:

THE CITY ORDINANCE § 14-5-2-11, THE ESC ORDINANCE;  
THE EPA'S 2022 CONSTRUCTION GENERAL PERMIT (CGP); AND  
THE CITY OF ALBUQUERQUE CONSTRUCTION BMP MANUAL

ALL TEMPORARY SEDIMENT AND EROSION CONTROL MEASURES MUST BE INSTALLED PRIOR TO BEGINNING ANY EARTH MOVING ACTIVITIES EXCEPT AS SPECIFIED HEREON IN THE PHASING PLAN. CONSTRUCTION OF EARTHEN BMPS SUCH AS SEDIMENT TRAPS, SEDIMENT BASINS, AND DIVERSION BERMS SHALL BE COMPLETED AND INSPECTED PRIOR TO ANY OTHER CONSTRUCTION OR EARTHWORK. SELF-INSPECTION IS REQUIRED AFTER INSTALLATION OF THE BMPS AND PRIOR TO BEGINNING CONSTRUCTION.

SEE SECTION 3.5 OF THE SWPPP NARRATIVE OR THE CONTRACTOR'S SCHEDULE (TAB II OF SWPPP BINDER) FOR BMP SCHEDULING OR PHASING.

SELF-INSPECTIONS - AT A MINIMUM A ROUTINE COMPLIANCE SELF-INSPECTION IS REQUIRED TO REVIEW THE PROJECT FOR COMPLIANCE WITH THE CONSTRUCTION GENERAL PERMIT ONCE EVERY 14 DAYS AND AFTER ANY PRECIPITATION EVENT OF 1/4 INCH OR GREATER UNTIL THE SITE CONSTRUCTION HAS BEEN COMPLETED AND THE SITE DETERMINED AS STABILIZED BY THE CITY. REPORTS OF THESE INSPECTIONS SHALL BE KEPT BY THE PERSON OR ENTITY AUTHORIZED TO DIRECT THE CONSTRUCTION ACTIVITIES ON THE SITE AND MADE AVAILABLE UPON REQUEST.

CORRECTIVE ACTION REPORTS MUST BE KEPT BY THE PERSON OR ENTITY AUTHORIZED TO DIRECT THE CONSTRUCTION ACTIVITIES ON THE SITE AND MADE AVAILABLE UPON REQUEST.

STABILIZATION REPORTS MUST BE KEPT BY THE PERSON OR ENTITY AUTHORIZED TO DIRECT THE CONSTRUCTION ACTIVITIES ON THE SITE AND MADE AVAILABLE UPON REQUEST. REPORTS SHOULD INCLUDE RECORDS OF WEED REMOVAL PER CITY ORDINANCE (§ 9-8-1), STERILIZATION, SOIL TEST RESULTS AND RECOMMENDATION, MATERIALS AND MANUFACTURER'S SPECIFICATIONS FOR APPLICATION RATES, ESTIMATED FUNCTIONAL LONGEVITY, METHODS OF APPLICATION, INSPECTION AND MAINTENANCE. THE REDUCED SELF-INSPECTION SCHEDULE IN CGP 4.4.1 APPLIES TO STABILIZED AREA AND ANY DAMAGED OR WORN STABILIZATION MUST BE IDENTIFIED IN THE REPORTS ALONG WITH WEED PROBLEMS. CORRECTIVE ACTIONS FOR STABILIZATION SHALL BE DOCUMENTED IN A STABILIZATION REPORT INCLUDING ACTUAL RATES AND DATES OF STABILIZATION, AND THE MATERIALS AND MANUFACTURER'S SPECIFICATIONS USED.

BMPS SHALL BE INSPECTED AND MAINTAINED UNTIL ALL DISTURBED AREAS ARE STABILIZED IN ACCORDANCE WITH THE FINAL STABILIZATION CRITERIA (CGP 2.2.14.B). GENERALLY, ALL DISTURBED AREAS, OTHER THAN STRUCTURES AND IMPERVIOUS SURFACES, MUST HAVE UNIFORM PERENNIAL VEGETATION THAT PROVIDES 70 PERCENT OR MORE OF THE COVER PROVIDED BY NATIVE VEGETATION OR SEED THE DISTURBED AREA AND PROVIDE NON-VEGETATIVE MULCH THAT PROVIDES COVER FOR AT LEAST THREE YEARS WITHOUT ACTIVE MAINTENANCE. FINAL STABILIZATION MUST BE APPROVED BY THE CITY OF ALBUQUERQUE PRIOR TO REMOVAL OF BMPS AND DISCONTINUATION OF INSPECTIONS.



					DATE
					REVISION ITEM
					#

RMD CONSTRUCTION, LLC  
VOLCANO RV STORAGE  
SWPPP NOTES




SWPPP  
Stormwater  
Erosion Control  
Reclamation  
Seeding

www.e2rc.com | 505.867.4040

DESIGNED BY:  
K. FETTER, P.E.  
DRAWN BY:  
S. FETTER


SHEET:  
GENERAL  
NOTES

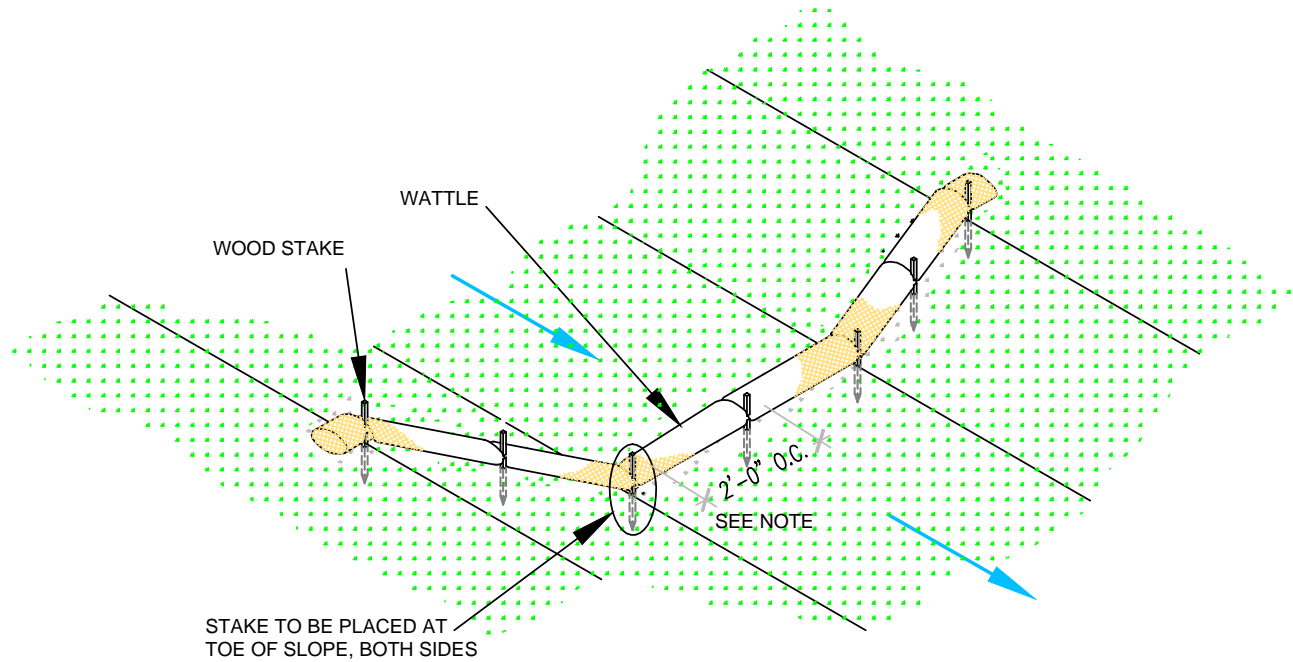

**WATTLE  
WITHOUT BLANKET**

NTS

2' FOR DRAWING ONLY. 8' MAX  
SPACING BETWEEN STAKES

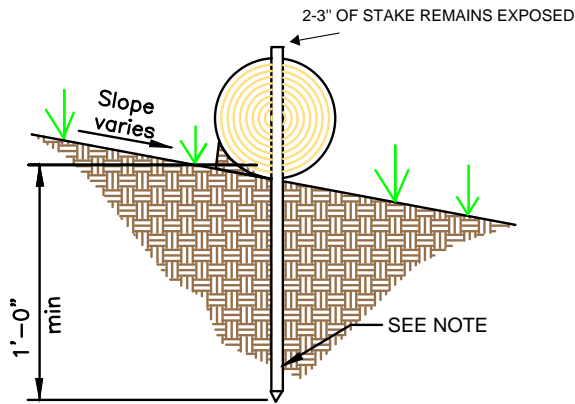



**WATTLE**

NTS

SECURE WATTLE WITH 18-24" STAKES EVERY 3-4' AND STAKES ON EACH END OF THE WATTLE.

DRIVE STAKES PERPENDICULAR TO THE SLOPE FACE AND THROUGH THE MIDDLE OF THE WATTLE LEAVING AT  
LEAST 2-3" OF THE STAKE ABOVE THE WATTLE.

VERTICAL SPACING DEPENDENT ON SLOPE GRADIENT.

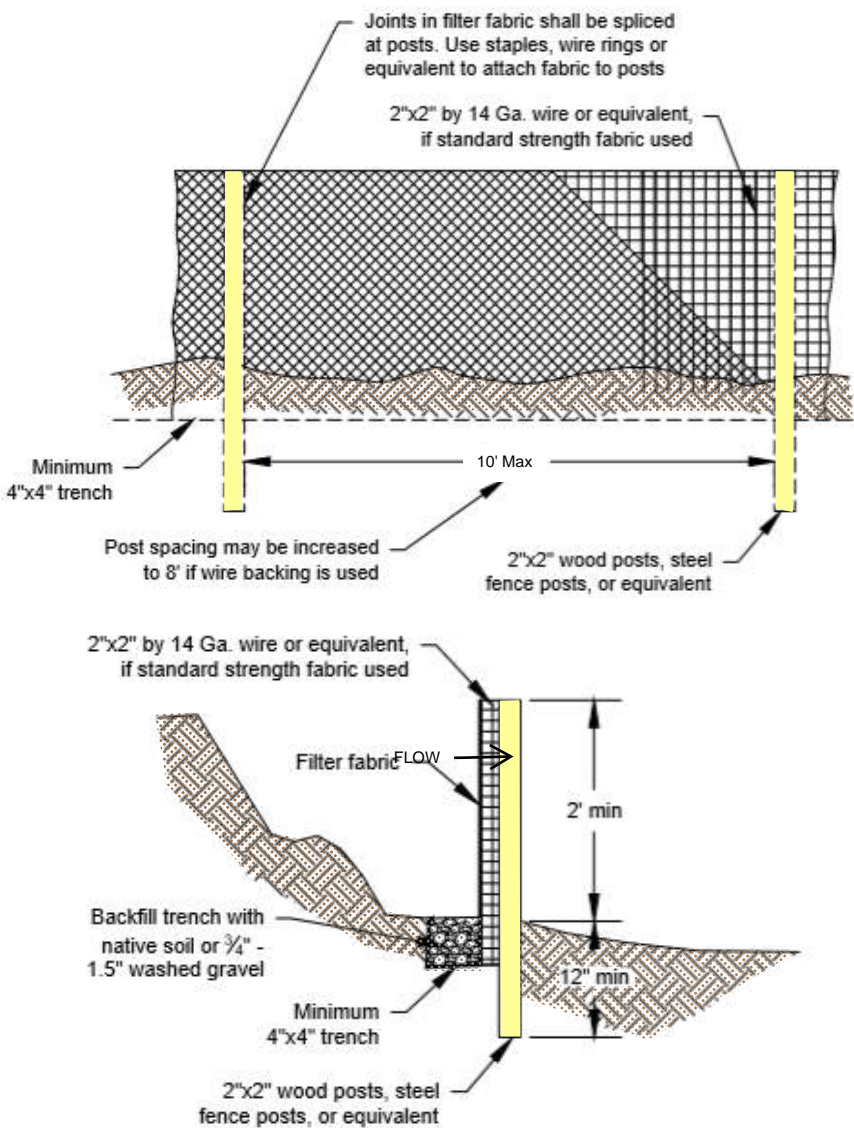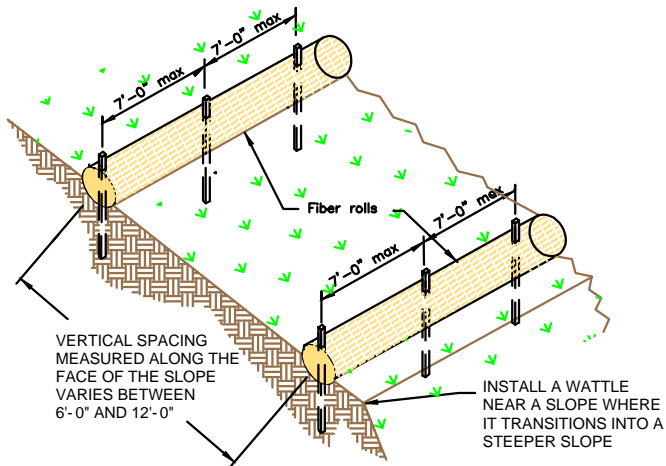

**SILT FENCE**

NTS

SILT FENCE IS TO BE PLACED PERPENDICULAR TO THE SLOPE OF THE SITE.

DIG A 4"x4" MINIMUM TRENCH UPSTREAM OF THE SILT FENCE. DRIVE STAKES AT LEAST 1' DEEP ON THE DOWNSTREAM EDGE.

RUN THE SILT FENCE ON THE INSIDE OF THE STAKES AND SECURE WITH HOG RINGS, WIRE, ZIP TIES OR STAPLES.

IF ONE CONTINUOUS PIECE OF FABRIC IS NOT AVAILABLE, OVERLAP THE FABRIC AT LEAST THE WIDTH OF THE STAKE AND SECURE WITH HOG RINGS, WIRE, ZIP TIES OR STAPLES.

COVER TRENCH WITH BACKFILLED COMPACTED SOIL, GRAVEL OR ROCK.



SWPPP  
Stormwater  
Erosion Control  
Reclamation  
Seeding

www.e2rc.com | 505.867.4040



				DATE
				REVISION ITEM
				#

RMD CONSTRUCTION, LLC  
VOLCANO RV STORAGE  
BMP DETAILS

DESIGNED BY:  
K. FETTER, P.E.  
DRAWN BY:  
S. FETTER

SHEET:

4



ONCE/IF THE SPOILS STOCKPILE IS DEPLETED OR MOVED,  
REMOVE THE WATTLES AND REUSE THEM IN THE NEXT  
LOCATION.



ONCE THE TRANCH IS BACKFILLED, WATTLES MAY BE REMOVED AND REUSED IN THE NEXT SECTION OF EXCAVATION PROVIDED THEY ARE IN GOOD CONDITION.



IF MULTIPLE DAMS ARE USED, THE TOP OF THE LOWER DAM SHOULD BE THE SAME HEIGHT AS THE ELEVATION AS THE TOE OF THE UPPER DAM.



2-3" OF THE WOODEN STAKE SHOULD BE PRESENT ABOVE THE WATTLE.



USE EQUIPMENT TO COMPACT EARTHEN BERM BY ROLLING OVER BERM TO MINIMIZE SPREAD.



www.e2rc.com | 505.867.4040




**RMD CONSTRUCTION, LLC**  
**VOLCANO RV STORAGE**  
**BMP DETAILS**

SHEET:

# 5





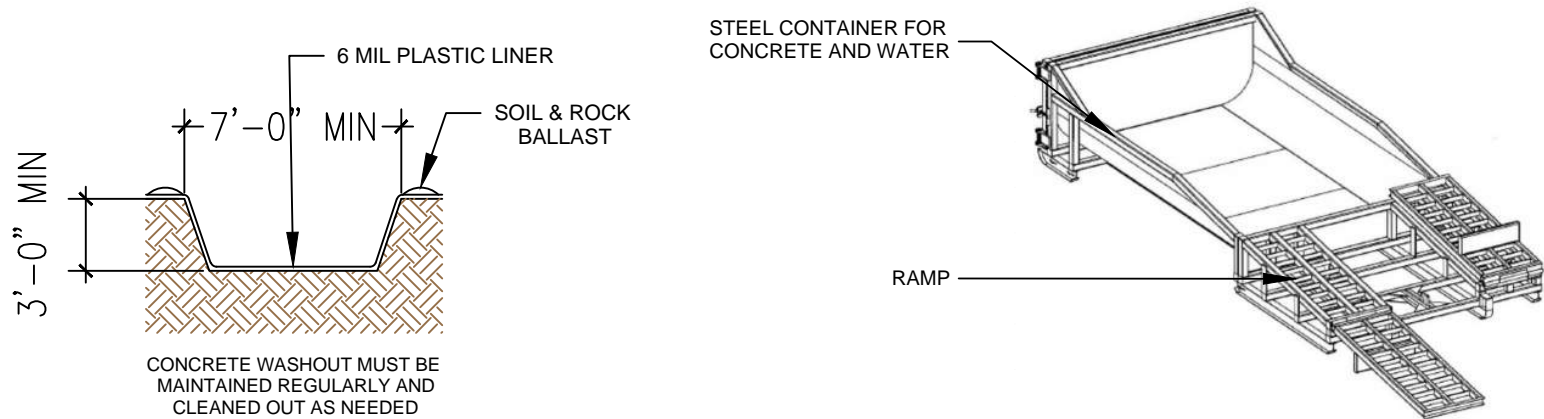

## CONCRETE WASHOUT


NTS

LOCATE WASHOUT AT LEAST 50 FT FROM STORMDRAINS, OPEN DITCHES, WATER BODIES OR PROJECT PERIMETER. A SIGN SHOULD BE INSTALLED ADJACENTLY TO THE WASHOUT.

WASH OUT WASTE INTO THE WASHOUT WHERE THE CONCRETE CAN SET, BE BROKEN UP AND DISPOSED OF CORRECTLY.

DO NOT CREATE RUNOFF BY DRAINING WATER TO BERMED AREA OR BY COLLECTING THE WATER WASTE WHEN WASHING CONCRETE TO REMOVE PARTICLES AND EXPOSE THE AGGREGATE.

DO NOT WASH SWEEPINGS FROM EXPOSED AGGREGATE CONCRETE INTO THE STREET, STORMDRAIN SYSTEMS OR OFF THE PROJECT SITE.

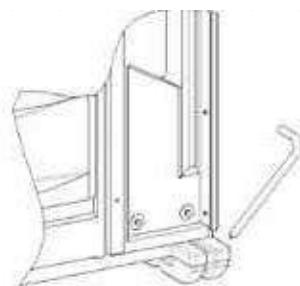


## PORTABLE TOILET STAKING

NTS

PLACE THE PORTABLE TOILET ON LEVEL GROUND. A FLAT PAVED SURFACE IS BEST IF AVAILABLE.


DRIVE THE STAKES OVER THE SKIDS OF THE PORTABLE TOILET, AROUND ALL SIDES.

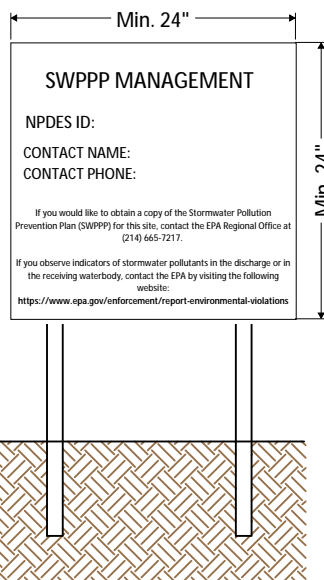

NPDES Permit must be positioned at the most active part of the project where it can be viewed by the public (e.g. project entrance).


## NPDES POSTING BOARD

NTS



## SECTION B-B

NTS

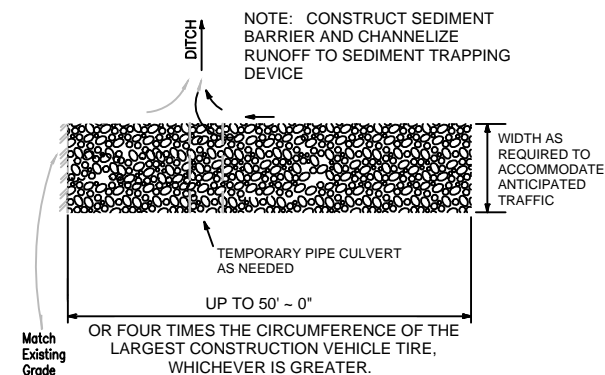

## STABILIZED CONSTRUCTION ENTRANCE

NTS

CONSTRUCT THE ENTRANCE ON A LEVEL SURFACE WHERE AN UNPAVED ROAD MEETS A PAVED ROAD. TYPICALLY AT PROJECTS ACCESS AREA.

GRADE THE ENTRANCE TOWARD THE CONSTRUCTION SITE TO PREVENT RUNOFF.



INSPECT THE ENTRANCE TO KEEP TRASH AND DEBRIS OUT OF THE WAY.

AFTER PRECIPITATION EVENTS, INSPECT THE ENTRANCE FOR ANY REPAIRS THAT MAY BE NEEDED.



SWPPP  
Stormwater  
Erosion Control  
Reclamation  
Seeding

## DRAWING KEY

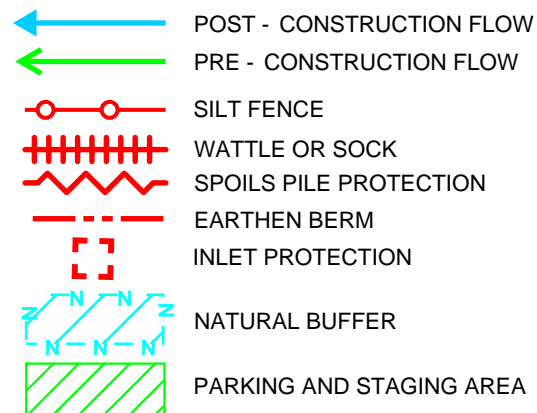

CONCRETE WASHOUT


STABILIZED CONSTRUCTION ENTRANCE

VEGETATIVE STABILIZATION

ENDANGERED/THREATENED SPECIES

CHEMICAL STORAGE

CHECK DAM




TEMP TOILET

LOCATION FOR PUBLIC NOTIFICATION OF NPDES


PROJECT BOUNDARY

DISTURBED AREA  
PROJECT AND DISTURBED BOUNDARY

CULVERT BLANKET  
CUTBACK CURB



PARKING AND STAGING AREA, CHEMICAL STORAGE AND CONCRETE WASHOUT IN APPROXIMATE LOCATION. THESE AREAS ARE TO REMAIN TOGETHER IF MOVED. AREAS CAN BE MOVED AFTER START OF CONSTRUCTION.



DATE

REVISION ITEM

#


RMD CONSTRUCTION, LLC  
VOLCANO RV STORAGE  
BMP DETAILS

DESIGNED BY:  
K. FETTER, P.E.  
DRAWN BY:  
S. FETTER

SHEET:

7


www.e2rc.com | 505.867.4040

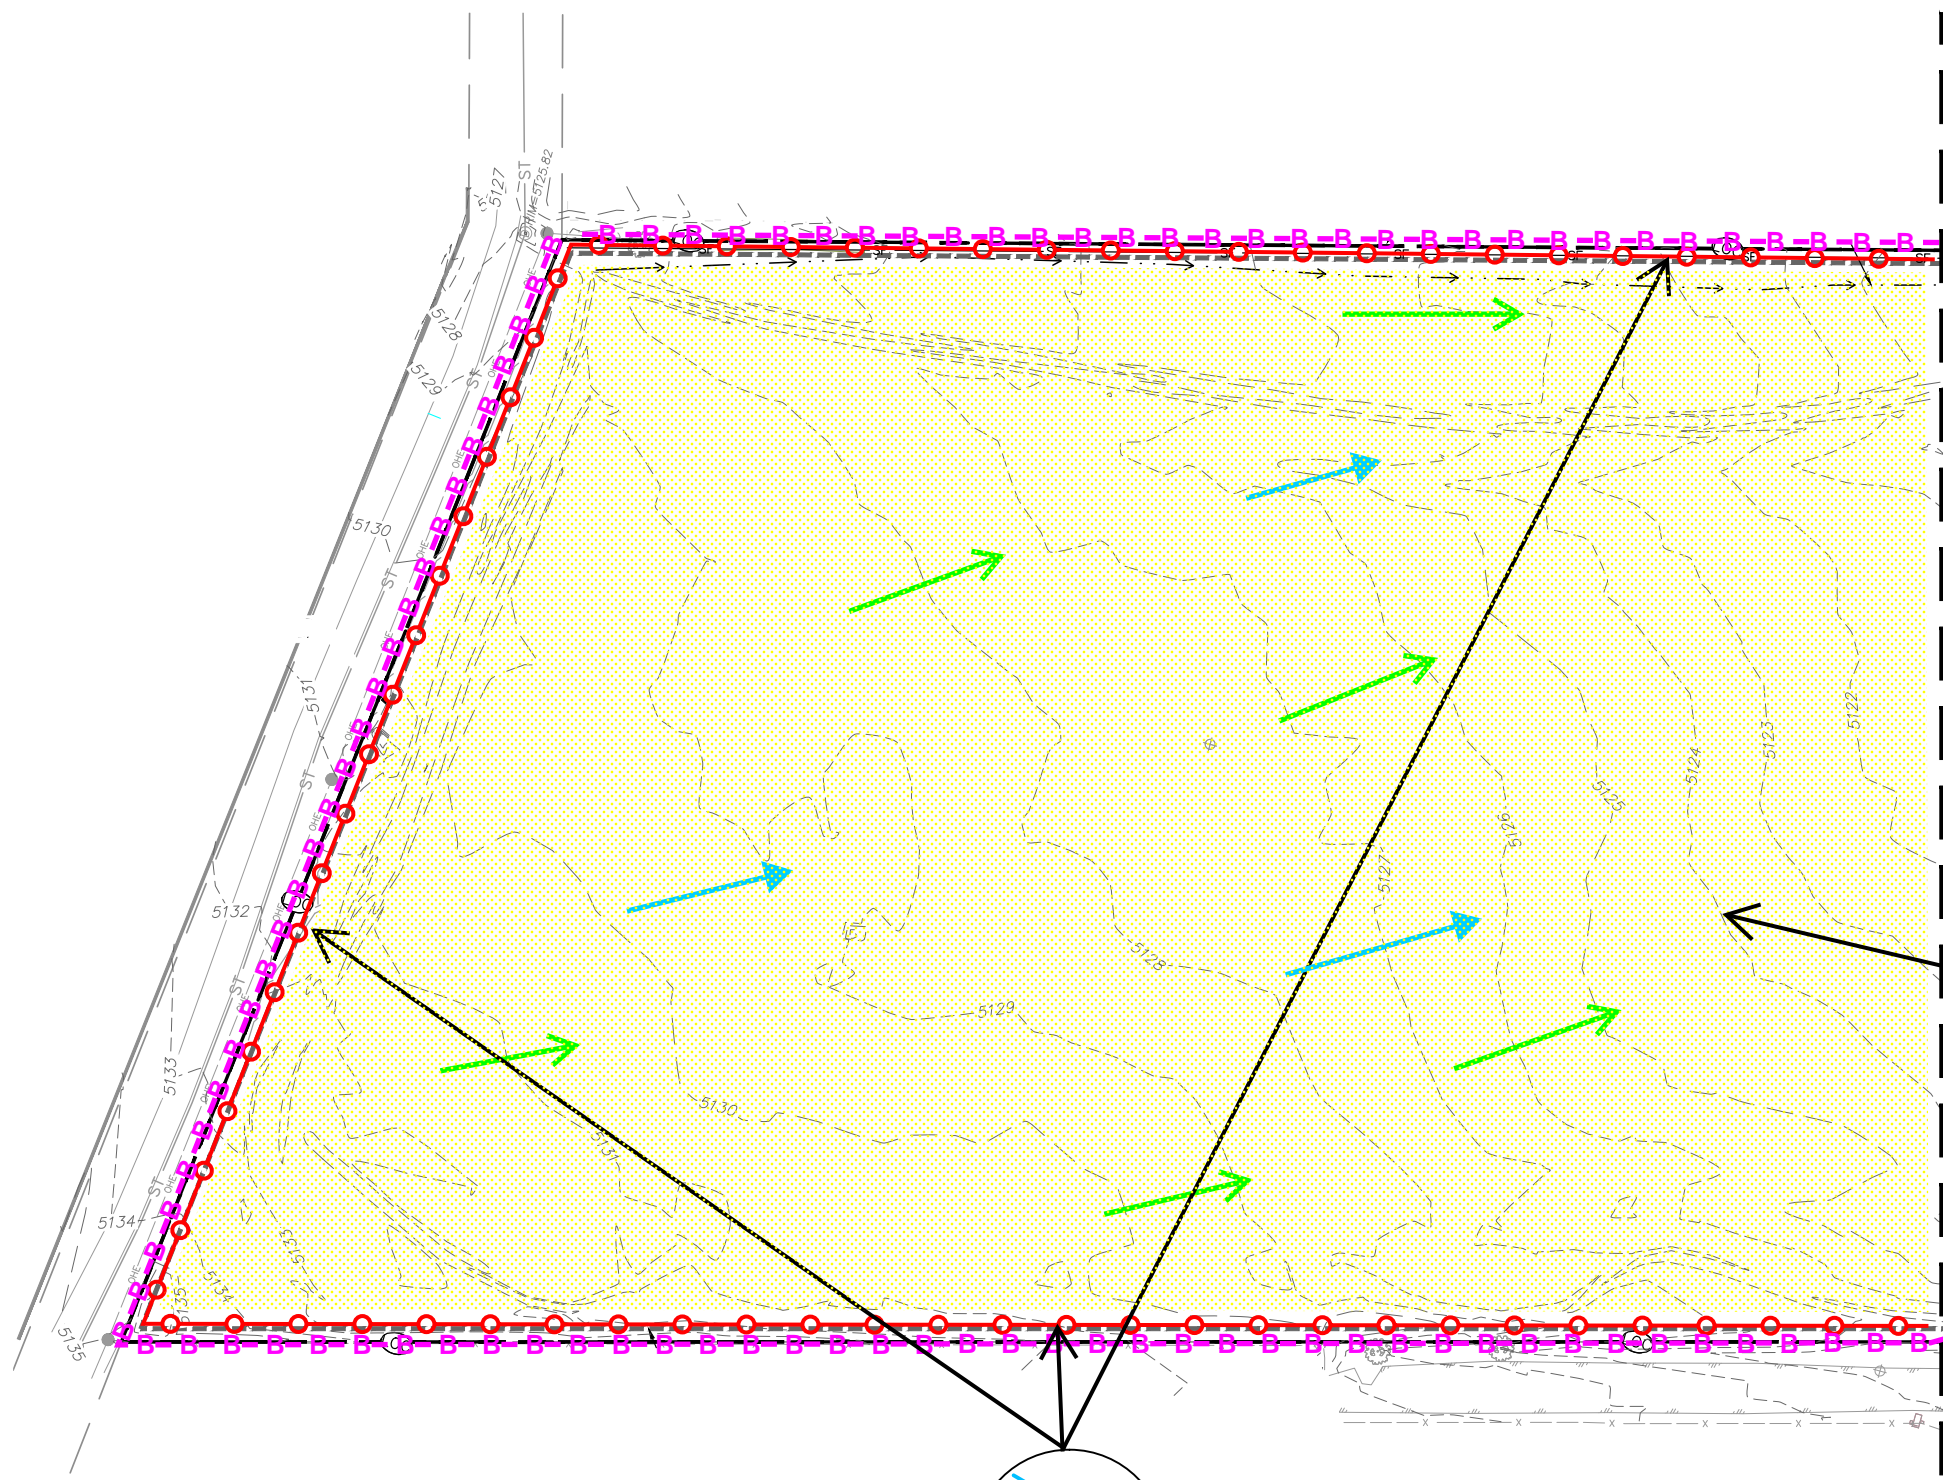

TEMPORARY SOIL STABILIZER SHALL BE APPLIED TO DISTURBED AREAS WHICH WILL REMAIN INACTIVE FOR 14 - DAYS OR MORE.


BMP DETAILS AND MANUFACTUER INFORMATION IS INCLUDED IN THE SWPPP NARRATIVE.

MATCHLINE - SEE SHEET 9




SOIL STABILIZER

IMPLEMENTATION	
BMP INSTALL	BMP REMOVE



SILT FENCE

IMPLEMENTATION	
BMP INSTALL	BMP REMOVE



- SWPPP
- Stormwater
- Erosion Control
- Reclamation
- Seeding



DATE	REVISION ITEM	#

RMD CONSTRUCTION, LLC  
VOLCANO RV STORAGE  
TESCP


DESIGNED BY:  
K. FETTER, P.E.  
DRAWN BY:  
S. FETTER

SHEET:  
**8**







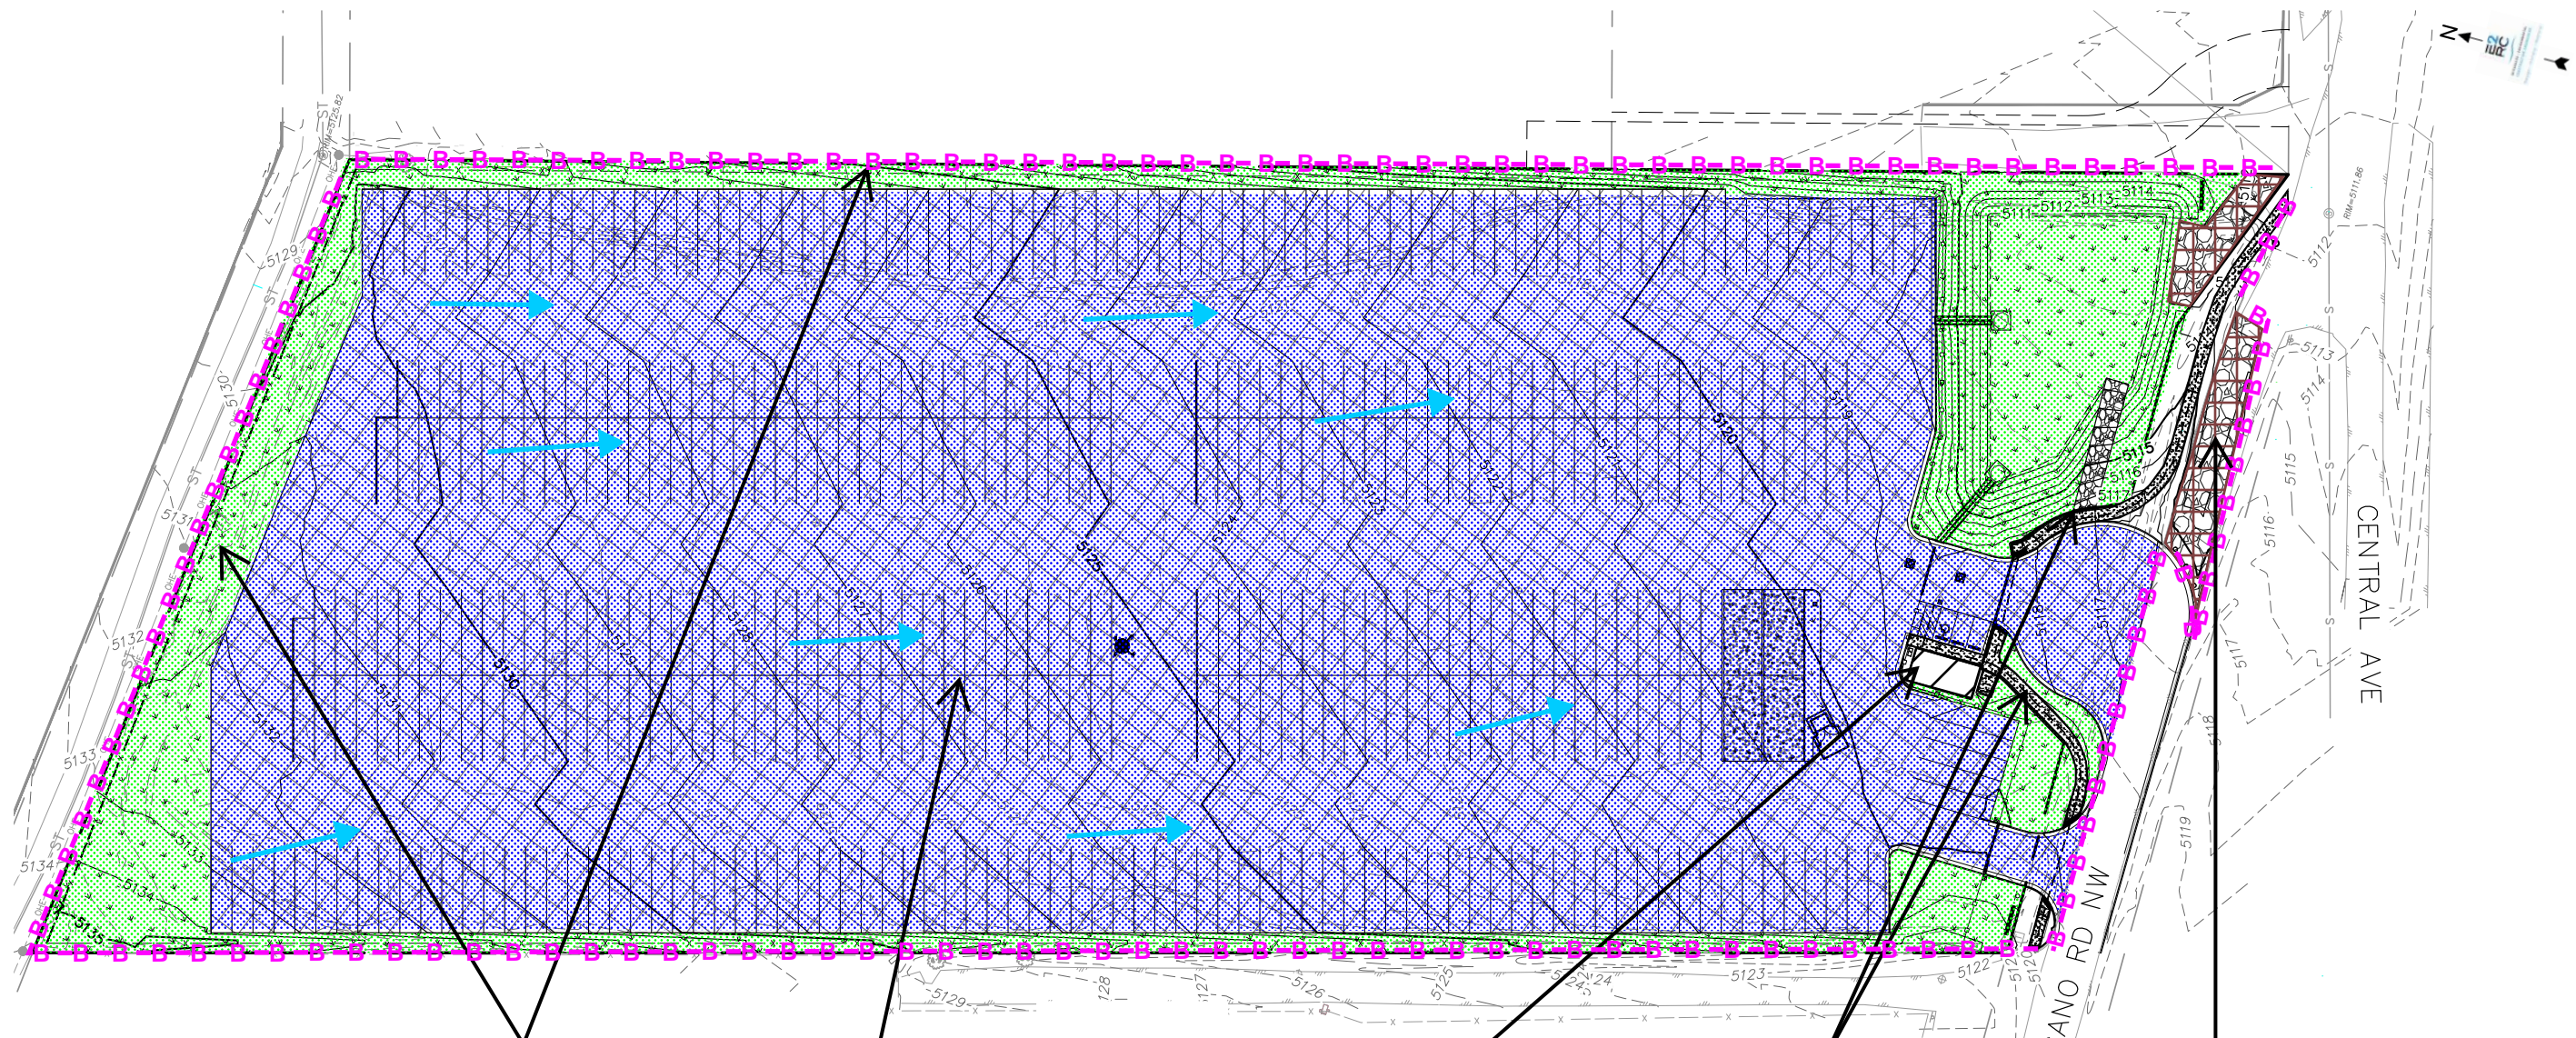

LANDSCAPING - SEE  
APPROVED LANDSCAPING  
PLAN

FINAL STABILIZATION

ASPHALT PAVING

FINAL STABILIZATION

VERTICAL STRUCTURE


FINAL STABILIZATION

CONCRETE CURB, GUTTER,  
SIDEWALK

FINAL STABILIZATION

RIPRAP

FINAL STABILIZATION



SWPPP  
Stormwater  
Erosion Control  
Reclamation  
Seeding

www.e2rc.com | 505.867.4040



REVISION ITEM				DATE
#				

RMD CONSTRUCTION, LLC  
VOLCANO RV STORAGE  
FINAL STABILIZATION

DESIGNED BY:  
K. FETTER, P.E.  
DRAWN BY:  
S. FETTER

SHEET:  
**10**
