### Mercado El Milagro 10,000 Central Avenue SW

# TEMPORARY EROSION AND SEDIMENT CONTROL PLAN



GPS COORDINATES: 35.071107 -106.743300



NEW MEXICO

## STORMWATER POLLUTION PREVENTION PLAN INFORMATION

## PERMIT NUMBER: NMR10055I, and NMR10056E

COVERED UNDER COLORADO PERMIT COR101000 NMR101000 INDIAN COUNTRY WITHIN THE STATE OF NEW MEXICO, EXCEPT PERMIT AZR101000 AND UTE MOUNTAIN RESERVATION LANDS THAT ARE NAVAJO RESERVATION LANDS THAT ARE COVERED UNDER ARIZONA NMR100000 STATE OF NEW MEXICO, EXCEPT INDIAN COUNTRY

OPERATOR NAME: Wilger Enterprises

OPERATOR POINT OF CONTACT. John Wilger

NOI PREPARED BY: Inspections Plus 2

PROJECT/SITE NAME

PROÆCT/SITE ADDRESS: 10,000 Central Ave. SW

Mercado El Milagro

ESTIMATED PROJECT COMPLETION DATE ESTIMATED PROJECT START DATE LONGITUDE LATITUDE -106.743300 35.071107 12/30/2023 01/01/2023

HISTORIC PRESERVATION CRITERIA: CRITERION "A" PREEXISTING DEVELOPMENT ENDANGERED SPECIES CRITERIA: CRITERION "A"; NO CRITICAL HABITATS SWPPP CONTACT INFORMATION: IS RECEIVING WATER IMPAIRED? TIER DESIGNATION RECEIVING WATER? SURFACE WATERS WITHIN 50FT? COMMENCED EARTH DISTURBING ACTIVITIES? WAS THE PREDEVELOPMENT LAND USED FOR GREATER BUILT OR RENOVATED BEFORE JANUARY 1, 1980? TYPE OF CONSTRUCTION ESTIMATED AREA TO BE DISTURBED WHAT ARE THE IMPAIRMENTS, IF ANY? DISCHARGE TO MS4? MS4 NAME? AGRICULTURE? DEMOLITION OF ANY STRUCTURES, 10,000 SQ FT OF John Wilder, 505-345-2854 jwilger@wilger.com Dissolved Oxygen, E. Coli Mercury, Temp Ö COMMERCIAL BUILDING Rio Grande NO NO NO Ö

### EROSION CONTOL NOTES

ESC Plan Standard Notes (2022-10-10)

1.All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:

c.The City Of Albuquerque Construction BMP Manual b.The EPA's 2017 Construction General Permit (CGP), and a.The City Ordinance § 14-5-2-11, the ESC Ordinance,

required after installation of the BMPs and prior to beginning construction. berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is the Phasing Plan. Construction of earthen BMP's such as sediment traps, sediment basins, and diversion 2.All BMP's must be installed prior to beginning any earth moving activities except as specified hereon ir

direct the construction activities on the site and made available upon request. stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to event of 1/4 inch or greater until the site construction has been completed and the site determined as for compliance with the Construction General Permit once every 14 days and after any precipitation 3.Self-inspections - At a minimum a routine compliance self-inspection is required to review the project

activities on the site and made available upon request. 4. Corrective action reports must be kept by the person or entity authorized to direct the construction

problems. Corrective actions for stabilization shall be documented in a stabilization report including stabilized area and any damaged or worn stabilization must be identified in the reports along with weed manufacturer's specifications for application rates, estimated functional longevity, methods of 5.Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal actual rates and dates of stabilization, and the materials and manufacturer's specifications used. application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and

by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections. cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the provides cover for at least three years without active maintenance. Final stabilization must be approved Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and 6.BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the



ESC Stamp	12/2022	MA 10631 CO	PESC
B. Henriksen / J. Tolman	10/10/2022 DATE	ALBUQUERQUE, NM, BERNALILLO COUNTY	Mercado El Milagro
INSPECTIONS PLUS		ALILLO COUNTY CITY, COUNTY, STATE	gro PROJECT TITLE

SEDIMENT TRACK OUT CONTROL



BMP ObjectivesSediment Control



BMP ObjectivesRunoff Control

- Run-on Diversion

SILT FENCE

INLET PROTECTION



- BMP ObjectivesSediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control

MULCH SOCK/STRAW WATTLE





- BMP ObjectivesSediment Control
- Sheet Flow Runoff Control
- Wind Erosion Control



- Sediment Control
  Reduce Runoff Velocity
  Inlet Protection




Mercado El Milagro

PROJECT TITLE

B. Henriksen / J. Tolman ALBUQUERQUE, NM, BERNALILLO COUNTY CITY, COUNTY. STAT 08/23/2022 NSPECTIONS PLUS

3 of 8

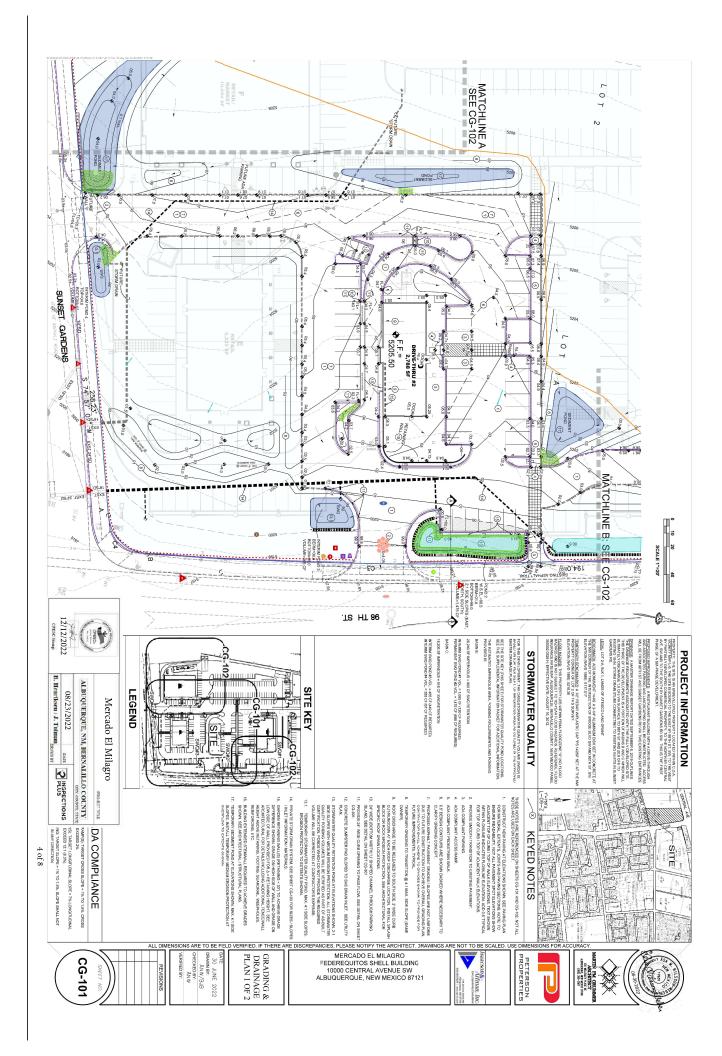

### Mercado El Milagro Inspections Plus, LLC Commercial SWPPP Map 1-Final

### LEGEND





Temporary Sediment Basin (5)




Rip Rap (7)



Retention Basin (2)

- Silt Fence (4)
- ---- Cutback Curb / Sidewalk (22)
- Pre & Post Construction Water Flow (4)
- Property Boundary / Limit of Disturbance (1)
- --- Compacted Earthen Berm (3)
- Limit of Disturbance (1)
- Portable Concrete Washout Bin (1)
- Portable Toilet (1)
- Spill Kit (1)
- ▲ ERTEC Inlet Protection (6)
- Water Truck (1)
- Stabilized Construction Exit (1)
- Materials Storage (1)
- Street Sweeping (1)
- SWPPP Sign (1)
- Stockpiles (1)
- Dumpster (1)



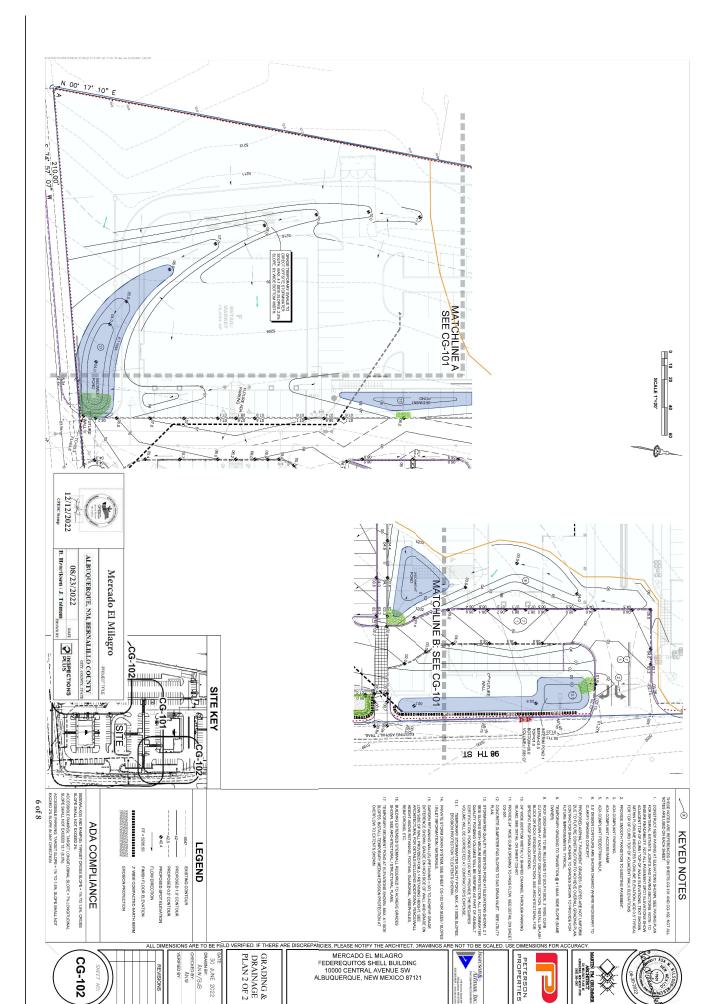

### Mercado El Milagro Inspections Plus, LLC Commercial SWPPP Map 2-Final

### LEGEND





Rip Rap (5)



Temporary Sediment Basin (4)

- Silt Fence (4)
- ---- Cutback Curb / Sidewalk (8)
- --- Compacted Earthen Berm (2)
- Pre & Post Construction Water Flow (3)
- Limit of Disturbance (2)
- Property Boundary / Limit of Disturbance (2)



**ERTEC Inlet Protection (2)** 



### SCHEDULE/SEQUENCING OF CONSTRUCTION: MERCADO EL MILAGRO

- 1. POST PERMITS
- 2. INSTALL REQUIRED BMPs
  - 2.a. PERIMETER CONTROLS (SILT FENCE)
  - 2.b. STABILIZED CONSTRUCTION ENTRANCE
  - 2.c. CONCRETE WASHOUT AREA
- 3. EARTHWORK AND GRADING
- 4. UTILITY INSTALLATION
- **5. PAVEMENT STRUCTURES**
- 6. PAD STRUCTURES
- 7. LANDSCAPING
- 8. PUNCHLIST

Owner:
PPP II, LC
Doug Peterson
Property Owner Contact
505-884-3578
doug@petersonproperties.net

Operator: Wilger Enterprises John Wilger Project Manger 505-345-2854 jwilger@wilger.com

