

ALL DISTURBED AREAS WITHIN PUBLIC RIGHT-OF-WAY AND PUBLIC EASEMENTS WILL BE STABILIZED WITH NATIVE SEED AND AGGREGATE MULCH PER CITY STD. SPEC. 1012.

ANY SEDIMENT OR STOCKPILES LEFT IN ROADWAY MUST BE REMOVED.

ANY STOCKPILES LEFT ON SITE MUST HAVE SEDIMENT CONTROLS PLACED ON DOWNSLOPE SIDES.

FOR WORK ON KIMMICK DR. NW AND ROSA PARKS RD. NW PLACE SEDIMENT CONTROLS ON DOWNSLOPE SIDE OF WORK AREA.

**BMP MAP LEGEND**

- ..... LIMITS OF DISTURBANCE
- (SF)—(SF) PERIMETER BMP (SILT FENCE)
- FILTER SOCK/WATTLE
- INLET PROTECTION
- ← SHEET FLOW
- ← CONCENTRATED FLOW
- PORTABLE TOILETS
- WASTE CONTAINER
- CONCRETE WASHOUT
- STAGING/LAY DOWN YARD



OPERATOR: JUBILEE DEVELOPMENT, LLC

TOTAL DISTURBED AREA: 5.68 ACRES

RECEIVING WATERS: RIO GRANDE RIVER


REFER TO THE ESC BMP DETAILS (ESC-5) FOR INSTALLATION, INSPECTION AND MAINTENANCE REQUIREMENTS.

**\*\*GRADING PLAN BY OTHERS\*\***

**PASEO AND KIMMICK PUBLIC IMPROVEMENTS**

**TEMPORARY EROSION AND SEDIMENT CONTROL PLAN**

Drawn By: M. VALLEJOS, CPESC, CISEC 03/11/2026



ESC-4

ESC PLAN STANDARD NOTES (02/02/26)

- ALL EROSION AND SEDIMENT CONTROL (ESC) WORK ON THESE PLANS, EXCEPT AS OTHERWISE STATED OR PROVIDED HEREON, SHALL BE PERMITTED, CONSTRUCTED, INSPECTED, AND MAINTAINED IN ACCORDANCE WITH:
  - THE CITY ORDINANCE § 14-5-6-6, THE ESC ORDINANCE,
  - THE EPA'S 2022 CONSTRUCTION GENERAL PERMIT (CGP),
  - THE CITY OF ALBUQUERQUE CONSTRUCTION BMP MANUAL AND DETAILS.
- ALL BMPS MUST BE INSTALLED BEFORE BEGINNING ANY EARTH-MOVING ACTIVITIES EXCEPT AS SPECIFIED IN THE PHASING PLAN. CONSTRUCTION OF EARTHEN BMPS SUCH AS SEDIMENT TRAPS, SEDIMENT BASINS, AND DIVERSION BERMS SHALL BE COMPLETED AND INSPECTED PRIOR TO ANY OTHER CONSTRUCTION OR EARTHWORK. SELF-INSPECTION IS REQUIRED AFTER INSTALLATION OF THE BMPS AND BEFORE CONSTRUCTION BEGINS.
- SELF-INSPECTIONS - IN ACCORDANCE WITH CITY ORDINANCE § 14-5-6-6(C)(1), "AT A MINIMUM, A ROUTINE SELF-INSPECTION IS REQUIRED TO REVIEW THE PROJECT FOR COMPLIANCE WITH THE CONSTRUCTION GENERAL PERMIT ONCE EVERY 14 DAYS AND AFTER ANY PRECIPITATION EVENT OF 1/4 INCH OR GREATER UNTIL THE SITE CONSTRUCTION HAS BEEN COMPLETED AND THE SITE DETERMINED AS STABILIZED BY THE CITY. REPORTS OF THESE INSPECTIONS SHALL BE KEPT BY THE PERSON OR ENTITY AUTHORIZED TO DIRECT THE CONSTRUCTION ACTIVITIES ON THE SITE AND MADE AVAILABLE UPON REQUEST.
- CORRECTIVE ACTION REPORTS MUST BE KEPT BY THE PERSON OR ENTITY AUTHORIZED TO DIRECT THE CONSTRUCTION ACTIVITIES ON THE SITE AND MADE AVAILABLE UPON REQUEST.
- FINAL STABILIZATION AND NOTICE OF TERMINATION (NOT) - IN ACCORDANCE WITH CITY ORDINANCE § 14-5-6-6(C)(2), SELF-INSPECTIONS MUST CONTINUE UNTIL THE SITE IS "DETERMINED AS STABILIZED BY THE CITY." THE PROPERTY OWNER/OPERATOR IS RESPONSIBLE FOR DETERMINING WHEN THE "CONDITIONS FOR TERMINATING CGP COVERAGE" PER CGP PART 8.2 ARE SATISFIED AND THEN FOR FILING THEIR NOTICE OF TERMINATION (NOT) WITH THE EPA. EACH OPERATOR MAY TERMINATE CGP COVERAGE ONLY IF ONE OR MORE OF THE CONDITIONS IN PART 8.2.1, 8.2.2, OR 8.2.3 HAS OCCURRED. AFTER FILING THE NOT WITH THE EPA, THE PROPERTY OWNER IS RESPONSIBLE FOR REQUESTING A DETERMINATION OF STABILIZATION FROM THE CITY.
- WHEN WORKING IN THE PUBLIC RIGHT-OF-WAY (E.G., SIDEWALK, DRIVE PADS, UTILITIES, ETC.), PREVENT DIRT FROM ENTERING THE STREET. IF DIRT IS ON THE STREET, IT SHOULD BE SWEEP DAILY AND BEFORE A RAIN OR CONTRACTOR-INDUCED WATER EVENT (E.G., CURB CUT OR WATER TEST).
- WHEN INSTALLING UTILITIES BEHIND THE CURB, THE EXCAVATED DIRT SHOULD NOT BE PLACED IN THE STREET.
- WHEN CUTTING THE STREET FOR UTILITIES, THE DIRT SHALL BE PLACED ON THE UPHILL SIDE OF THE STREET CUT, AND THE AREA SWEEP AFTER THE WORK IS COMPLETE. A COMPOST FILTER SOCK MAY BE PLACED AT THE TOE OF THE EXCAVATED DIRT PILE IF SITE CONSTRAINTS DO NOT ALLOW PLACING THE EXCAVATED DIRT ON THE UPHILL SIDE OF THE STREET CUT.


- STORMWATER CONTROLS MUST BE DESIGNED IN ACCORDANCE WITH GOOD ENGINEERING PRACTICES BY A QUALIFIED NMPE OR CPESC ACCORDING TO CGP 9.6.1.C. THE CERTIFICATION OF THE PROFESSIONAL RESPONSIBLE FOR THE DESIGN MUST BE SIGNED AND DATED ON THE EROSION AND SEDIMENT CONTROL (ESC) PLAN MAINTAINED IN THE SWPPP AND AVAILABLE ONSITE. MAJOR CHANGES TO THE ESC PLAN AFTER CITY APPROVAL MUST BE RECERTIFIED BY THE PROFESSIONAL AND SUBMITTED TO THE CITY FOR APPROVAL BEFORE MODIFYING THE STORMWATER CONTROLS. THE OPERATOR(S) MUST IMPLEMENT AND MAINTAIN BMPS IN THE MANNER SPECIFIED ON THE APPROVED ESC PLAN.
  - IF ANY PART OF THE PROPERTY IS SOLD TO A NEW OWNER OR LEASED TO A NEW TENANT BEFORE CONSTRUCTION IS FINISHED, THE NEW OWNER OR TENANT MUST SUBMIT A NEW ESC PLAN AND NOI TO THE CITY FOR APPROVAL 14 DAYS PRIOR TO THE TRANSFER OF PROPERTY RIGHTS, IN ACCORDANCE WITH CITY ORDINANCE § 14-5-6-6(A). IF NEW LAND-DISTURBING ACTIVITIES ARE ADDED, THE PROPERTY OWNER MUST SUBMIT A REVISED ESC PLAN TO THE CITY FOR APPROVAL 14 DAYS BEFORE BEGINNING CONSTRUCTION IN THE NEW AREAS.
  - OFF-SITE CONSTRUCTION SUPPORT ACTIVITIES MUST BE SHOWN ON THE ESC PLAN WITH STORMWATER CONTROLS DESIGNED BY A PROFESSIONAL AND APPROVED BY ALBUQUERQUE'S STORMWATER QUALITY (SWQ) SECTION. THE OFFSITE PROPERTY OWNER'S NOI MUST ALSO BE SUBMITTED TO THE CITY FOR APPROVAL. THE DEVELOPER MUST STABILIZE OFF-SITE PROPERTY DISTURBED BY CONSTRUCTION ACTIVITIES ASSOCIATED WITH HIS DEVELOPMENT USING "NATIVE SEED AND AGGREGATE MULCH PER COA STD 1012" OR AN EQUIVALENT, IN COMPLIANCE WITH THE FINAL STABILIZATION CRITERIA IN CGP 2.2.14.C AND AS APPROVED BY THE OFF-SITE PROPERTY OWNER.
  - FROM MAY 1 THROUGH OCTOBER 31, ANY GRADING WITHIN OR ADJACENT TO A FACILITY THAT CONVEYS A 100-YEAR FLOW RATE OF 50 CFS OR RECEIVES A 100-YEAR 24-HOUR VOLUME OF 2.0 ACRE-FEET OR MORE MUST PROVIDE STORMWATER CONTROL, EROSION CONTROL, AND SAFE PASSAGE OF THE 10-YEAR DESIGN STORM RUNOFF DURING CONSTRUCTION. THE ESC PLAN MUST INCLUDE DESIGN CALCULATIONS AND CONSTRUCTION SPECIFICATIONS WITH AN ENGINEER'S STAMP FOR TEMPORARY FACILITIES THAT ENSURE SAFE, NON-EROSIVE PASSAGE OF THE 10-YEAR STORM TO PREVENT SEDIMENT DISCHARGE INTO THE CITY'S MS4, IN ACCORDANCE WITH CITY ORDINANCE § 14-5-2-12(B)(3). THE ESC PLAN, INCLUDING THIS INFORMATION, MUST BE SUBMITTED TO THE SWQ SECTION OF THE PLANNING DEPARTMENT OF THE CITY OF ALBUQUERQUE FOR APPROVAL AT LEAST 14 DAYS PRIOR TO ANY LAND DISTURBANCE OR CONSTRUCTION ACTIVITIES IN OR NEXT TO THE FACILITY DURING THE RESTRICTED PERIOD. |

COMPOST FILTER SOCK (CFS)

- DESCRIPTION & PURPOSE:**  
A COMPOST FILTER SOCK IS A MESH TUBE FILLED WITH COMPOST STAKES OR CONTOUR TO CREATE TEMPORARY PONDING TO FACILITATE THE DEPOSITION OF SUSPENDED SOLIDS AND FILTER POLLUTANTS FROM SHEET FLOW. THE COMPOST FILTER SOCK IS OFTEN MORE EFFECTIVE AND CAN REPLACE TRADITIONAL EROSION AND SEDIMENT CONTROL PRACTICES, SUCH AS A SILT FENCE OR STRAW BALE BARRIER. COMPOST FILTER SOCKS HAVE MORE SURFACE AREA CONTACT WITH THE UNDERLYING SOIL THAN TYPICAL SEDIMENT CONTROL DEVICES, SO STORMWATER IS LESS LIKELY TO CREATE RILLS UNDER THEM AND/OR CHANNELS CARRYING UNFILTERED SEDIMENT. THE GREATER CONTACT AREA AND WEIGHT OF COMPOST FILTER SOCKS ALSO ALLOW WATER TO POND AND ALLOW SUSPENDED SEDIMENTS TO SETTLE OUT. COMPOST FILTER SOCKS ALSO FILTER HEAVY METALS, POLLUTANTS, AND OIL FROM STORMWATER WHEN SOCKS ARE FILLED WITH ADSORBENT MEDIA.
- CONDITION WHERE PRACTICE APPLIES:** COMPOST FILTER SOCKS CAN BE USED IN MANY CONSTRUCTION SITE APPLICATIONS WHERE EROSION WILL OCCUR IN THE FORM OF SHEET EROSION, AND THERE IS NO CONCENTRATION OF WATER FLOWING TO THE SOCK. IN AREAS WITH STEEP SLOPES AND/OR ROCKY TERRAIN, SOIL CONDITIONS MUST MAINTAIN GOOD CONTINUOUS CONTACT BETWEEN THE SOCK AND THE SOIL THROUGHOUT ITS LENGTH. FOR USE ON IMPERVIOUS SURFACES SUCH AS ROAD PAVEMENT OR PARKING AREAS, PROPER ANCHORAGE MUST BE PROVIDED TO PREVENT SHIFTING OF THE SOCK OR SEPARATION OF THE CONTACT BETWEEN THE SOCK AND THE PAVEMENT. COMPOST FILTER SOCKS ARE UTILIZED BOTH AT THE SITE PERIMETER AND WITHIN THE CONSTRUCTION AREAS. THESE SOCKS MAY BE FILLED AFTER PLACEMENT BY BLOWING COMPOST INTO THE TUBE PNEUMATICALLY, OR FILLED AT A STAGING LOCATION AND MOVED INTO THEIR DESIGNED LOCATION. UPON COMPLETION OF CONSTRUCTION, COMPOST FILTER SOCKS CAN BE CUT OPEN TO SPREAD THE COMPOST AROUND THE SITE AS SOIL AMENDMENT OR MULCH. THEY THEN DISPOSE OF THE MESH SOCK UNLESS IT IS BIODEGRADABLE.
- DESIGN SPECIFICATIONS:**
  - COMPOST FILTER SOCKS WILL BE PLACED ON THE CONTOUR WITH BOTH TERMINAL ENDS OF THE SOCK EXTENDED 8 FEET UPSLOPE AT A 45 DEGREE ANGLE TO PREVENT BYPASS FLOW.
  - DIAMETERS DESIGNED FOR USE SHALL BE 12" - 22" EXCEPT THAT 8" DIAMETER SOCKS MAY BE USED FOR RESIDENTIAL LOTS TO CONTROL AREAS LESS THAN 0.25 ACRES.
  - THE FLAT DIMENSION OF THE SOCK SHALL BE AT LEAST 1.5 TIMES THE NOMINAL DIAMETER.

DIAM. (IN)	SLOPE (%)							
	2	5	10	20	25	33	50	
8	225	200	100	50	20			
12	250	225	125	65	50	40	25	
18	275	250	150	70	55	45	30	
25	350	275	200	130	100	60	35	
32	450	325	275	150	120	75	50	

- CONSTRUCTION SPECIFICATIONS:**
  - THE ADVANTAGE OF COMPOST FILTER SOCKS OVER SIMILAR STORMWATER CONTROLS IS THAT THEY DO NOT REQUIRE TRENCHING. THEREFORE, INSTALLING THEM DOES NOT DISTURB THE SOIL. HOWEVER, TRIM OR REMOVE VEGETATION AND DEBRIS TO ENSURE FULL CONTACT WITH THE GROUND SURFACE.
  - THE COMPOST FILTER SOCK SHOULD BE ANCHORED WITH 2" X 2" HARDWOOD STAKES DRIVEN THROUGH THE MIDDLE OF THE SOCK TO 12" MINIMUM INTO THE GROUND WITH NOT MORE THAN 10" BETWEEN STAKES. ON UNEVEN TERRAIN, EFFECTIVE GROUND CONTACT CAN BE ENHANCED BY THE PLACEMENT OF A FILLET OF COMPOST MEDIA ON THE DISTURBED AREA SIDE OF THE COMPOST.
  - SOCK MATERIALS: THE COMPOST FILTER SOCK IS TYPICALLY MADE OF HIGH-DENSITY POLYETHYLENE (HDPE) OR BIODEGRADABLE PLASTIC FILAMENT MESH TUBES FILLED WITH COMPOST.
  - SOCKS MUST BE FILLED WITH COMPOST MATERIAL CONFORMING TO CITY STANDARD SPECIFICATION 1005.2.4.B, LATEST EDITION, OR APPROVED EQUAL. SOCKS FILLED WITH STRAW OR WOODCHIPS ARE NOT ACCEPTABLE STORMWATER CONTROLS IN ALBUQUERQUE. COMPOST MATERIAL IS SPECIFIED AS FOLLOWS: ORGANIC MATTER SHALL CONSIST OF ORGANIC CARBON SOURCES SUCH AS STRAW, HAY, BARK, SAWDUST, OR WOOD SHAVINGS, AND NITROGEN SOURCES SUCH AS MANURE, BLOOD MEAL, OR CHEMICAL FERTILIZERS. NITROGEN SOURCES MUST BE ADDED BEFORE COMPOSTING. THIS MIXTURE SHALL BE AEROBICALLY COMPOSTED AT TEMPERATURES BETWEEN 120° AND 160° FOR AT LEAST 15 DAYS, WITH AN ADDITIONAL CURING PERIOD OF NO LESS THAN 3 MONTHS. WEED SEEDS MUST BE DESTROYED DURING COMPOSTING. FINISHED COMPOST WILL BE SCREENED TO ENSURE LESS THAN 2% REMAINS ON A 1/2-INCH SCREEN. THE CARBON-TO-NITROGEN RATIO OF ORGANIC MATTER SHALL BE LESS THAN 50 PARTS CARBON TO ONE PART NITROGEN.
  - ALL SPECIFIC CONSTRUCTION DETAILS AND MATERIAL SPECIFICATIONS SHALL APPEAR ON THE EROSION AND SEDIMENT CONTROL (ESC) PLAN WHEN COMPOST FILTER SOCKS ARE INCLUDED IN THE PLAN.

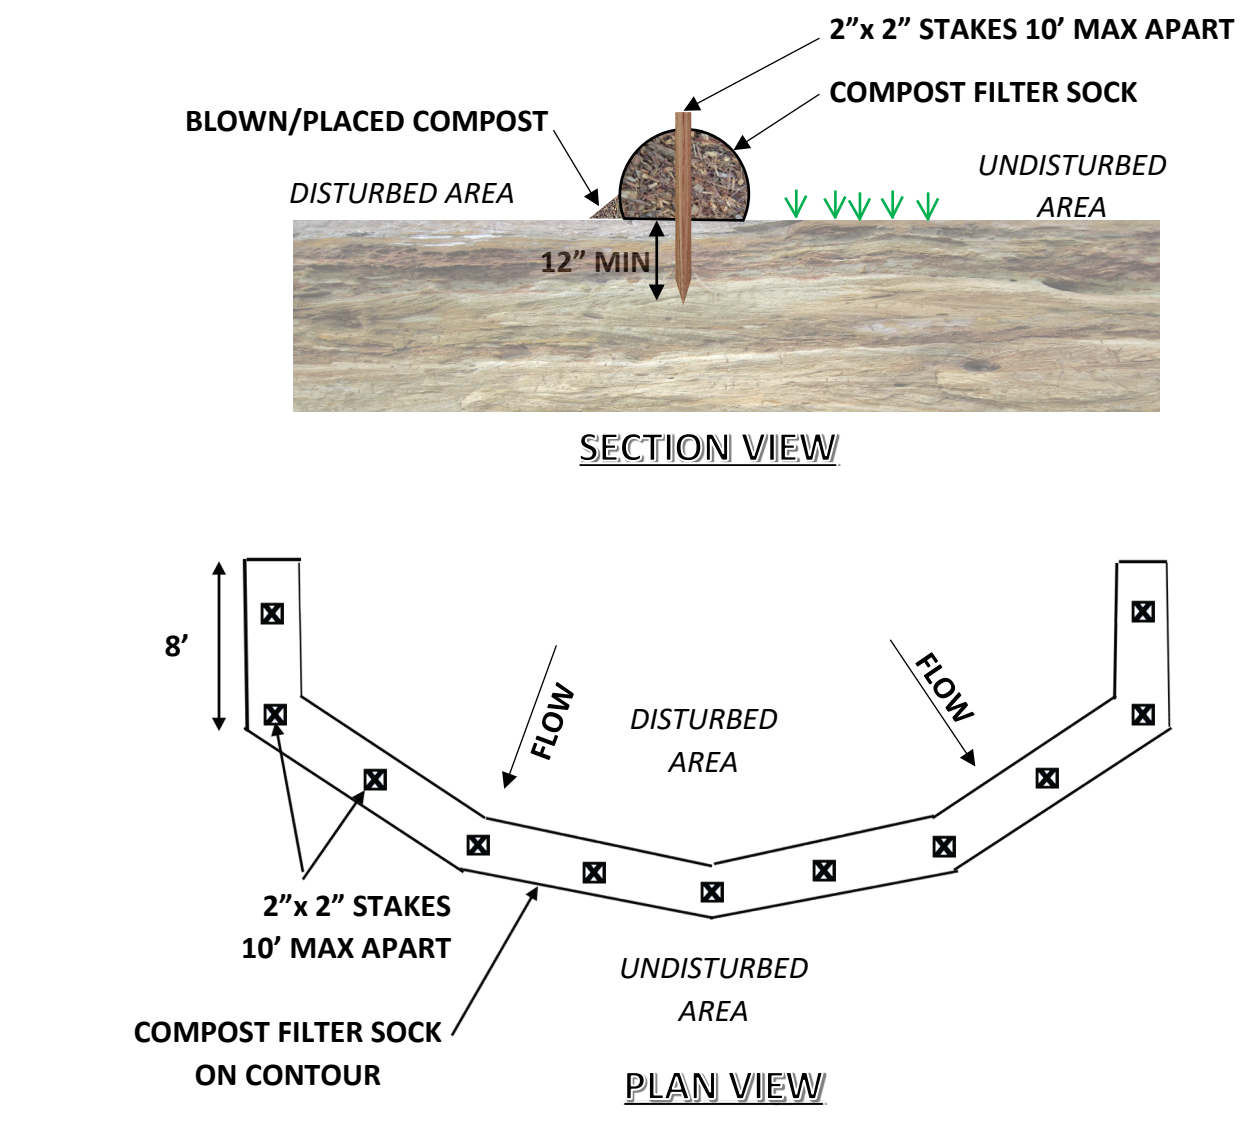

REVISIONS	CITY OF ALBUQUERQUE
Draft 7/29/2025	CONSTRUCTION STORMWATER QUALITY COMPOST FILTER SOCK (CFS)

SHEET 1 OF 1



SILT FENCES

- DESCRIPTION & PURPOSE:**  
STORMWATER SILT FENCES (SWSF) ARE TEMPORARY SEDIMENT BARRIERS MADE OF POROUS FABRIC HELD UP BY WOODEN OR METAL POSTS DRIVEN INTO THE GROUND. THEY ARE INEXPENSIVE AND RELATIVELY EASY TO REMOVE. THE FABRIC PONDS STORMWATER RUNOFF, CAUSING SEDIMENT TO BE RETAINED BY THE SETTLING PROCESSES. IT ALSO KNOCKS DOWN WIND-DRIVEN SAND. IT KEEPS SOIL OUT OF CITY STREETS, THUS PREVENTING CLOGGED STORM DRAINS AND THE DEGRADATION OF AQUATIC HABITATS.
- PRIMARY USE:**  
STORMWATER SILT FENCE (SWSF) IS PRIMARILY FOR STORMWATER CONTROL, BUT DUST CONTROL MAY BE A SECONDARY BENEFIT. SEE SEPARATE DUST CONTROL SILT FENCE (DCSF) FOR SILT FENCE USED PRIMARILY FOR FUGITIVE DUST CONTROL. BOTH TYPES OF SILT FENCE MAY BE SHOWN ON A STORMWATER POLLUTION PREVENTION PLAN (SWPPP) MAP AND/OR AN EROSION AND SEDIMENT CONTROL (ESC) PLAN WITH CLEAR DIFFERENTIATION BETWEEN THE TWO. STORMWATER SILT FENCE IS UNSUITABLE TO CONTROL STORMWATER AT CONCENTRATED DISCHARGE POINTS, LARGE DRAINAGE AREAS, OR WHERE THE SILT FENCE ISN'T ON CONTOUR. WHERE SILT FENCES ARE UNSUITABLE, A SEPARATE STORMWATER CONTROL IS REQUIRED, SUCH AS A BERM OR A POND, IN ADDITION TO DUST CONTROL SILT FENCE. DUST CONTROL SILT FENCES ARE STILL NEEDED TO CONTROL WIND EROSION ON TOP OF OTHER STORMWATER CONTROLS, SUCH AS BERMS AND PONDS, AT THE DOWNSTREAM PERIMETER OF CONSTRUCTION SITES. STORMWATER SILT FENCE IS USED AS A PERIMETER STORMWATER CONTROL WHEN INSTALLED DOWNSLOPE FROM EXPOSED SOIL PER PART 2.2.3 OF THE EPA'S CONSTRUCTION GENERAL PERMIT (CGP), AND AS AN AIR QUALITY CONTROL AROUND THE REST OF THE PERIMETER IN SUPPORT OF CGP PART 2.2.6 AND THE ALBUQUERQUE-BERNALILLO COUNTY AIR QUALITY PROGRAM.
- STORMWATER QUALITY DESIGN SPECIFICATIONS:**
  - SILT FENCE IS FOR SHEET FLOW ONLY. NEVER FOR CONCENTRATED STORMWATER. STORMWATER SILT FENCE ISN'T ALLOWED AS THE STORMWATER CONTROL AT CONCENTRATED DISCHARGE POINTS. OTHER STORMWATER CONTROLS, SUCH AS PONDS AND BERMS, ARE REQUIRED AT DISCHARGE POINTS. ALTERNATIVELY, SILT FENCES MAY BE USED ALONG THE SIDES OF STABILIZED CONCENTRATED FLOW PATHS THROUGH CONSTRUCTION SITES TO REMOVE SEDIMENT FROM THE STORMWATER BEFORE IT ENTERS THE STABILIZED CONCENTRATED FLOW PATH.
  - THE DRAINAGE AREA IS LIMITED TO 25,000 SF PER 100 FT OF FENCE OR COMBINED WITH A SEDIMENT BASIN ON A LARGER SITE.
  - THE MAXIMUM SLOPE DISTANCE ABOVE THE FENCE IS FURTHER LIMITED BY THE SLOPE STEEPNESS, AS SHOWN IN THE TABLE BELOW.

LAND SLOPE (%)	MAXIMUM SLOPE DISTANCE ABOVE FENCE (FT)
2	250
5	180
10	100
20	50
30	30


- SELECT STANDARD STRENGTH OR EXTRA STRENGTH SILT FENCE MATERIAL**
  - STANDARD STRENGTH SILT FENCE** IS APPROPRIATE IF THE SLOPE OF AREA DRAINING TO FENCE IS 4:1 (H:V) OR LESS AND THE DRAINAGE AREA PRODUCES LOW SEDIMENT LOADS. THE EXPECTED LONGEVITY IS GENERALLY LIMITED TO LESS THAN FIVE MONTHS.
  - EXTRA STRENGTH SILT FENCE** IS APPROPRIATE IF THE SLOPE OF AREA DRAINING TO FENCE IS 1:1 (H:V) OR LESS AND AREA DRAINING TO FENCE PRODUCES MODERATE SEDIMENT LOADS. EXPECTED LONGEVITY IS GENERALLY LIMITED TO EIGHT MONTHS. LONGER PERIODS MAY REQUIRE FABRIC REPLACEMENT. HEAVY-DUTY FENCE FABRIC HAS GREATER TENSILE STRENGTH AND PERMEABILITY THAN OTHER FABRIC TYPES. THE POSTS MAY BE SPACED CLOSER TOGETHER THAN OTHER PREMANUFACTURED SILT FENCE TYPES AVAILABLE FROM THE MANUFACTURER.

STORMWATER SILT FENCE MATERIAL	
PHYSICAL PROPERTY	REQUIREMENTS
TENSILE STRENGTH AT 20% (MAXIMUM)	STANDARD STRENGTH: 30 LB/IN (MINIMUM) EXTRA STRENGTH: 50 LB/IN (MINIMUM)
UV RESISTANT	90%
SLURRY FLOW RATE	0.3 GAL/MIN (MINIMUM)

REVISIONS	CITY OF ALBUQUERQUE
Draft 7/29/2025	CONSTRUCTION STORMWATER QUALITY STORMWATER SILT FENCE (SWSF)

SHEET 1 OF 2

- CONSTRUCTION SPECIFICATIONS:**
  - INSTALL SILT FENCE ALONG A LEVEL CONTOUR, WITH THE ENDS TURNED UPHILL 12" VERTICALLY. MIN 1' PACE ENOUGH TO PREVENT FLANKING. EXCEPT FOR THE ENDS, THE DIFFERENCE IN ELEVATION BETWEEN THE HIGHEST AND LOWEST POINT ALONG THE TOP OF THE SILT FENCE SHALL NOT EXCEED ONE-THIRD THE FENCE HEIGHT.
  - CLEAR THE GROUND AT THE SILT FENCE LOCATION TO BARE DIRT. REMOVE VEGETATION, ROCKS, GRAVEL, AND PAVEMENT.
  - INSTALL POSTS SPACED A MAXIMUM OF 10 FEET APART AND DRIVEN SECURELY INTO THE GROUND A MINIMUM OF 18 INCHES. HARDWOOD 1" OR 1 1/2" SECTION MUST HAVE A MINIMUM WEIGHT OF 1.33 POUNDS PER LINEAR FOOT AND SHALL HAVE A MINIMUM LENGTH OF 4' FEET. DOUBLE POSTS ARE REQUIRED AT BOTH ENDS OF EACH PIECE OF SILT FENCE AND AT SPICES.
  - EXCAVATE A TRENCH A MINIMUM OF 6" DEEP BY 6" WIDE ALONG THE UPHILL SIDE OF THE POSTS. ALTERNATIVELY, A 12" DEEP STATIC SLICE IS ALLOWED.
  - OPTIONAL WIRE FENCE REINFORCEMENT IS TYPICALLY 14 GAUGE OR MORE WITH A MAXIMUM MESH SPACING OF 6 INCHES. FASTENED SECURELY TO THE UPSLOPE SIDE OF THE POSTS USING HEAVY-DUTY WIRE STAPLES AT LEAST 1 INCH LONG. THE WIRES, OR HOG RINGS. THE WIRE REINFORCEMENT SHOULD ALSO EXTEND 6" INTO THE TRENCH.
  - THE FILTER FABRIC SHOULD BE STAPLED OR WIRED TO THE FENCE AND POSTS, AND 12 INCHES OR MORE OF THE FABRIC SHOULD EXTEND INTO THE TRENCH. THE WIRE REINFORCEMENT (IF USED) AND FILTER FABRIC SHOULD BE STRETCHED TIGHTLY WHILE ATTACHING THEM.
  - EMBED THE FILTER FABRIC 12" MINIMUM INTO THE TRENCH AND BACKFILL WITH CLEAN EARTH, FREE OF ROCKS AND ORGANIC MATTER, AND COMPACTED WITH OPTIMUM MOISTURE BY WHEEL ROLLING, TAMPING, OR OTHER SIMILAR MEANS. THE FINISHED GRADE SHOULD BE THE SAME ON BOTH SIDES OF THE FENCE, AND THE DEPTH OF EMBEDMENT SHOULD BE MEASURED FROM THE LOWEST GRADE ADJACENT TO THE FENCE. SUBSTITUTIONS INSTEAD OF EMBEDMENT, LIKE WATTLES, ARE NOT ALLOWED.
  - THE HEIGHT OF A STORMWATER SILT FENCE SHALL BE A MINIMUM OF 24 INCHES ABOVE THE HIGHEST GROUND SURFACE ADJACENT TO THE FENCE. ADDITIONAL HEIGHT (30" MIN.) IS REQUIRED TO SATISFY THE ALBUQUERQUE-BERNALILLO COUNTY AIR QUALITY PROGRAM.
  - THE FILTER FABRIC MAY BE ATTACHED TO A CHAIN LINK FENCE CONSTRUCTED IN ACCORDANCE WITH COA STD DWG 2252 INSTEAD OF THE ABOVE-SPECIFIED WIRE FENCE REINFORCEMENT AND POSTS, PROVIDED THAT CHAIN LINK REINFORCEMENT AND FILTER FABRIC ARE EMBEDDED AS SPECIFIED ABOVE.

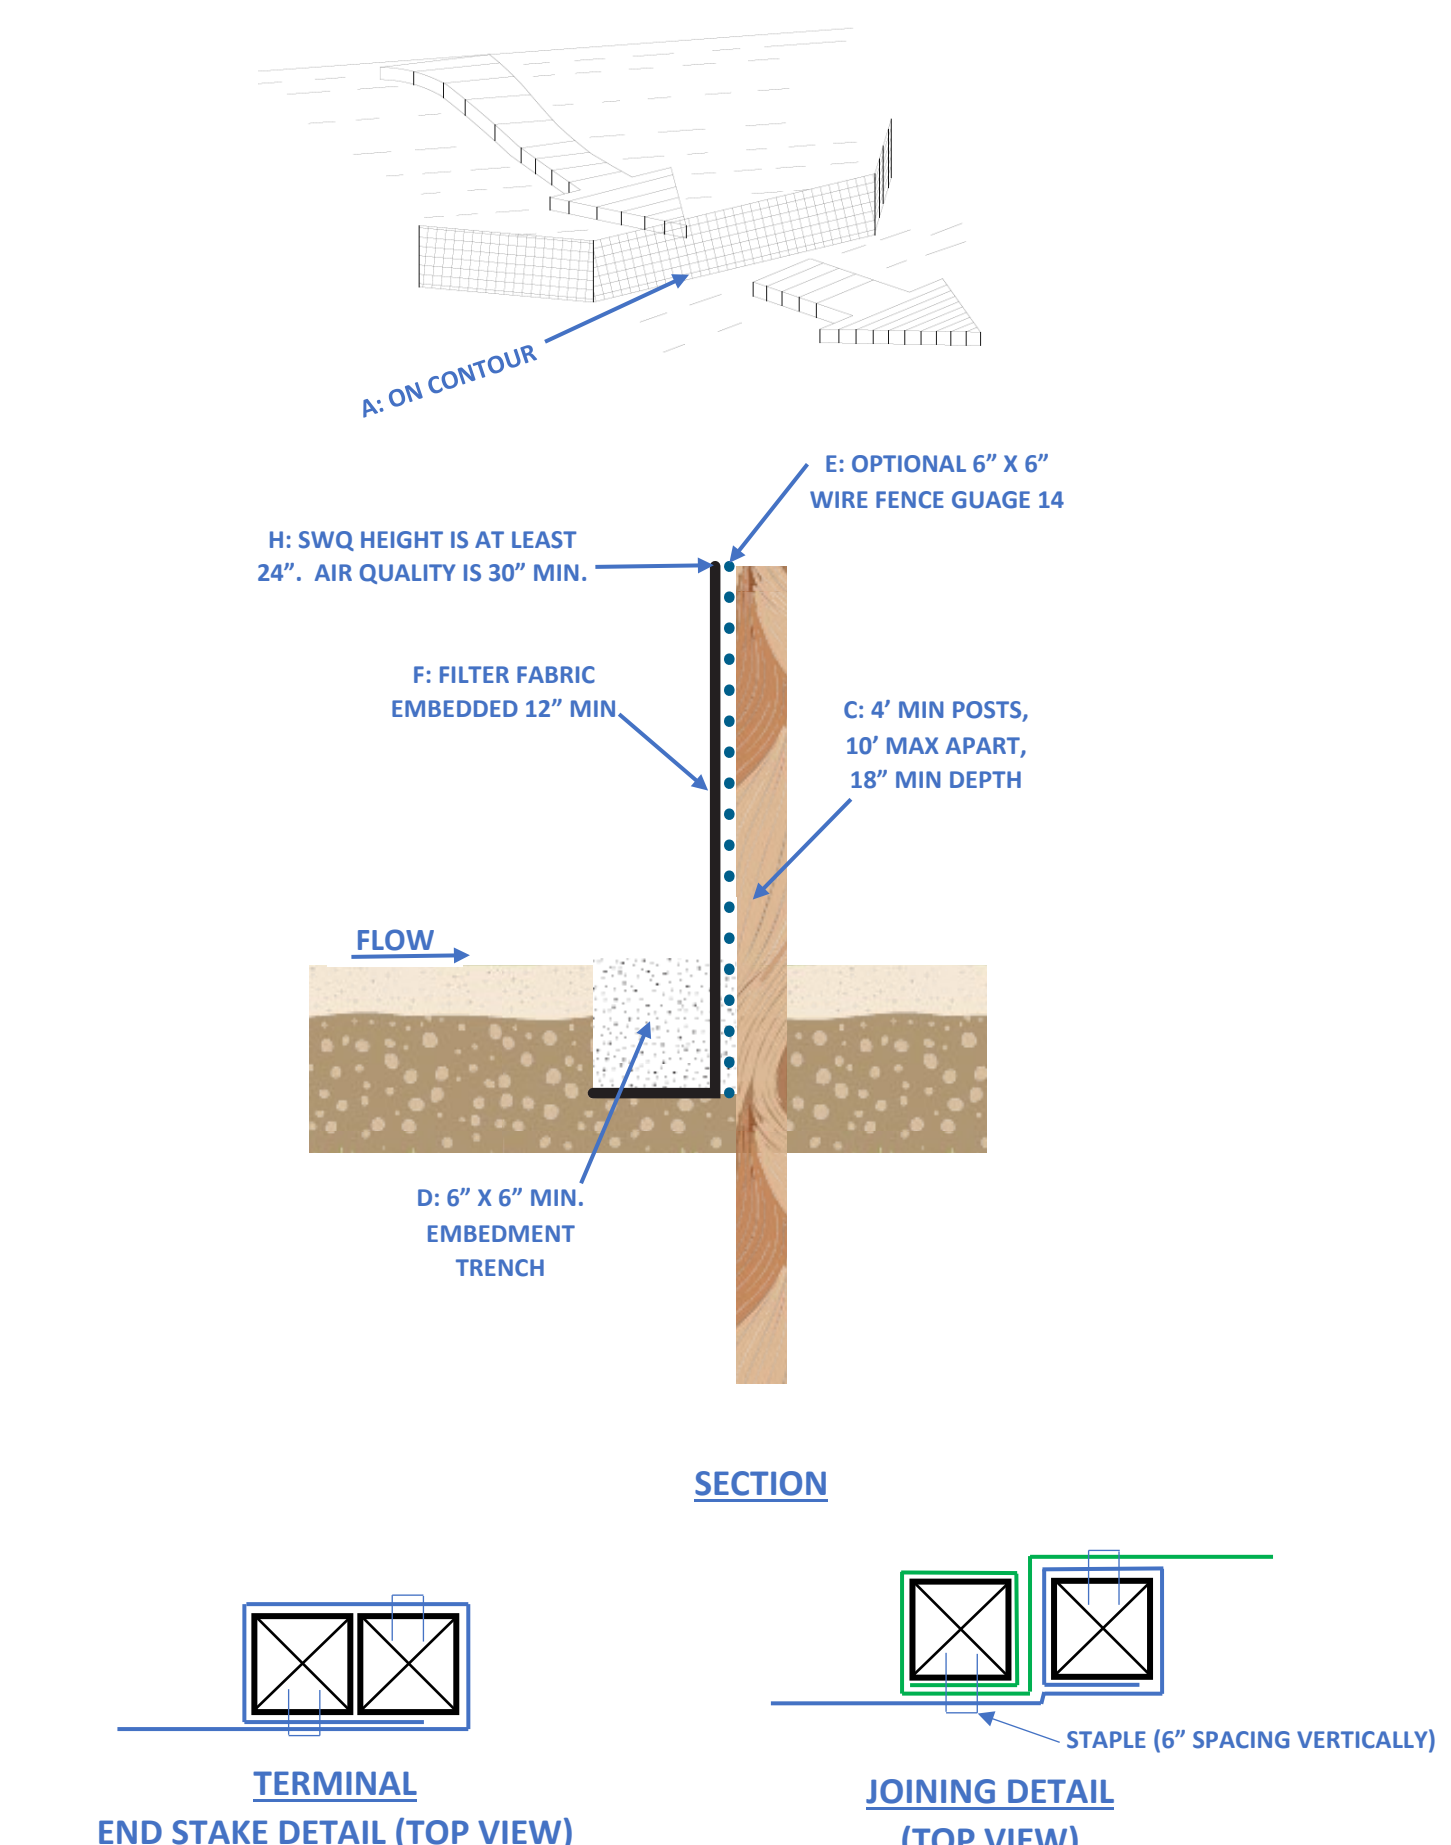

- MAINTENANCE:**
  - SELF-INSPECTION IS REQUIRED BY A CERTIFIED INSPECTOR EVERY 14 DAYS AND IMMEDIATELY AFTER EACH RAINFALL OF 3" OR MORE, AND AT LEAST DAILY DURING PROLONGED RAINFALL.
  - INSPECTION CHECKLIST:
    - DOES THE SILT FENCE FOLLOW A CONTOUR?
    - ARE THE ENDS OF THE SILT FENCE TURNED UPHILL FOR THE LAST 12" VERTICALLY?
    - IS THE HEIGHT OF THE SILT FENCE 24" OR MORE ABOVE GROUND?
    - IS THE COLOR BAND EMBEDDED 6" OR MORE?
    - IS THE SILT FENCE SECURE TO THE WIRE FENCE REINFORCEMENT OR THE STAKES?
    - HAS SEDIMENT ACCUMULATED BEHIND THE FENCE BY MORE THAN 1/2 THE HEIGHT OF THE FENCE? IF YES, THEN CLEAR IT.
    - DOES ANY 100-FOOT OF SILT FENCE SERVE MORE THAN 25,000 SQUARE FEET (ABOUT 1/2 ACRE) OF EXPOSED AREA?
    - IS THERE ANY INDICATION OF WASH AROUND OR UNDER WASH? IF YES, THEN RESET THE FENCE AND DETERMINE IF IT IS OVERLOADED (I.E., ANOTHER FENCE SHOULD BE INSTALLED UPSTREAM).
  - REPAIRS MUST BE COMPLETED WITHIN 24 HOURS OF FINDING THE DEFECT. DEFECTS TYPICALLY INCLUDE LOOSE POSTS OR ATTACHMENTS TO POSTS OR WIRE REINFORCEMENT. SOMETIMES REPAIRS INCLUDE TRENCHING AND EMBEDMENT. CORRECTIVE ACTIONS MUST BE COMPLETED WITHIN 7 DAYS OF DETECTING THE DEFECT.
  - CORRECTIVE ACTIONS INCLUDE RESETTING THE EXISTING FENCE OR REPLACING THE SECTION WHERE THE FILTER FABRIC HAS BEEN TORN OR WORN OUT. HOLES IN THE FILTER FABRIC REQUIRE REMOVAL AND REPLACEMENT WITH DOUBLE POSTS ON BOTH REPLACEMENT ENDS. PATCHES ARE NOT ADEQUATE REPAIRS OF HOLES. SHOULD THE FABRIC ON A SILT FENCE DECOMPOSE OR BECOME INFERIOR BEFORE THE END OF THE EXPECTED USAGE LIFE, AND THE BARRIER IS STILL NECESSARY, THE FABRIC SHALL BE REPLACED.
  - EITHER REMOVE SEDIMENT DEPOSITS WHEN THE DEPOSIT REACHES HALF THE HEIGHT OF THE FENCE OR INSTALL A SECOND SILT FENCE AS DIRECTED BY THE PE/CPESC.
  - THE SILT FENCE SHALL REMAIN IN PLACE UNTIL THE PE/CPESC DIRECTS IT BE REMOVED. UPON REMOVAL, THE CONTRACTOR SHALL REMOVE AND DISPOSE OF ANY EXCESS SEDIMENT ACCUMULATIONS, DRESS THE AREA TO GIVE IT A PLEASANT APPEARANCE, AND VEGETATE ALL BARE AREAS PER CONTRACT REQUIREMENTS.
  - CLOSE ATTENTION SHALL BE PAID TO THE REPAIR OF DAMAGED SILT FENCES RESULTING FROM END RUNS AND UNDERCUTTING.

REVISIONS	CITY OF ALBUQUERQUE
Draft 7/29/2025	CONSTRUCTION STORMWATER QUALITY STORMWATER SILT FENCE (SWSF)

SHEET 2 OF 2

**OPERATOR: JUBILEE DEVELOPMENT, LLC**

**TOTAL DISTURBED AREA: 5.68 ACRES**

**RECEIVING WATERS: RIO GRANDE RIVER**

**REFER TO THE ESC BMP DETAILS (ESC-5) FOR INSTALLATION, INSPECTION AND MAINTENANCE REQUIREMENTS.**

**PASEO AND KIMMICK PUBLIC IMPROVEMENTS  
TEMPORARY EROSION AND SEDIMENT CONTROL PLAN**

Drawn By: **M. VALLEJOS, CPESC, CISEC**      **03/11/2026**

**ESC-5**

**Nature of Construction Activity:**

This project consists of utility installation, roadway and sidewalk improvements along Kimmick and Rosa Parks. Basalt was encountered during trenching operations along Valiente Rd. NW. Basalt removals are being stockpiled in area north of Valiente Rd. NW as shown on ESC Plan. This project covers approximately 5.68 acres of the Paseo – Kimmick Public Improvements project. JP3 Solutions is responsible for all construction activities including earthwork, infrastructure, utilities, flatwork, and asphalt paving. The activities to occur on-site are consistent with utility and roadway improvements.

**Project/Site Name:** Paseo – Kimmick Public Improvements  
**Project Street/Location:** Paseo Del Norte Blvd. NW and Kimmick Dr. NW  
**City:** Albuquerque  
**State:** NM  
**Zip Code:** 87114  
**County:** Bernalillo

**Project Latitude:** 35.17840 **Longitude:** -106.70903

**Determination of Latitude/Longitude:**

USGS topographic map (scale: \_\_\_\_\_ )  
 EPA Web Site  NM OpenEnviroMap  GPS  
 Other (please specify): \_\_\_\_\_

**Function of Construction Activity:**

Residential  Commercial  Industrial  Linear (roadway)  
 Linear (Utility)  Development  Other (specify): \_\_\_\_\_

**Is your project/site located on Federal or Native American Lands** Yes  No   
**Description:** \_\_\_\_\_

Start Date-Finish Date (dates to be marked on site plan by operator)	Construction Activity, BMPs, and location
<b>Initial Phase</b>	Pre-Site Grading 1. Install perimeter BMPs (silt fence, erosion control logs, downstream inlet protection, etc.) 2. Construct VTC. 3. Set up construction trailer, construction barrier, and material storage areas, etc. 4. Install sanitary facilities and dumpster 5. Implement stabilization procedures where work is complete or ceases (per section 2.2.14 of the 2022 EPA CGP)
<b>Interim Phase</b>	Basalt Removals/Roadway Improvements 1. Asphalt and concrete removals 2. Install utilities, infrastructure 3. Asphalt Concrete Replacement 4. Implement stabilization procedures where work is complete or ceases (per section 2.2.14 of the 2022 EPA CGP)
<b>Final Phase</b>	Final Stabilization 1. Implement stabilization procedures where work is complete or ceases (per section 2.2.14 of the 2022 EPA CGP) 2. Prepare final seeding and landscaping 3. Monitor stabilized areas until final stabilization is reached 4. Remove temporary control BMPs and stabilize any areas disturbed by the removal

ROLE	COMPANY	REPRESENTATIVE NAME	PHONE	EMAIL
OPERATOR	JP3 SOLUTIONS	JOEL PIAROWSKI	505-918-8888	<a href="mailto:JOEL@JP3NM.COM">JOEL@JP3NM.COM</a>
OWNER	JUBILEE DEVELOPMENT, LLC	ALEEM HASHAM	501-256-9687	<a href="mailto:ALEEMHASHAM@GMAIL.COM">ALEEMHASHAM@GMAIL.COM</a>
BMP MAINTENANCE	SUPERIOR STORMWATER SERVICES	TIM SLATUNAS	505-353-2558	<a href="mailto:TM@SUPERIORSTORMWATER.COM">TM@SUPERIORSTORMWATER.COM</a>
SWPPP INSPECTIONS	GREEN GLOBE ENVIRONMENTAL, LLC	TIM SLATUNAS	505-353-2558	<a href="mailto:TIM@GREENGLOBENM.COM">TIM@GREENGLOBENM.COM</a>



Rio Grande (Tijeras Arroyo to Alameda Bridge)			AU IR CATEGORY	LOCATION DESCRIPTION	
			5/5C	HUC: 13020203 Rio Grande-Albuquerque	
AU ID	WQS REF	WATER TYPE	SIZE	ASSESSED	MONITORING SCHEDULE
NM-2105_51	20.6.4.105	RIVER	15.6 MILES	2020	2025
USE	ATTAINMENT	CAUSE(S)	FIRST LISTED	TMDL DATE	PARAMETER IR CATEGORY
IRR	Fully Supporting				
LW	Fully Supporting				
MWWAL	Not Supporting	Temperature Dissolved oxygen PCBS - Fish Consumption Advisory Mercury - Fish Consumption Advisory	2010 2008 2010 2020	2023 (est.) 2023 (est.)	5/5A 5/5A 5/5C 5/5C
PC	Not Supporting	E. coli	2020	6/30/2010	4A
PWS	Not Assessed				
WH	Fully Supporting				

**AU Comment:** TMDL for E. coli. Fish Consumption Advisory listings are based on NM's current fish consumption advisories for this water body. Per USEPA guidance, these advisories demonstrate non-attainment of CWA goals stating that all waters should be "fishable." Therefore, the impaired designated use is the associated aquatic life even though human consumption of the fish is the actual concern.

Summary by Map Unit – Bernalillo County and Parts of Sandoval and Valencia Counties, New Mexico (NM600)				
Map unit symbol	Map unit name	Rating	Acres in AOI	Percent of AOI
AmB	Alameda sandy loam, 0 to 5 percent slopes	.24	5.1	100.0%
<b>Totals for Area of Interest</b>			<b>5.1</b>	<b>100.0%</b>

**OPERATOR: JUBILEE DEVELOPMENT, LLC**

**TOTAL DISTURBED AREA: 5.68 ACRES**

**RECEIVING WATERS: RIO GRANDE RIVER**

**REFER TO THE ESC BMP DETAILS (ESC-5) FOR INSTALLATION, INSPECTION AND MAINTENANCE REQUIREMENTS.**

**PASEO AND KIMMICK PUBLIC IMPROVEMENTS  
 TEMPORARY EROSION AND SEDIMENT CONTROL PLAN**

**Drawn By:**  
 M. VALLEJOS, CPESC, CISEC 03/11/2026

**ESC-6**
