



Construction Erosion and Sediment Control (ESC) Permit

Project Title ABCWUA DISTRIBUTION YARD ROADWAY

Project Address 5408 2ND ST. NW, ALBUQUERQUE, NM, 87107D

Property Owner:

Company or Owner Name: ABCWUA

Street: PO BOX 568

City, State, Zip Code: ALBUQUERQUE, NM, 87103

Responsible Person:
Name: LUIS ORDONEZ

Phone Number: 505-289-3216

E-mail: LORDONEZ@ABCWUA.ORG

-The person listed on the permit and/or the onsite representative will be contacted if any issues are observed during an inspection.

At a minimum a routine compliance self-inspection is required to review the project for compliance with the Construction General Permit once every 14 days and after any precipitation event of 1/4 inch or greater until the site construction has been completed and the site determined as stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to direct the construction activities on the site along with a copy of the CGP, the "stormwater team" contact sheet, and the approved ESC Plan. This permit expires the day after the "Project End Date" of the Low Erosivity Waiver (LEW) or one year from the date signed below, whichever happens first.

LEW NMR1004RK Project end 5/31/2022

For City personnel use only:

City Personnel Signature: James D. Hughes Date 3/25/2022



POND SLOPES AND AREA SHOWN TO BE STABILIZED WITH NATIVE GRASS SEED AND AGGREGATE MULCH (PER COA STD. SPEC. 1012) TO SATISFY THE FINAL STABILIZATION CRITERIA PER CGP 2.2.14.c.iii.(a).

EXISTING TRACK-OUT PAD TO REMAIN IN PLACE

POND A:
2' DEEP W/ 10:1 SLOPES
POND VOL.: 8492CF
CONTRIBUTING 100YR 177CF
10DAY VOL.: 5267CF

DISCHARGE POINT/OUTFALL #1

EXCAVATION & GRADING QUANTITIES		
TOTAL CUT (CY)	TOTAL FILL	TOTAL EXPORT
2750	200	2550

NOTE:
CONTRACTOR SHALL STORE EXPORT ON SITE AS DIRECTED BY THE WUA, MAXIMUM HEIGHT OF FILL IS 15FT.

DISCHARGE POINT/OUTFALL #2

SEWER LINE EASEMENT

EXIST FIRE HYDRANT

ASPHALT DRIVEWAY

EXISTING BERM/SWALE TO REMAIN IN PLACE

1 SIDES
114CF
IG 100YR,
177CF

DISCHARGE POINT/OUTFALL #3

- BMP MAP LEGEND**
- LIMITS OF DISTURBANCE
 - PERIMETER BMP (SILT FENCE)
 - EXISTING BERM/SWALE
 - VEHICLE TRACKOUT CONTROL
 - FLOW DIRECTION
 - PORTABLE TOILETS
 - WASTE CONTAINER
 - CONCRETE WASHOUT
 - AREA TO BE STABILIZED



OPERATOR: BRADBURY STAMM CONSTRUCTION

TOTAL SITE AREA: 2.5 ACRES
TOTAL DISTURBED AREA: 2.5 ACRES

RECEIVING WATERS: ON-SITE RETENTION PONDS

REFER TO THE ESC BMP DETAILS (ESC-2) FOR INSTALLATION, INSPECTION AND MAINTENANCE REQUIREMENTS.


****GRADING PLAN BY OTHERS****

ABCWUA DISTRIBUTION YARD ROADWAY

TEMPORARY EROSION AND SEDIMENT CONTROL PLAN

Drawn By:
M. VALLEJOS, CPESC, CISEC

03/23/22

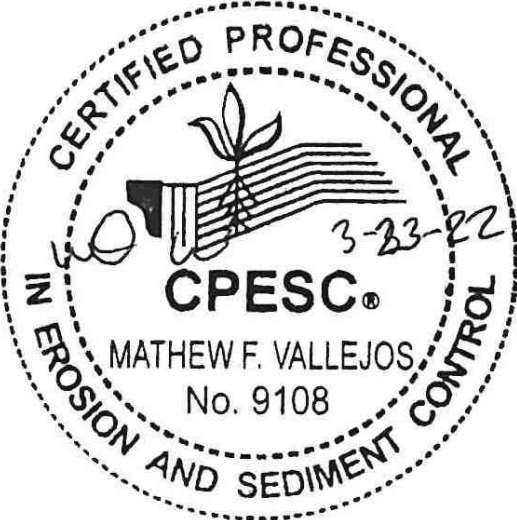

ESC-1

Silt Fence Detail

Non-woven Silt Fence


A silt fence is a temporary sediment barrier consisting of a geotextile attached to supporting posts and trenched into the ground. Intended to retain sediment that has been dislodged by stormwater.

Use silt fence as a perimeter control particularly at lower or down slope edge of a disturbed area. Leave space for maintenance between slope and silt fence or roll. Trench in the silt fence on the uphill side (6 in deep by 6 in wide). Install stakes on the downhill side of the fence. Curve silt fence up-gradient to help it contain runoff.

To maintain remove sediment when it reaches one-third of the height of the fence. Replace the silt fence where it is worn, torn, or otherwise damaged. Retrench or replace any silt fence that is not properly anchored to the ground. If the silt fence cannot be toed in properly due to existing hard surface, place mulch filter sock at base to prevent sediment from leaving site.

8’ max wood stake spacing and 10’ max spacing for steel T-post.

Silt Fence Installation

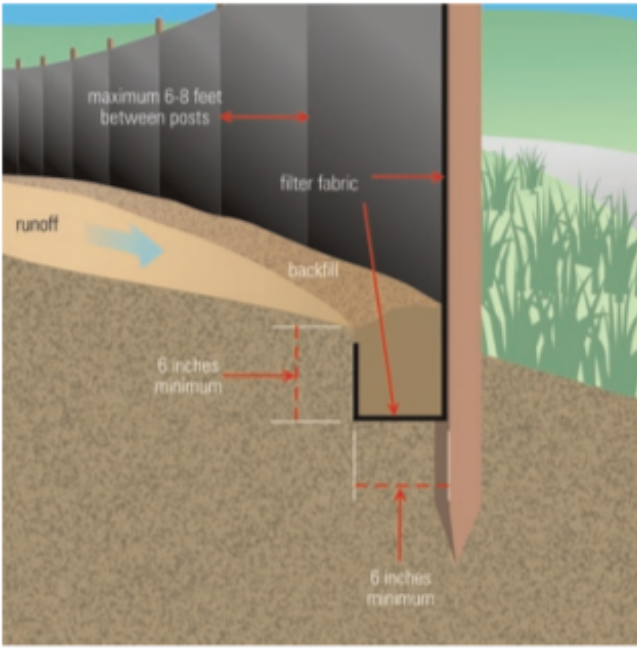


Source: USEPA Guide for Construction Site

TYPICAL CONCRETE WASHOUT-BELOW GRADE



- Install appropriate signage to inform concrete equipment operators of the proper washout location.
- An appropriate stabilized entrance shall be installed where applicable. The length and width of the stabilized entrance may vary based on size and location of the washout.
- Washout facilities must be sized to contain washout water and solids.
- Typical dimensions are 10 feet long by 10 feet wide but may vary upon site limitations.
- Pit shall be delineated with Orange Filter Sock and A-Framed staked.
- The pit shall be lined with 10mil (minimum) polyethylene impermeable liner on the bottom and sides overlapping the top edges completing a leak-proof container.

PORTABLE CONCRETE WASHOUT CONTAINER

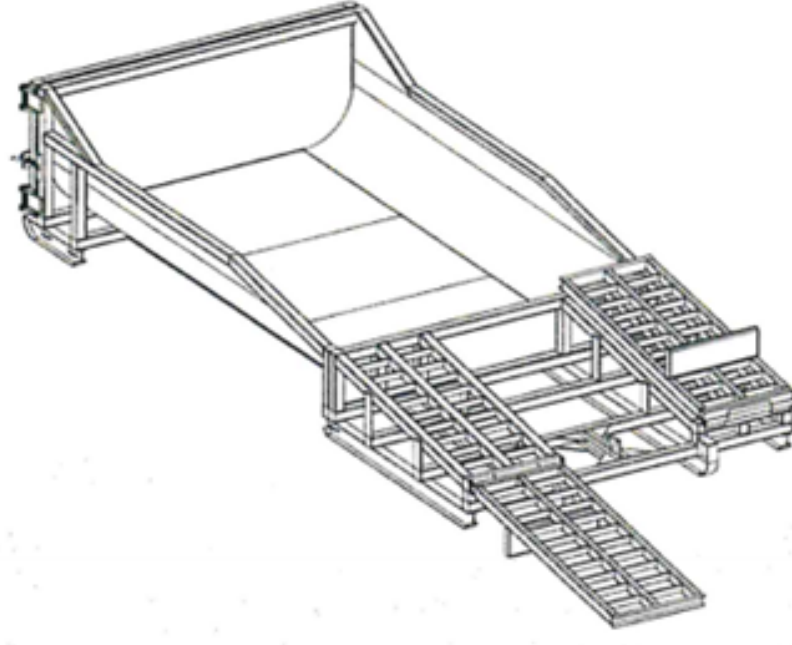

CONCRETE WASHOUT SYSTEMS
PO Box 2604
Carmichael, CA. 95609
Phone: 1.877.292.7468
Fax: 1.916.244.0403
info@concretewashout.com
www.concretewashout.com
Patent Pending

DESCRIPTION
A portable, self-contained and watertight container affixed with ramps that controls, captures and contains caustic concrete wastewater and washout material.

PURPOSE & OBJECTIVE
Allows trade personnel to easily washout concrete trucks, pumps and other equipment associated with cement on site and allows easy off site recycling of the same concrete materials and wastewater.

APPLICATION
Construction projects where concrete, stucco, mortar, grout and cement are used as a construction material or where cementitious wastewater is created.

MAINTENANCE
Inspect and clean out when ¾ full, not allowing the container to overflow.
Inspect wastewater level and request a vacuum if needed.
Inspect subcontractors to ensure that proper housekeeping measures are employed when washing out equipment.

SPECIFICATIONS
The container must be portable and temporary, watertight, equipped with ramps and have a holding capacity to accept washout from approximately 350 yards of poured concrete. A vacuum service must accompany washout container and be used by site superintendent as needed. A rampless container may be used in conjunction with a ramped container or by itself if a concrete pump is not needed. The washwater must be disposed of or treated and recycled in an environmentally safe manner and in accordance with federal, state or local regulatory guidelines.

TARGETED POLLUTANTS
Caustic wastewater (high pH level near 12 units)
Suspended solids
Assorted Metals; Chromium VI, Nickel, Sulfate, Potassium, Magnesium and Calcium Compounds



ESC Plan Standard Notes (2021-03-24)

1. All Erosion and Sediment Control (ESC) work on these plans, except as otherwise stated or provided hereon shall be permitted, constructed, inspected, and maintained in accordance with:
 - a. The City Ordinance § 14-5-2-11, the ESC Ordinance,
 - b. The EPA’s 2017 Construction General Permit (CGP), and
 - c. The City Of Albuquerque Construction BMP Manual.
2. All BMP’s must be installed prior to beginning any earth moving activities except as specified hereon in the Phasing Plan. Construction of earthen BMP’s such as sediment traps, sediment basins, and diversion berms shall be completed and inspected prior to any other construction or earthwork. Self-inspection is required after installation of the BMPs and prior to beginning construction.
3. Self-inspections - At a minimum a routine compliance self-inspection is required to review the project for compliance with the Construction General Permit once every 14 days and after any precipitation event of 1/4 inch or greater until the site construction has been completed and the site determined as stabilized by the city. Reports of these inspections shall be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.
4. Corrective action reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request.
5. Stabilization reports must be kept by the person or entity authorized to direct the construction activities on the site and made available upon request. Reports should include records of weed removal per City Ordinance (§ 9-8-1), sterilization, soil test results and recommendation, materials and manufacturer’s specifications for application rates, estimated functional longevity, methods of application, inspection and maintenance. The reduced self-inspection schedule in CGP 4.4.1 applies to stabilized area and any damaged or worn stabilization must be identified in the reports along with weed problems. Corrective actions for stabilization shall be documented in a stabilization report including actual rates and dates of stabilization, and the materials and manufacturer’s specifications used.
6. BMPs shall be inspected and maintained until all disturbed areas are stabilized in accordance with the Final Stabilization Criteria (CGP 2.2.14.b). Generally, all disturbed areas, other than structures and impervious surfaces, must have uniform perennial vegetation that provides 70 percent or more of the cover provided by native vegetation or seed the disturbed area and provide non-vegetative mulch that provides cover for at least three years without active maintenance. Final stabilization must be approved by the City of Albuquerque prior to removal of BMPs and discontinuation of inspections.

OPERATOR: BRADBURY STAMM
CONSTRUCTION

TOTAL SITE AREA: 2.5 ACRES
TOTAL DISTURBED AREA: 2.5 ACRES

RECEIVING WATERS: ON-SITE RETENTION
PONDS


REFER TO THE ESC BMP DETAILS (ESC-2)
FOR INSTALLATION, INSPECTION AND
MAINTENANCE REQUIREMENTS.

ABCWUA DISTRIBUTION YARD
ROADWAY

TEMPORARY EROSION AND SEDIMENT
CONTROL PLAN

Drawn By:
M. VALLEJOS, CPESC, CISEC

03/23/22

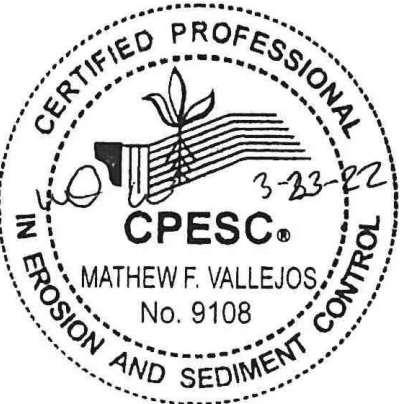
ESC-2

Start Date-Finish Date (dates to be marked on site plan by operator)		Construction Activity, BMPs, and location
Initial Phase		Pre-Site Grading 1. Install perimeter BMPs (silt fence, erosion control logs, downstream inlet protection, etc.) 2. Construct VTC. 3. Set up construction trailer, construction barrier, and material storage areas, etc. 4. Install sanitary facilities and dumpster 5. Implement stabilization procedures where work is complete or ceases (per section 2.2.14 of the 2022 EPA CGP)
Interim Phase		Site Grading/ Building Construction 1. Mass grade site 2. Construct utilities, infrastructure 3. Building, pavement construction 4. Implement stabilization procedures where work is complete or ceases (per section 2.2.14 of the 2022 EPA CGP)
Final Phase		Final Stabilization 1. Implement stabilization procedures where work is complete or ceases (per section 2.2.14 of the 2022 EPA CGP) 2. Prepare final seeding and landscaping 3. Monitor stabilized areas until final stabilization is reached 4. Remove temporary control BMPs and stabilize any areas disturbed by theremoval

Nature of Construction Activity:

This project consists of pave an access and perimeter drive for the sifting yard. This project covers approximately 2.5 acres of the ABCWUA Distribution Yard Roadway project. Bradbury Stamm Construction is responsible for all construction Activities including earthwork, infrastructure, utilities, flatwork, and asphalt paving. The activities to occur on-site are consistent with commercial construction.

Project/Site Name: ABCWUA Distribution Roadway Project
Project Street/Location: 5408 2nd St. NW
City: Albuquerque
State: NM
Zip Code: 87107
County: Bernalillo

Project Latitude: 35.13720 **Longitude:** -106.63440

Determination of Latitude/Longitude:

☐ USGS topographic map (scale:)
☐ EPA Web Site ☒ NM OpenEnviroMap ☐ GPS
☐ Other (please specify):

Function of Construction Activity:

☐ Residential ☒ Commercial ☐ Industrial ☒ Linear (roadway)
☐ Linear (Utility) ☐ Other (specify):

ROLE	COMPANY	REPRESENTATVIE NAME	PHONE	EMAIL
OWNER	ABCWUA	LUIS ORDONEZ	505-289-3216	LORDONEZ@ABCWUA.ORG
OPERATOR	BRADBURY STAMM CONSTRUCTION	DOUG HARNED	505-259-9534	DHARNED@BRADBURYSTAMM.COM
BMP MAINTENANCE	BRADBURY STAMM CONSTRUCTION	DOUG HARNED	505-259-9534	DHARNED@BRADBURYSTAMM.COM
SWPPP INSPECTIONS	GREEN GLOBE ENVIRONMENTAL	TIM SLATUNAS	505-353-2558	TIM@GREENGLOBENM.COM



Tables — K Factor, Whole Soil — Summary By Map Unit				
Summary by Map Unit — Bernalillo County and Parts of Sandoval and Valencia Counties, New Mexico (NM600)				
Summary by Map Unit — Bernalillo County and Parts of Sandoval and Valencia Counties, New Mexico (NM600)				
Map unit symbol	Map unit name	Rating	Acres in AOI	Percent of AOI
Gb	Gila loam, 0 to 1 percent slopes mlra 42-1	.55	2.1	100.0%
Totals for Area of Interest			2.1	100.0%



OPERATOR: BRADBURY STAMM CONSTRUCTION

TOTAL SITE AREA: 2.5 ACRES
TOTAL DISTURBED AREA: 2.5 ACRES

RECEIVING WATERS: ON-SITE RETENTION PONDS


REFER TO THE ESC BMP DETAILS (ESC-2) FOR INSTALLATION, INSPECTION AND MAINTENANCE REQUIREMENTS.

ABCWUA DISTRIBUTION YARD ROADWAY

TEMPORARY EROSION AND SEDIMENT CONTROL PLAN

Drawn By:
M. VALLEJOS, CPESC, CISEC

03/23/22

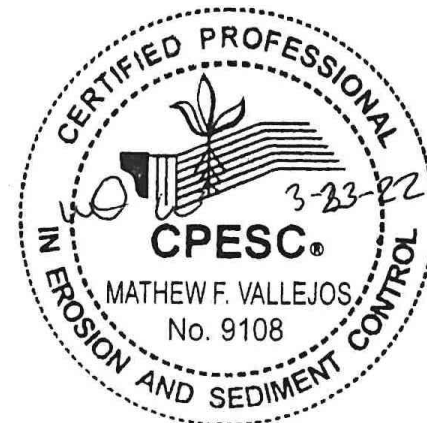

ESC-3

NPDES FORM		UNITED STATES ENVIRONMENTAL PROTECTION AGENCY WASHINGTON, DC 20460 Low Erosivity Waiver Certification	FORM Approved OMB No. 2-4-0004
Waiver Eligibility Information			
NPDES ID: <u>NMR1004KR</u> State/Territory to which your project/site is discharging: <u>NM</u> Is your project/site located on federally recognized Indian country lands? No Are you requesting coverage under this NOI as a "Federal Operator" or a "Federal Facility" as defined in Appendix A (https://www.epa.gov/system/files/documents/2022-01/2022-cgp-final-appendix-a-definitions.pdf)? No Is construction activity at the project site less than five (5) acres in area? Yes ➤ Is your rainfall erosivity factor (R-Factor (https://lew.epa.gov)) less than five (5)? Yes			
Low Erosivity Waiver Information			
Estimated Project Start Date: <u>02/28/2022</u> Estimated Project End Date: <u>05/31/2022</u> Estimated Area to be Disturbed (in Acres): <u>2.5</u> Construction site's R-Factor <u>1.95</u> Rainfall Erosivity factor was calculated using: <u>Online Calculator</u> Are interim non vegetative site stabilization measures used to establish the project completion date for purposes of obtaining this waiver? Yes			
Operator Information			
Operator Name: <u>ALBUQUERQUE BERNALILLO COUNTY WATER UTILITY AUTHORITY</u> Operator Mailing Address: Address Line 1: <u>PO BOX 568</u> Address Line 2: City: <u>ALBUQUERQUE</u> ZIP/Postal Code: <u>87103</u> State: <u>NM</u> County or Similar Division: <u>Bernalillo</u> Operator Point of Contact Information First Name Middle Initial Last Name: <u>DAVID</u> <u>LAUGHLIN</u> Title: <u>OWNER</u> Phone: <u>505-289-3035</u> Ext.: Email: <u>DLAUGHLIN@ABCWUA.ORG</u>			
Project/Site Information			
Project/Site Name: <u>ABCWUA DISTRIBUTION YARD ROADWAY</u> Project/Site Address Address Line 1: <u>5408 2ND ST. NW</u> Address Line 2: City: <u>ALBUQUERQUE</u> ZIP/Postal Code: <u>87107</u> State: <u>NM</u> County or Similar Division: <u>Bernalillo</u> Latitude/Longitude: <u>35.137239°N, 106.634917°W</u> Latitude/Longitude Data Source: <u>Map</u> Horizontal Reference Datum: <u>WGS 84</u> Is your project/site located on federally recognized Indian Country lands? No Is your project/site located on a property of religious or cultural significance to an Indian tribe? <u>No</u>			
Certification Information			
I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I have no personal knowledge that the information submitted is other than true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations. Signing an electronic document on behalf of another person is subject to criminal, civil, administrative, or other lawful action. Certified By: <u>David K. Laughlin</u> Certifier Title: <u>Chief Engineer</u> Certifier Email: <u>dlaughlin@abcwua.org</u> Certified On: <u>03/04/2022 9:34 AM ET</u>			
