


CITY OF ALBUQUERQUE



September 25, 2019

Kent Trauernicht, RA
Akt Architects
P.O. Box 3366
Albuquerque, NM 87190

Re: 4801 Lincoln Rd. NE
4801 Lincoln Rd. NE, 87109
30-Day Temporary Certificate of Occupancy
Transportation Development Final Inspection
Engineer's/Architect's Stamp dated 01-15-19 (F17D024A)
Certification dated 9-19-19

Dear Mr. Trauernicht,

Based upon the information provided in your submittal received 9-20-19, Transportation Development has no objection to a 30-day Temporary Certificate of Occupancy based. This letter serves as a "green tag" from Transportation Development for a 30-day Temporary Certificate of Occupancy to be issued by the Building and Safety Division.

Prior to the issuance of a permanent Certificate of Occupancy, the following items must be addressed:

- Label the compact parking spaces by placing the words "**COMPACT**" on the pavement of each space. (Parking stall with fire hydrant. See attached photo)
- Motorcycle parking spaces shall be designated by its own conspicuously posted upright sign, either free-standing or wall mounted per the IDO. (Each stall requires its own sign)
- Please remove security fences, porta potty, construction equipment and trash container.

Once these corrections are complete, email pictures showing the changes to PLNDRS@cabq.gov, and epgomez@cabq.gov

If you have any questions, please contact me at (505) 924-3981.


Sincerely,


Ernie Gomez,
Plan Checker, Planning Dept.
Development Review Services

EG via: email
C: CO Clerk, File

KEYED NOTES

- EXISTING LANDSCAPE AREA TO REMAIN, PROTECT AGAINST DAMAGE, REVERSE AS SHOWN. FILL PLANTER WITH TOP SOIL TO 1-INCH BELOW ADJOINING CONCRETE CURBING OR WALK WHERE APPLICABLE.
- EXISTING CONCRETE WALK AS SHOWN, PROTECT AGAINST DAMAGE DURING CONSTRUCTION.
- CUT AND REMOVE EXISTING ASPHALT PAVING AND INSTALL LANDSCAPING AND/OR CONCRETE WALK, TYPICAL AS SHOWN.
- CUT AND REMOVE EXISTING LANDSCAPING AND INSTALL ASPHALT PAVING TO MATCH EXISTING, ASSOCIATED IRRIGATION SYSTEM SHALL BE MODIFIED AS REQUIRED.
- EXISTING CONCRETE CURB AND GUTTER TO REMAIN, PROTECT AGAINST DAMAGE DURING CONSTRUCTION.
- EXISTING CURB CUT (SHARED ACCESS) TO REMAIN.
- CUT AND REMOVE EXISTING CURB CUT AND REPLACE WITH STANDARD CURB & GUTTER PER COA STD DWG 2415A. SAWCUT, REMOVE, AND REPLACE EXISTING STREET ASPHALT PAVING PER COA STD DWG 2465. ALL BACKFILL SHALL BE COMPACTED TO 95% MIN. REMOVE AND REPLACE EXIST CONCRETE WALK PER COA STD DWG 2430. SEE DETAIL B/AS-5.0.
- CONC WHEELCHAIR RAMP, PER COABQ STANDARD DETAIL 2441. ALL RAMPS SHALL COMPLY WITH ADA REQUIREMENTS, 1:12 MAX SLOPE AND 1:10 MAX SLOPE AT SIDE FLARES, WITH TRUNCATED DOME MAT FOR THE FIRST 36-INCHES AT BOTTOMS OF RAMPS WITHIN R.O.W. SEE DETAIL E/AS-5.0.
- 4'x8' MOTORCYCLE PARKING (3 SPACES) WITH PAINTED "MOTORCYCLE" 6" H LETTERS AS SHOWN. MINIMUM 12"x18" SIGN DESIGNATING "MOTORCYCLE PARKING", MOUNT ON SIGN STANDARD, BOTTOM OF SIGN NO LESS THAN 48" ABOVE FINISH GRADE, SEE DETAIL J/AS-5.0.
- BICYCLE RACK. SEE DETAIL F/AS-5.0.
- INSTALL CONCRETE WALK PER COA STD DWG 2430. SEE DETAIL H/AS-5.0.
- ADA ACCESSIBLE (MAX 1:12 SLOPE) PEDESTRIAN PATHWAY FROM PUBLIC SIDEWALK TO BUILDING ENTRANCE. PAINT STRIPING AND RAMPS AS SHOWN AND AS REQUIRED, SEE DETAIL.
- REFUSE CONTAINER PAD. SEE DETAIL L/AS-5.0.
- INSTALL PRECAST CONC WHEEL STOPS, INSTALL WITH #6x48" REBAR, TYPICAL AS SHOWN. MAY RELOCATE EXISTING IF IN GOOD CONDITION.
- CONCRETE CURB, TYPICAL AROUND LANDSCAPE AREAS AS SHOWN. SEE DETAIL B1/AS-5.0.
- ACCESSIBLE PARKING SIGN, DESIGNATE VAN PARKING AS SHOWN. SEE DETAIL D/AS-5.0.
- TWO COATS TRAFFIC PAINT, 4-INCH WIDE STRIPING (YELLOW ON CONCRETE, WHITE ON ASPHALT), TYP. AS SHOWN THROUGHOUT TRAFFIC/PARKING AREAS. ALL EXISTING MARKINGS SHALL BE PAINTED OUT AS REQUIRED TO VISUALLY ELIMINATE.
- ACCESSIBLE PARKING SYMBOL PER COABQ STANDARD DETAIL 2426. SEE DETAIL C/AS-5.0. PAINTED "VAN" 6" H LETTERS AS SHOWN AT VAN SPACE.
- TRAFFIC PAINTED "NO PARKING" DESIGNATION. MINIMUM 12" H x 2" W LETTERS. PLACED AS SHOWN.
- EXISTING TELEPHONE PEDESTAL BUILDING SERVICE.
- EXISTING ELECTRICAL SERVICE TRANSFORMER ON ON PAD WITH METER, SEE ELECTRICAL.
- EXISTING FIRE HYDRANT.
- MAIN DISTRIBUTION CABINETS A & B, SEE ELECTRICAL.
- CUT AND REMOVE EXISTING ASPHALT PAVING AS REQUIRED AND INSTALL ACCESSIBLE RAMP WITH SIDE CURBS AS REQUIRED FOR NEW ACCESS FROM EXISTING STREET CONCRETE WALK. DETAIL E/AS-5.0.
- CUT AND REMOVE EXISTING ASPHALT PAVING AND INSTALL NEW LANDSCAPED AREA. ROTO-TILL SOILS AND INSTALL TOP SOIL SUITABLE FOR PLANTING MATERIAL. TOP OF SOIL SHALL BE 1-INCH BELOW TOP OF ADJOINING CONC. SEE LANDSCAPE PLAN.
- LANDSCAPE & IRRIGATION NOTE: IRRIGATION CONTROLS ARE TO BE PLACED INSIDE THE BUILDING AND LOCATED AS DIRECTED BY THE OWNER.
- INSTALL FIRE LINE AND FIRE SPRINKLER RISER, SEE PLAN, SHT A-1.1 FOR LOCATION. FIRE LINE SHALL EXTEND AND TAP INTO STREET MAIN. INSTALL WITH POST INDICATOR VALVE AND FIRE DEPARTMENT CONNECTION AS SHOWN. INSTALL PER CABQ REQUIREMENTS AND WORK ORDERS.
- EXISTING ASPHALT PAVING TO REMAIN, PATCH, REPAIR. ALL ASPHALT SHALL BE SEAL COATED.
- NEW ASPHALT PAVING AS REQUIRED. SEE DETAIL G/AS-5.0. ALL ASPHALT SHALL BE SEAL COATED.
- EXISTING 6.5-FT HIGH CHAINLINK FENCE WITH CONCERTINA TOP, ALL AROUND AS SHOWN, TO REMAIN.
- EXISTING GATE, TO REMAIN. INSTALL KNOX PADLOCK AS REQUIRED BY FIRE MARSHAL.
- INSTALL GATE WITH CLOSURE FENCE, SEE DETAIL.
- CONCRETE PAD/STAIR AT EXTERIOR DOOR, SEE DETAIL O/AS-5.0.
- CONCRETE LANDING/STEPS AT EXTERIOR DOOR, SEE DETAIL 4/A-3.6.
- CONCRETE COMPRESSOR PAD AND ENCLOSURE, SEE DETAIL.
- GAS SERVICE ENTRANCE AND METERS, SEE MECHANICAL.
- POWER POLE WITH LINES ABOVE.
- CMU RETAINING WALL AT PROPERTY LINE AS SHOWN.
- CONCRETE SLAB SLOPED WITH GRADE AT ADJOINING PROPERTY.
- INSTALL GATE AND FENCING. GATE SHALL BE EQUIPPED WITH KNOX PADLOCK PER FIRE MARSHAL'S REQUIREMENT. SEE DETAIL 1/AS-5.1.
- BOLLARDS AS SHOWN. SEE DETAIL 1/AS-5.0.
- PROJECT MONUMENT SIGN. SEE DETAIL N/AS-5.0. EXTEND POWER AS REQUIRED, COORDINATE WITH SIGN COMPANY.
- NO SITE WORK BEYOND GATE.
- 30-FT FLAG POLE WITH UP LIGHT, SEE DETAIL M/AS-5.0.
- CONCRETE STAIR AT DOCK DOOR, SEE DETAIL 2/AS-5.1.
- FIRE DEPARTMENT CONNECTION WITH 6" LINE, PER COA STD DETAILS.
- POST INDICATOR VALVE (6-INCH)
- 3" PVC PIPE UNDER PAVEMENT FOR INSTALLATION OF IRRIGATION LINES AND OR ELECTRICAL. COORDINATE WITH LANDSCAPE AND ELECTRICAL CONTRACTORS.
- NEW FIRE HYDRANT WITH FIRE LINE EASEMENT AS REQUIRED, PER COABQ REQUIREMENTS AND WORK ORDERS. INSTALL WITH 6" CONC RETAINING WALL AND BOLLARDS (3" DIA, CONC FILL) AS REQUIRED TO PROTECT HYDRANT.

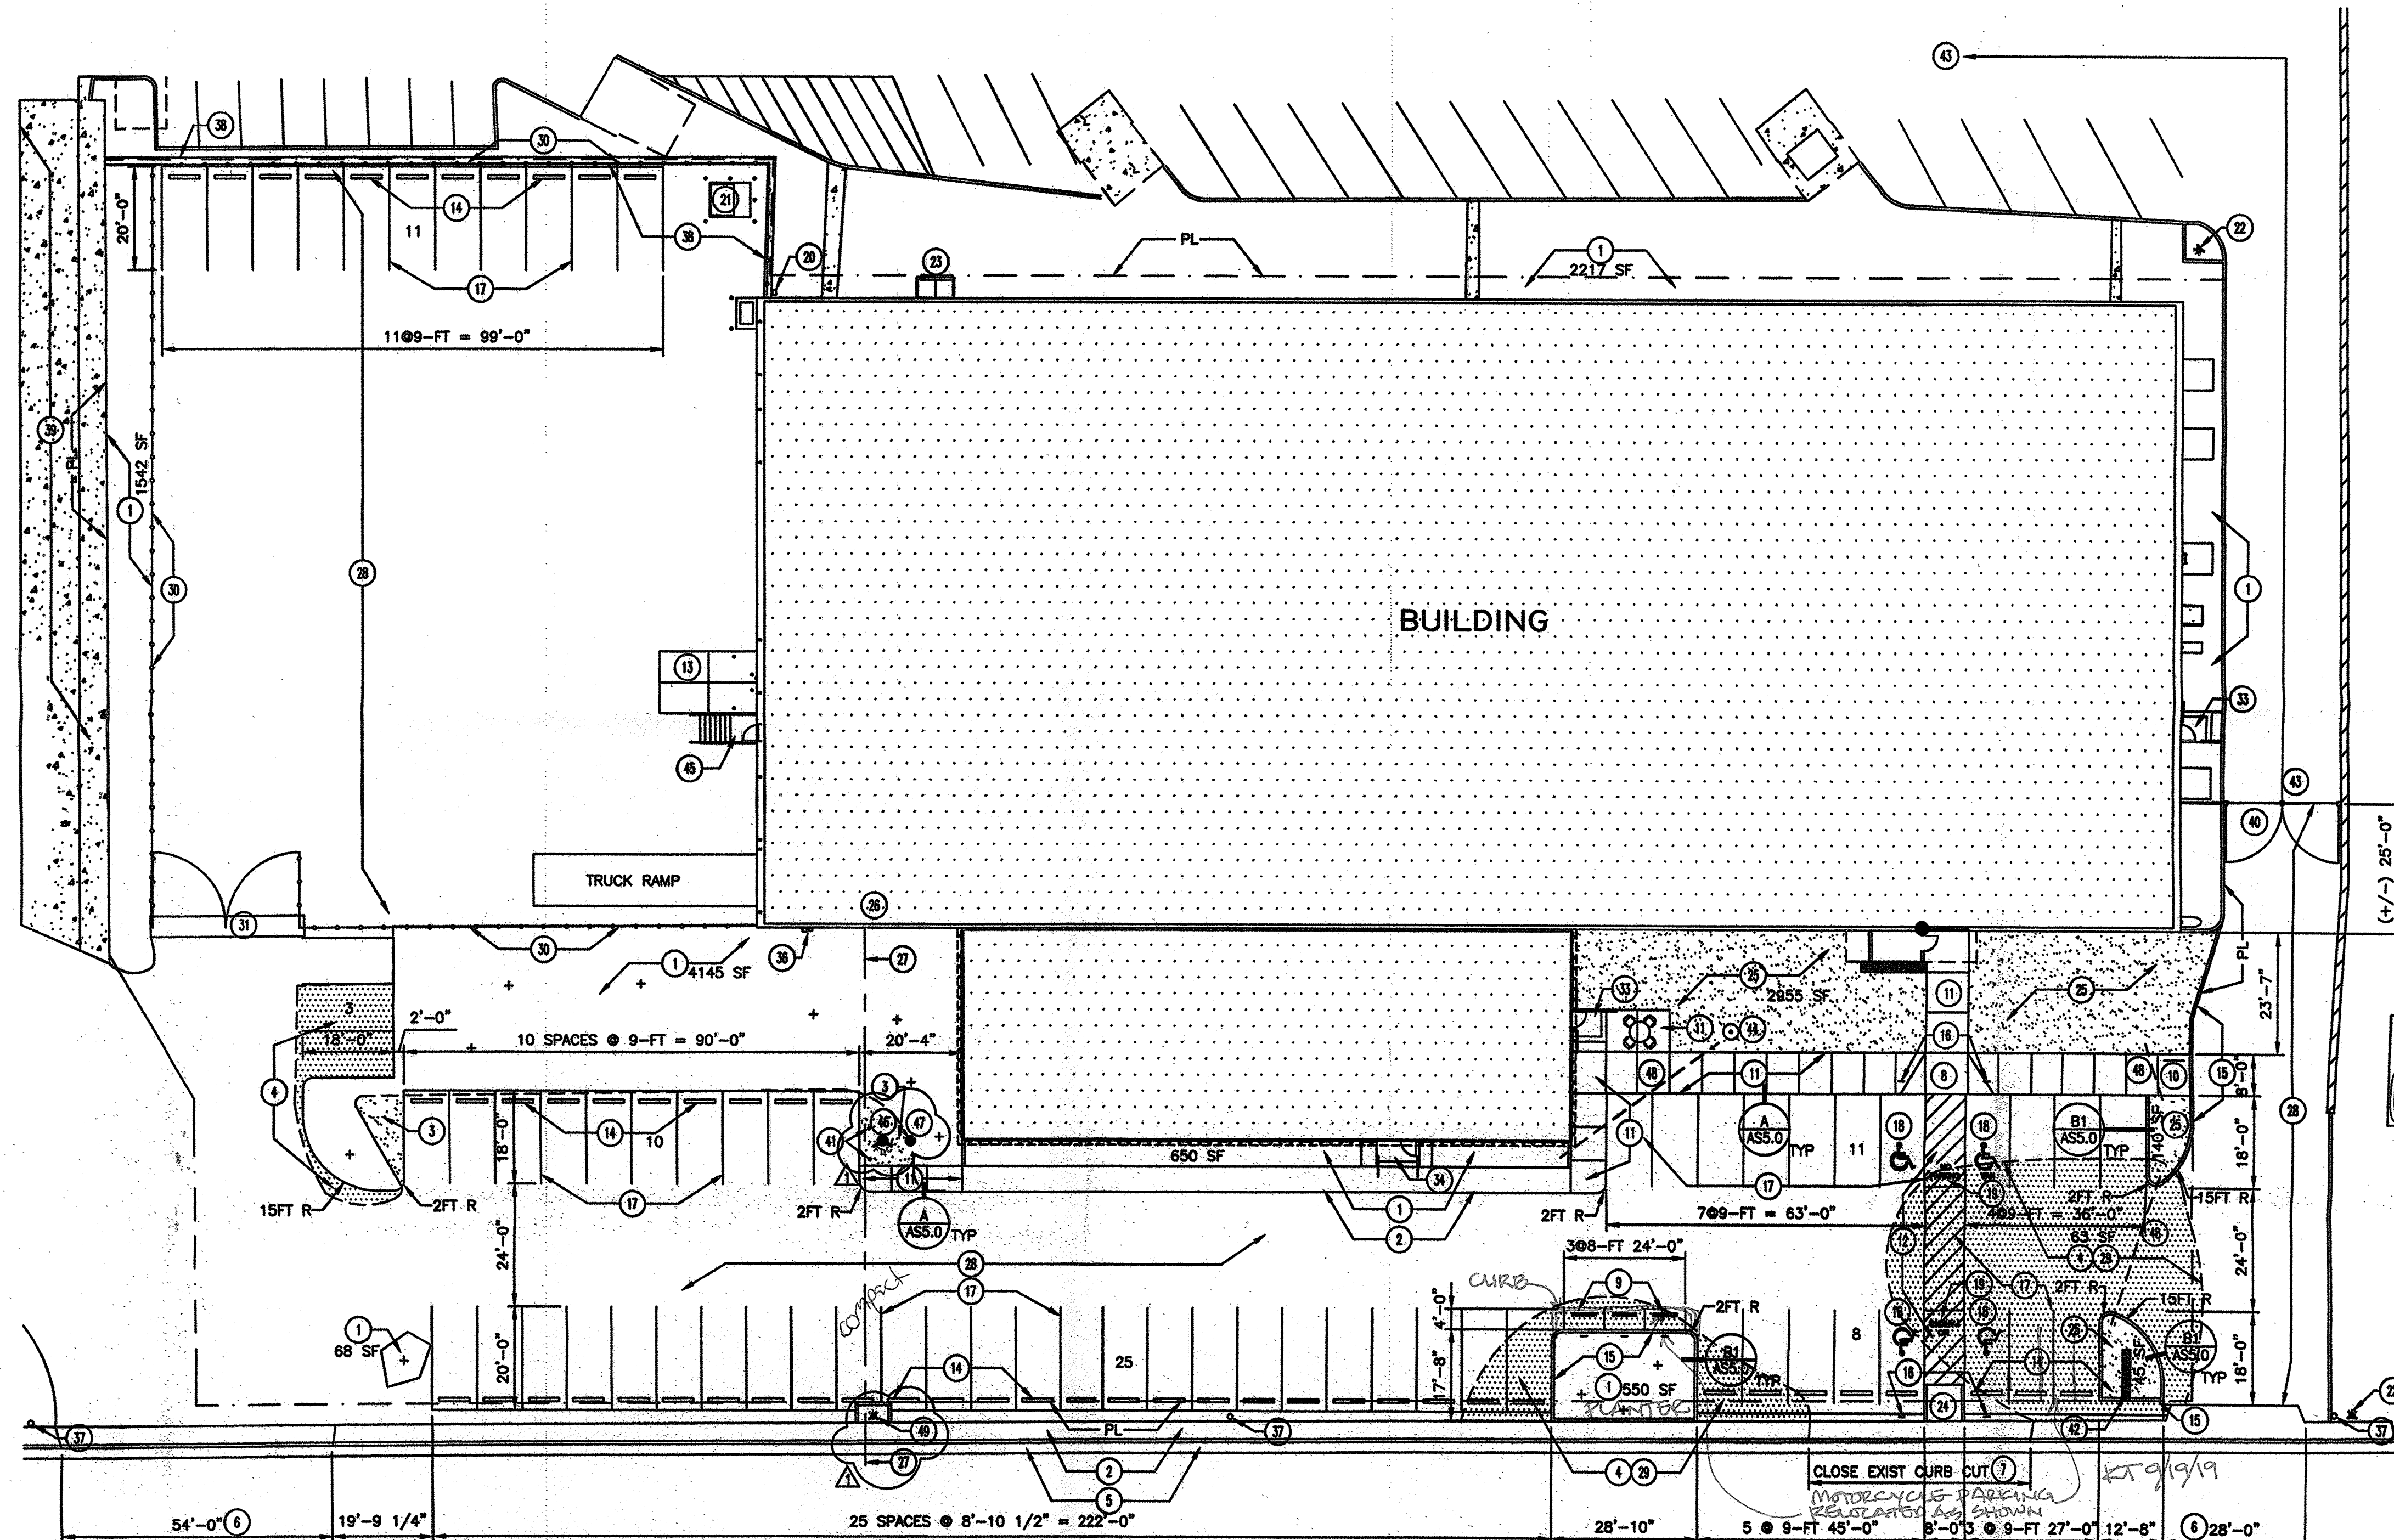

4801 Lincoln Road NE
(64' R/W)

REMODEL SITE PLAN
1" = 20'-0"

SITE LEGEND

- EXISTING BUILDING
- REMOVE EXISTING LANDSCAPE AREA AND INSTALL ASPHALT
- NEW LANDSCAPE AREAS
- EXISTING CONCRETE WALKS OR ASPHALT PAVED AREAS AS INDICATED
- NEW CONCRETE WALKS AS INDICATED, SHOWN WITH CONTROL JOINTS
- EDGE OF EXIST ASPHALT
- EXISTING TREE TO REMAIN. PROTECT ROOTS AND TRUNK TO ASSURE SURVIVAL.

TRAFFIC CIRCULATION LAYOUT
APPROVED
03/21/19

ALL WHEELCHAIR RAMPS LOCATED WITHIN THE PUBLIC RIGHT OF WAY MUST HAVE TRUNCATED DOMES.

GENERAL NOTES:

- THE GRADE AT ALL LANDSCAPE OR PLANTED AREAS THAT ADJUT CONCRETE WALKS OR CURBS SHALL BE DECREASED SO THAT THE LANDSCAPING SOIL AND/OR ROCK MATERIAL WILL BE FLUSH WITH THE TOP OF ADJOINING CONCRETE.
- PROVIDE CURB CUTS FOR DRAINAGE AS REQUIRED BY THE GRADING AND DRAINAGE PLAN.
- PROJECT IDENTIFICATION SIGNAGE IS NOT IN CONTRACT AND SHALL BE BY SEPARATE PERMIT.
- THE CONTRACTOR SHALL REMOVE ALL EXISTING SITE IMPROVEMENTS, UTILITIES, AND PLANT MATERIALS AND SHALL DISPOSE OF THEM AS REQUIRED.
- PROVIDE LEVEL CONCRETE HOUSE KEEPING SLAB AT ALL OUTDOOR EQUIPMENT LOCATIONS. RAISE A MINIMUM OF 1-1/2" ABOVE THE SURROUNDING CONCRETE WALKS WHERE EQUIPMENT IS LOCATED. COORDINATE SIZE OF PAD WITH EQUIPMENT SUPPLIERS.
- ALL SITE LIGHTING SHALL BE BUILDING MOUNTED, SEE ELEVATIONS AND ELECTRICAL. EXTERIOR FIXTURES ARE EXISTING AND SHALL REMAIN. FIXTURES SHALL BE SHIELDED WITH CUT OFFS PER CABQ NIGHT SKY ORDINANCE.


NOTE: REMODEL LANDSCAPE OR PAVING AREAS SHALL CONFORM TO EXISTING SITE DRAINAGE FLOW. NO SITE RUN-OFF SHALL FLOW TOWARD THE BUILDING. INSTALL OR CUT OPENINGS IN CURBS AS REQUIRED TO ALLOW THROUGH-DRAINAGE.

SITE DATA

PROPERTY: LOT A-1, FRIEDMAN SUBDIVISION
ZONING: M-1
LOT SIZE: 92,581 SF (2.1254 ACRES)
LAND USE: LIGHT MANUFACTURING
BUILDING AREA: 39,400 SF
TOTAL PARKING PROVIDED: 68 SPACES
TOTAL REQUIRED PARKING: 56 SPACES
OFFICE PARKING: 6,520/1000 x 3.5 = 23
MANUFACTURING PARKING: 32,880/1000 = 33
ACCESSIBLE PARKING REQUIRED: 4 SPACES (1 VAN)
ACCESSIBLE SPACES PROVIDED: 4
3 MOTORCYCLE PARKING SPACES REQUIRED AND PROVIDED
BICYCLE RACK SPACES REQUIRED AND PROVIDED: 77/20 = 4
LANDSCAPE AREA: 12,312 SF (526 SF LESS LANDSCAPE AREA THAN EXISTING)

PARKING: SITE AND BUILDING WERE CONSTRUCTED IN 1963 PRIOR TO PARKING AND LANDSCAPE ORDINANCES. ADDITIONAL PARKING PROVIDED AS SITE ALLOWS.

GRADING/DRAINAGE: BUILDING ADDITION IS LESS THAN 100SF. GRADING AND DRAINAGE SHALL RESPECT FOLLOW EXISTING CONDITIONS IN NEW PAVED AND LANDSCAPE AREAS.

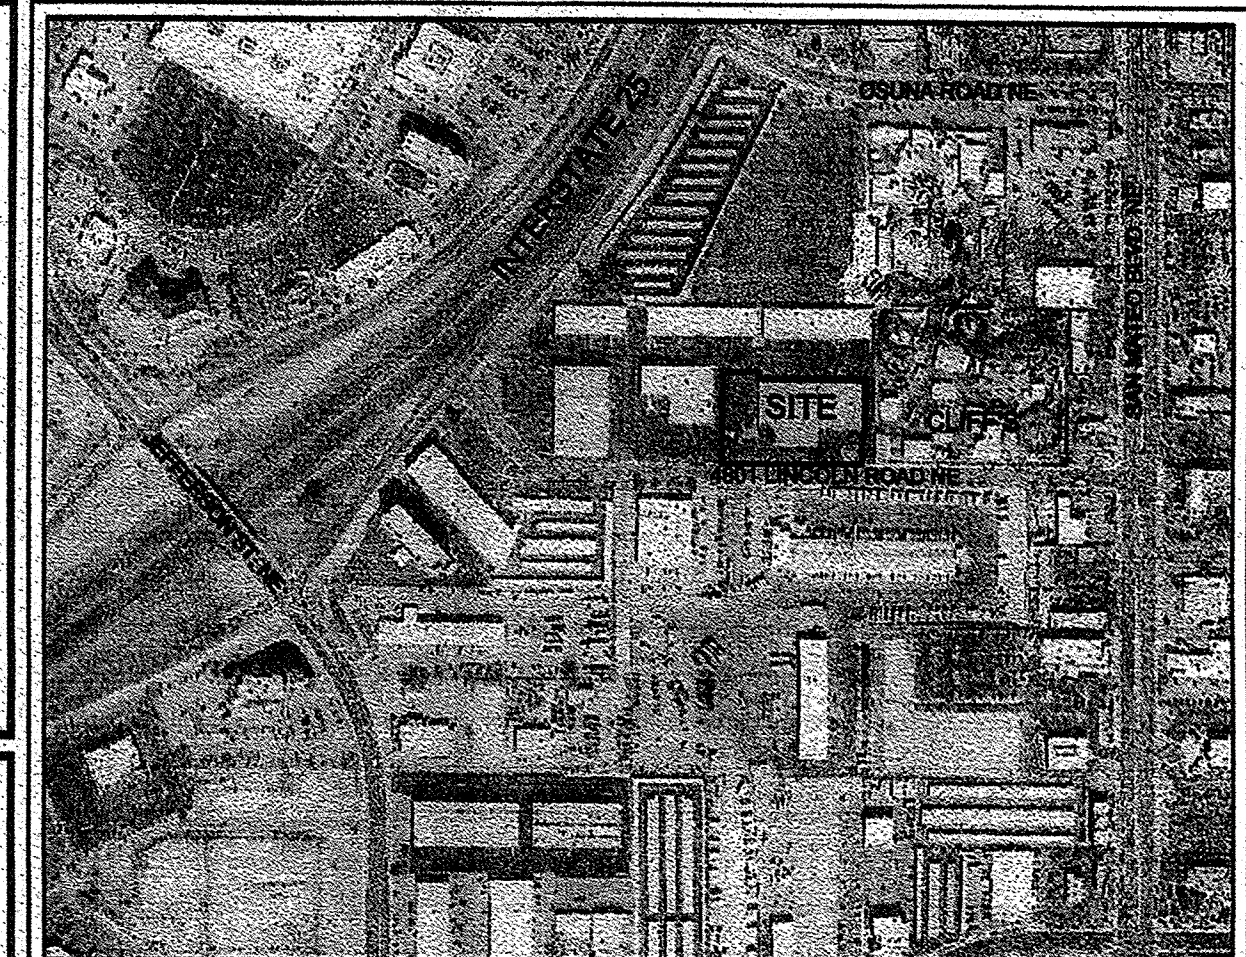

LOCATOR / ZONE ATLAS PAGE: F-17-Z

akt architects
P.O. BOX 3388
ALBUQUERQUE, NM 87100
T: (505) 281-9560
F: (505) 286-1055
C: (505) 259-7919
aktarch@earthlink.net

CONSULTANT



PROJECT


TENANT
IMPROVEMENT

PROJECT ADDRESS
4801 LINCOLN RD. NE
ALBUQUERQUE, NM
87109

MARK	DATE	DESCRIPTION
1/29/19	ADD FH, RELOCATE FDC AND PI VALVE	

PROJECT NO:
COPYRIGHT AKT ARCHITECTS, LLC
SHEET TITLE

SITE REMODEL
PLAN



AS-1.1





MOTORCYCLE
PARKING
ONLY
↔

RESERVED
PARKING
VAN
ACCESSIBLE

MOTORCYCLE



P. O. B O X 3 3 6 6
ALBUQUERQUE, NM 87190
T: (505) 281 - 9560
F: (505) 286 - 1055
C: (505) 259 - 7919
aktarch@earthlink.net

September 19, 2019

City of Albuquerque
Public Works Department
Transportation Development Services
600 2nd Street NW
Albuquerque, NM 87102

RE: Traffic Circulation Layout – Certification
BP-2019-06391
Office/Manufacturing Facility
4801 Lincoln Rd NE
Albuquerque, NM 87109



I, Kent Trauernicht, AKT Architects LLC, certify that this project is in substantial compliance and accordance with the design intent of the attached Traffic Circulation Layout/site plan, approved 3/21/19. I visited the site and determined by visual inspection that the Traffic Circulation Layout site plan is representative of actual site conditions and is true and correct to the best of my knowledge and belief. This certification is for the "Traffic Circulation Layout" substantial construction completion and Certificate of Occupancy.

The record information presented is not necessarily complete and is intended only to verify substantial compliance of the traffic aspects of this project. Those relying on the record document are advised to obtain independent verification of its accuracy before using it for any other purpose. This document neither expresses nor implies a warranty.



Sept 19, 2019



City of Albuquerque

Planning Department

Development & Building Services Division

DRAINAGE AND TRANSPORTATION INFORMATION SHEET (REV 11/2018)

Project Title: 4801 LINCOLN RD NE Building Permit #: 2019-0639 Hydrology File #: F170024A

DRB#: _____ EPC#: _____ Work Order#: _____

Legal Description: LOT A-1 FRIEDMAN SUBDIVISION

City Address: 4801 LINCOLN RD NE

Applicant: KENT TRAUERNICHT Contact: _____

Address: PO BOX 3366

Phone#: 281-9560 Fax#: _____ E-mail: AKTARCH@EARTHLINK.NET

Owner: _____ Contact: _____

Address: _____

Phone#: _____ Fax#: _____ E-mail: _____

TYPE OF SUBMITTAL: _____ PLAT (____ # OF LOTS) _____ RESIDENCE _____ DRB SITE ☒ ADMIN SITE


IS THIS A RESUBMITTAL?: _____ Yes ☒ No

DEPARTMENT: ☒ TRAFFIC/ TRANSPORTATION _____ HYDROLOGY/ DRAINAGE

Check all that Apply:

TYPE OF SUBMITTAL:

- ☒ ENGINEER/ARCHITECT CERTIFICATION
- _____ PAD CERTIFICATION
- _____ CONCEPTUAL G & D PLAN
- _____ GRADING PLAN
- _____ DRAINAGE MASTER PLAN
- _____ DRAINAGE REPORT
- _____ FLOODPLAIN DEVELOPMENT PERMIT APPLIC
- _____ ELEVATION CERTIFICATE
- _____ CLOMR/LOMR
- _____ TRAFFIC CIRCULATION LAYOUT (TCL)
- _____ TRAFFIC IMPACT STUDY (TIS)
- _____ OTHER (SPECIFY) _____
- _____ PRE-DESIGN MEETING?



TYPE OF APPROVAL/ACCEPTANCE SOUGHT:

- _____ BUILDING PERMIT APPROVAL
- ☒ CERTIFICATE OF OCCUPANCY
- _____ PRELIMINARY PLAT APPROVAL
- _____ SITE PLAN FOR SUB'D APPROVAL
- _____ SITE PLAN FOR BLDG. PERMIT APPROVAL
- _____ FINAL PLAT APPROVAL
- _____ SIA/ RELEASE OF FINANCIAL GUARANTEE
- _____ FOUNDATION PERMIT APPROVAL
- _____ GRADING PERMIT APPROVAL
- _____ SO-19 APPROVAL
- _____ PAVING PERMIT APPROVAL
- _____ GRADING/ PAD CERTIFICATION
- _____ WORK ORDER APPROVAL
- _____ CLOMR/LOMR
- _____ FLOODPLAIN DEVELOPMENT PERMIT
- _____ OTHER (SPECIFY) _____

DATE SUBMITTED: 9/20/19 By: KENT TRAUERNICHT

COA STAFF:

ELECTRONIC SUBMITTAL RECEIVED: _____

FEE PAID: _____
