

Address 600 Gons N.W. Engr/Arch. Phyllis Weiss
Plans Approved 4-1-82 Cond. _____

Comments:

J-11-D:4

Inspection Requested 4/1/83 Contractor General Contractor Inc.
Appr. 4/3/83 Disappr. 4/4/83 30 Day Temp. _____
Comments: 3-4" diameter pipes not installed, regrading to
from downspouts needed to divert water towards ponds.



City of Albuquerque
P.O. BOX 1293 ALBUQUERQUE, NEW MEXICO 87103

March 29, 1982

Mr. Chris Weiss
Consultants Terra-Sol, Inc.
1100 Alvarado NE, Suite B
Albuquerque, N.M. 87110

RE: RIO GRANDE UNITED PRESBYTERIAN CHURCH ADDITION DRAINAGE REPORT

Dear Chris:

The referenced report is approved. Please see that the revised plan is placed in the construction sets.

Very truly yours,

Brian G. Burnett
Civil Engineer/Hydrology

BGB/tsl

cc: Mike Coppedge

MUNICIPAL DEVELOPMENT DEPARTMENT

ENGINEERING DIVISION

Richard S. Heller, P.E., City Engineer

Telephone (505) 766-7467



City of Albuquerque

P.O. BOX 1293 ALBUQUERQUE, NEW MEXICO 87103

DRAINAGE REPORT INFORMATION SHEET

PROJECT TITLE An Addition to the Rio Grande United Presbyterian Church
ZONE ATLAS PAGE NO. J-11 CITY ADDRESS 600 Coors Road NW
LEGAL ADDRESS Lots C & D together w/ the adjacent portion of vacated alley, Block J
(Replat 1965) Northern Heights, a subdivision, Albuquerque, New Mexico.
ENGINEERING FIRM Consultants Terra-Sol Inc. CONTACT Chris Weiss
ADDRESS 1100 Alvarado NE Suite B Albuquerque PHONE 266-3444
OWNER Rio Grande United Presbyterian Church CONTACT Rev. Edwin Steinmetz Jr.
ADDRESS 600 Coors Road NW PHONE 831-1143 or 892-9324
ARCHITECT/SURVEYOR Weller & Coppedge, Architects CONTACT Mike Coppedge
ADDRESS 416 Washington SE Suite 1-A, Albuq. PHONE 255-8270
DATE SUBMITTED _____
BY _____

MUNICIPAL DEVELOPMENT DEPARTMENT
ENGINEERING DIVISION

Richard S. Heller, P.E., City Engineer


Telephone (505) 766-7467

CITY OF ALBUQUERQUE

DRAINAGE FACILITIES WITHIN CITY RIGHT-OF-WAY

J11-D14

B.M. S.S.E. Ret.
Brass Cap 3 J10
Elev. 5049.77

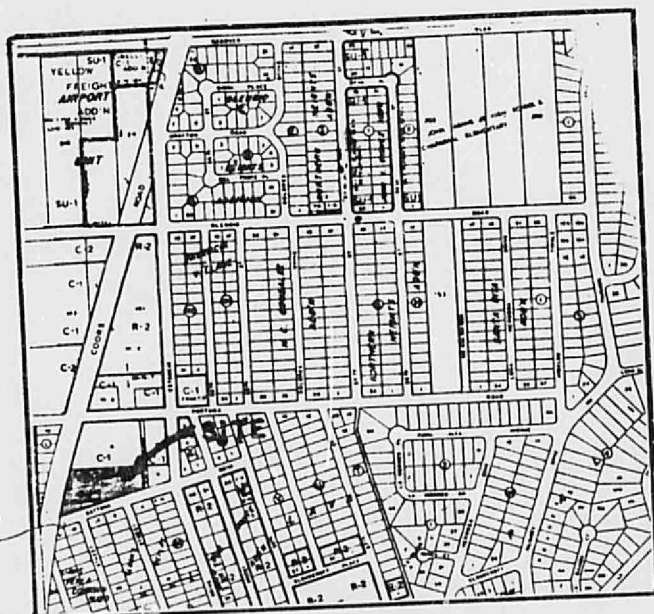

VICINITY MAP - J-II

NOTICE TO CONTRACTOR

1. An excavation/construction permit will be required before beginning any work within City right-of-way. An approved copy of these plans must be submitted at the time of application for this permit.
2. All work detailed on these plans to be performed, except as otherwise stated or provided hereon, shall be constructed in accordance with "Contract Documents for City-Wide Utilities and Cash Paving No. 30"
3. Two working days prior to any excavation, contractor must contact Line Locating Service, 765-1234, for location of existing utilities.
4. Prior to construction, the contractor shall excavate and verify the horizontal and vertical locations of all obstructions. Should a conflict exist, the contractor shall notify the engineer so that the conflict can be resolved with a minimum amount of delay.
5. Backfill compaction shall be according to Arterial B-12 street use.


CHURCH SITE ADDITION/N.E. CORNER OF COORS & DAYTONA N.W., ALBUQUERQUE, N.MEX.

APPROVALS	NAME	DATE	TITLE: REPEAT OF BK. J & THE EASTERLY PORTION OF BK. K & L OF THE NORTHERN HEIGHTS SUBDIVISION, ALBUQUERQUE, NEW MEXICO
A.C.E./DESIGN	<i>[Signature]</i>	23 Feb 82	
INSPECTOR	<i>[Signature]</i>	4-22-83	PERMIT NO.
A.C.E./FIELD	<i>[Signature]</i>	4-22-83	SHEET 1 OF 2
			MAP NO. J-II


[Signature]

CITY OF ALBUQUERQUE


DRAINAGE FACILITIES WITHIN CITY RIGHT-OF-WAY

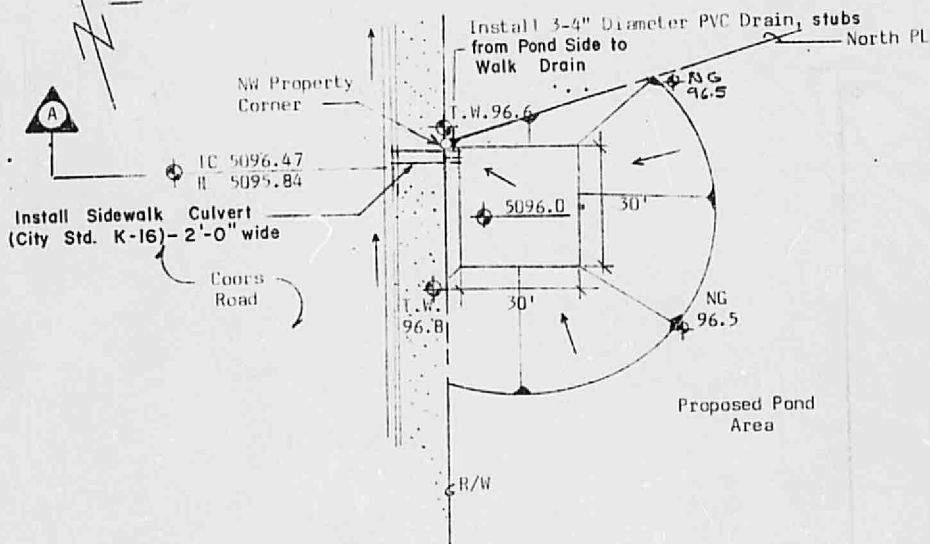

PLAN

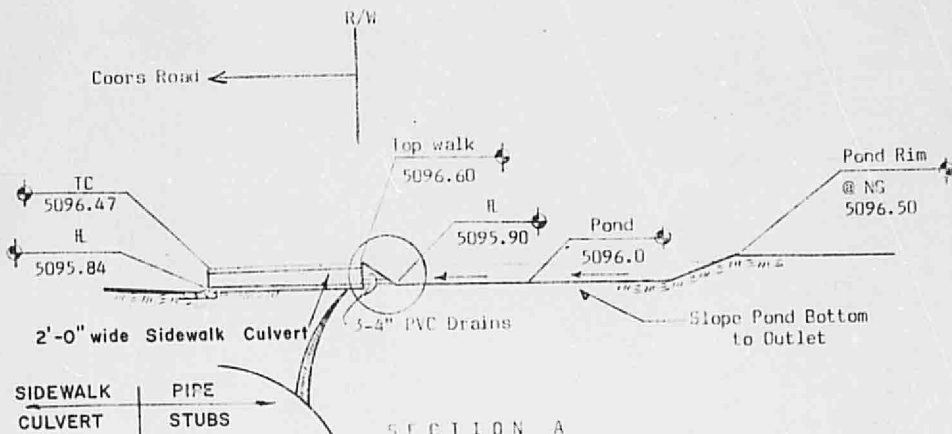

SECTION A



ENLARGED SECTION

Church Site Addition/NE Corner of Coors and Datona NW - Albuquerque, New Mexico

APPROVALS	NAME	DATE	TITLE:
A.C.E./DESIGN	<i>J. Kitch</i>	23 Feb 82	Replat of Bk. J and the Easterly Portion of Bk. K and L of the Northern Heights Subdivision, Albuquerque, New Mexico
INSPECTOR	<i>Quincy</i>	4-22-83	
A.C.E./FIELD			
PERMIT NO. SHEET 2 OF 2			MAP NO. J-11
